

I-80/Yerba Buena Island East Side Ramps & Vista Point: Project Status

Citizens Advisory Committee
Agenda Item 5



SAN FRANCISCO COUNTY TRANSPORTATION AUTHORITY
September 28, 2016

YBI Ramps Project Current Status



YBI Ramps Construction Contract Update

- **Awarded construction contract to Golden State Bridge, Inc.– Dec. 2013**
- **92% Complete**
- **\$63.89M CONSTRUCTION CAPITAL PHASE**
 - **12.5% DBE Goal**
- **New Ramps Opening: Last Week - October 2016**




YBI Ramps Upcoming Milestones

- **Northgate/Macalla Reconstruction – October 2016**
- **Traffic Electrical, Signing, Striping – October 2016**
- **Ribbon Cutting – October 21, 2016**
- **Final Improvements Complete – December 2016**



YBI Bike/Ped Vista Point

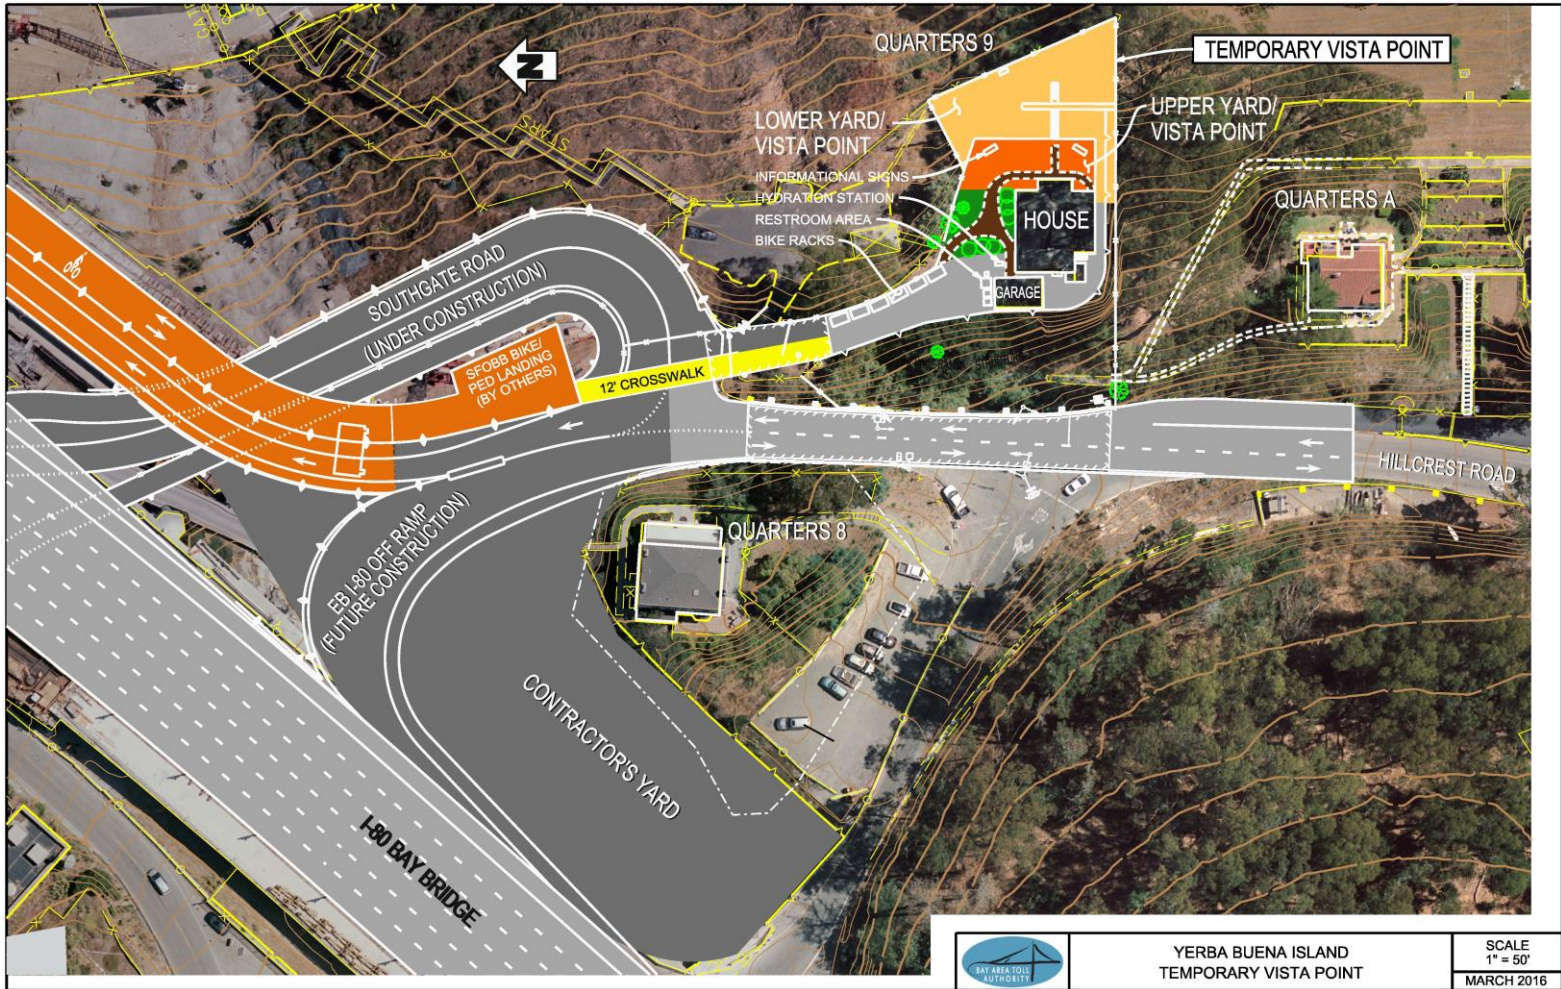

YBI Bike/Ped Vista Point

- **Vista Point Amenities:**
 - Hydration, restrooms, bike racks, benches
- **TA to construct on USCG Qtrs. 9**
- **Working with CT/TIDA/BATA to establish shuttle service between Treasure Island and Bike Path**
- **Funding: \$2M (BATA –TA)**
- **Vista Point Opening: Fall 2016**



YBI Bike/Ped Vista Point



© 2016 California Department of Transportation ALL RIGHTS RESERVED



YBI Ramps – Recommendations

- **Adopt a Motion of Support:**
 - To execute a MOA with TIDA for Vista Point operation services in an amount not to exceed \$500,000 through December 31, 2018

