

QUICK-BUILD PROGRAM UPDATE

SFCTA Board

September 10, 2024

Jen Wong, SFMTA

Item 10

RECENTLY COMPLETED



Frída Kahlo Way

- New two-way protected bikeway providing access to City College in time for new school year
- Bikeway features concrete islands and transit boarding islands for 43 Masonic



Photo: Walk SF

Guerrero Street

- Substantially complete with new painted safety zones, advanced limit lines, and turn calming treatments
- Walk San Francisco celebrated Field Operations in field

CORRIDOR PROJECTS – WELL UNDERWAY

#	PROJECT	PLANNING/DESIGN PHASE	CONSTRUCTION PHASE	CURRENT STATUS
1	Valencia St.	Mar 2022 – Apr 2023	Apr 2023 – Aug 2023	PILOT INSTALLED
2	Bayshore Blvd.	Oct 2021 – Mar 2023	Aug 2023 – Sep 2023	INSTALLED
3	Hyde St.	Sep 2022 – Oct 2023	Nov – Dec 2023	INSTALLED
4	Lake Merced Blvd.	Jul 2021 – Jan 2023	Sep 2023 – Fall 2024	Under Construction
5	Lincoln Way	Sep 2022 – May 2023	Jan – May 2024	INSTALLED
6	Sloat Blvd.	Sep 2022 – Jul 2023	Fall 2024	Preparing for construction
7	Guerrero St.	Jul 2023 – Sep 2023	Aug 2024	INSTALLED
8	17th St.	May 2022 – Mar 2024	Apr – Jun 2024	INSTALLED
9	3rd St.	Aug 2023 – Mar 2024	Mar 2024	INSTALLED
10	Frida Kahlo Way	Jan 2023 – May 2024	May - Aug 2024	INSTALLED

CORRIDOR PROJECTS – DESIGN/OUTREACH IN THE WORKS

#	PROJECT	PLANNING/DESIGN PHASE	CONSTRUCTION PHASE	CURRENT STATUS
11	Oak St.	Aug 2023 – Fall 2024	Late 2024	Planning/design in progress
12	Sutter St.	Aug 2023 – Winter 2024	Early 2025	Planning/design in progress
13	Beach St.	Oct 2023 – Fall 2024	Early 2025	Planning/design in progress
14	Alemanly Blvd.	Jan 2024 – Fall 2024	Fall 2024	Planning/design in progress
15	Cesar Chavez St.	Jan 2024 – Fall 2024	Early 2025	Planning/design in progress
16	Larkin St.	April 2024 – Fall 2024	Following repaving	Planning/design in progress
17	Clarendon Ave.	Sep 2023 – Spring 2024	Following repaving	Planning/design in progress

PROJECTS TO DATE




39

Corridor projects completed



2

Construction phase projects


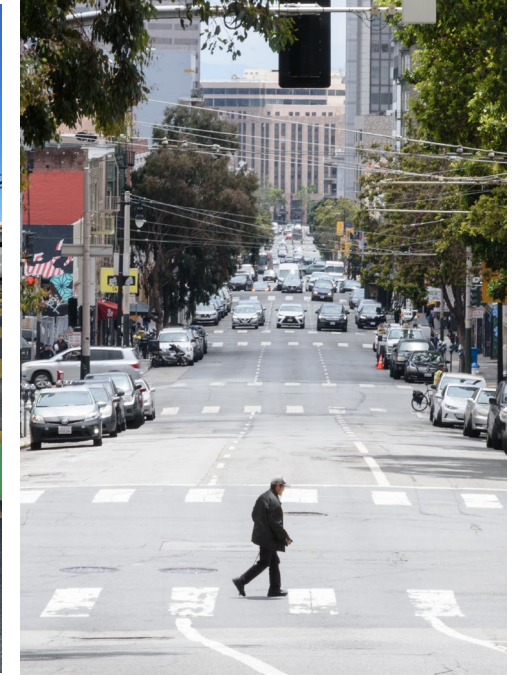


7

Design phase projects

QUICK-BUILD TOOLKIT PROJECT

Progress through 8/21/2024

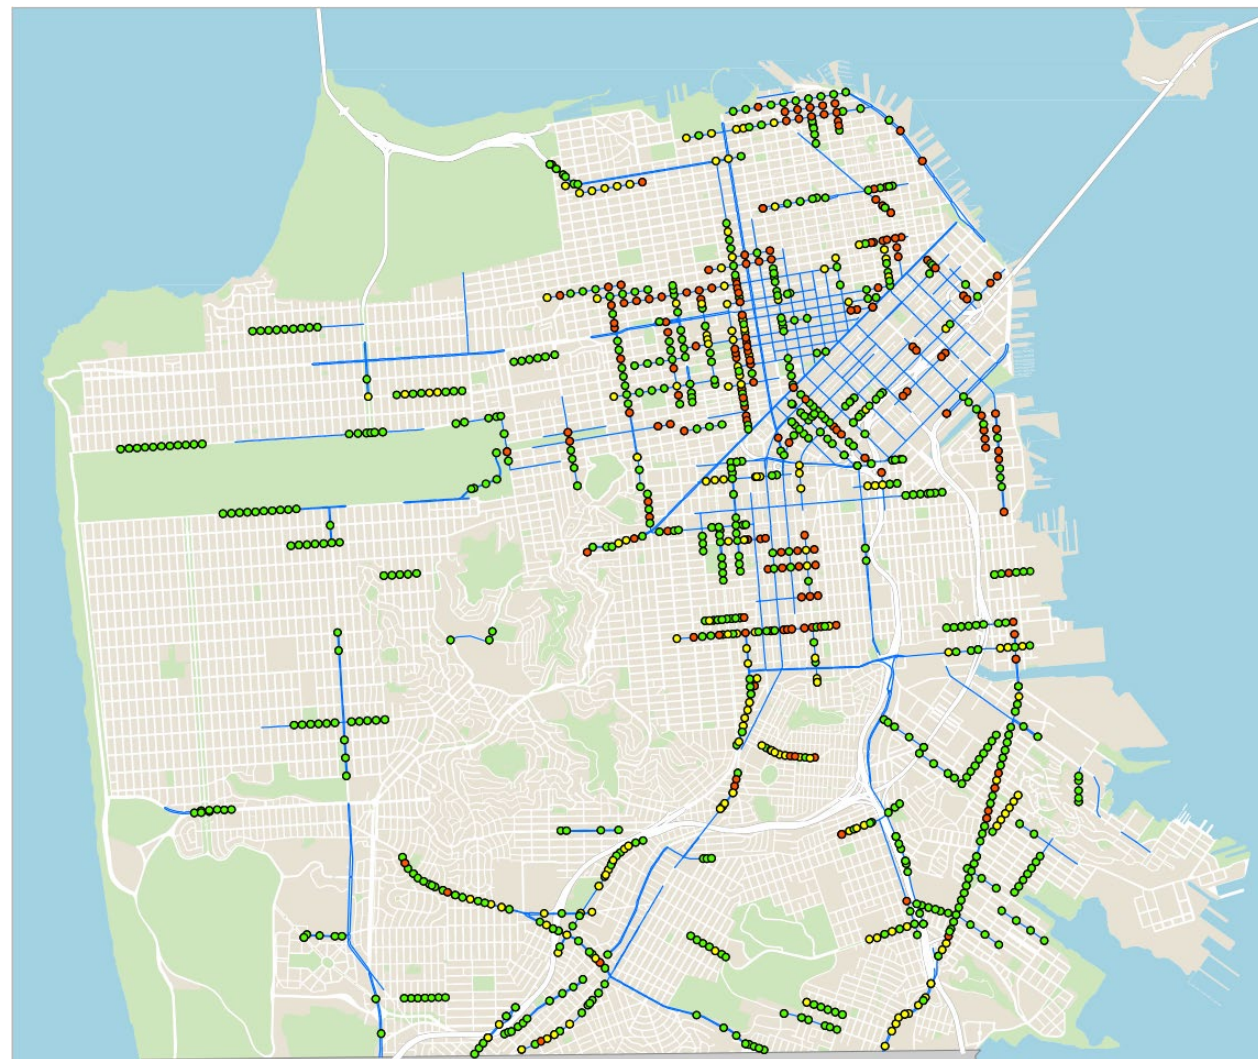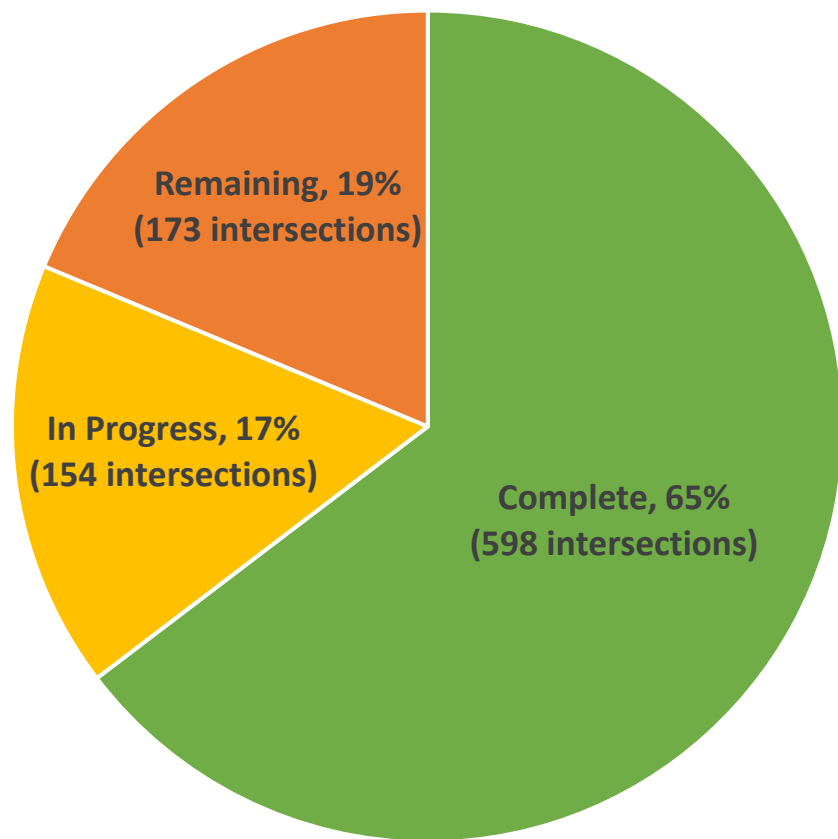

UPCOMING QUICK-BUILD EFFORTS




Daylighting



Lower Speed Limits



Bikeway Hardening

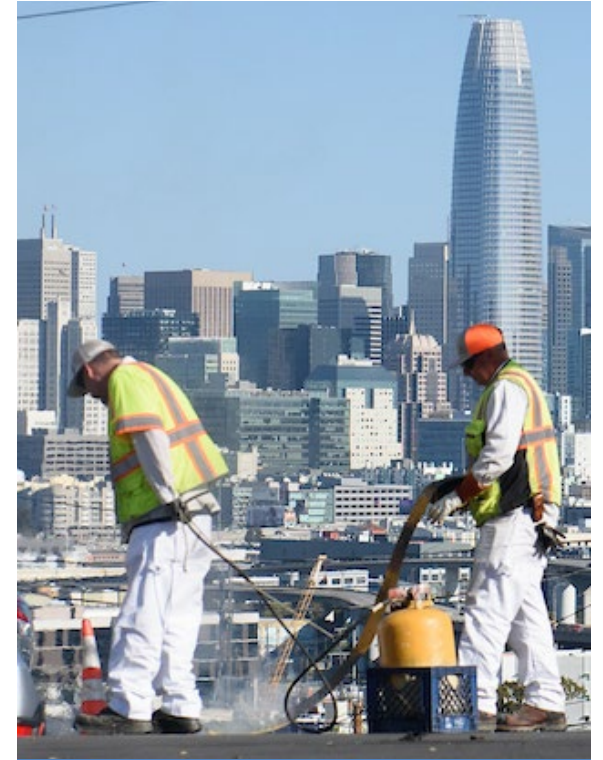

Corridor Projects

~\$3.5M

~\$5M
