



**VISION  
ZERO  
SF**

---

Through Vision Zero SF we commit to working together to prioritize street safety and eliminate traffic deaths in San Francisco by 2024

---

# **VISION ZERO SF: *ELIMINATING TRAFFIC DEATHS BY 2024***

---

**SEPTEMBER 15, 2016**

## OVERVIEW

- Update on 57 Priority Projects
  - Completed
  - Schedule Updates
  - Upcoming
- Two year Action Strategy
- Legislation Update

# VISION ZERO PRIORITY PROJECTS

Share Print Measure


Find address or place

Accountability and Transparency:  
50+ projects from all focus areas  
with key milestones in the next 2  
years to advance Vision Zero

**Columbus Avenue Safety Project**

Project Description	Safety measures include installation of a permanent pedestrian bulbout, a continental crosswalk, bicycle lanes, and bulbs at intersections of Stockton/Green, Vallejo, and Grant.
Key Milestone	Complete Construction
Expected Milestone Completion Date	Winter 2017
Status	On Schedule

Zoom to

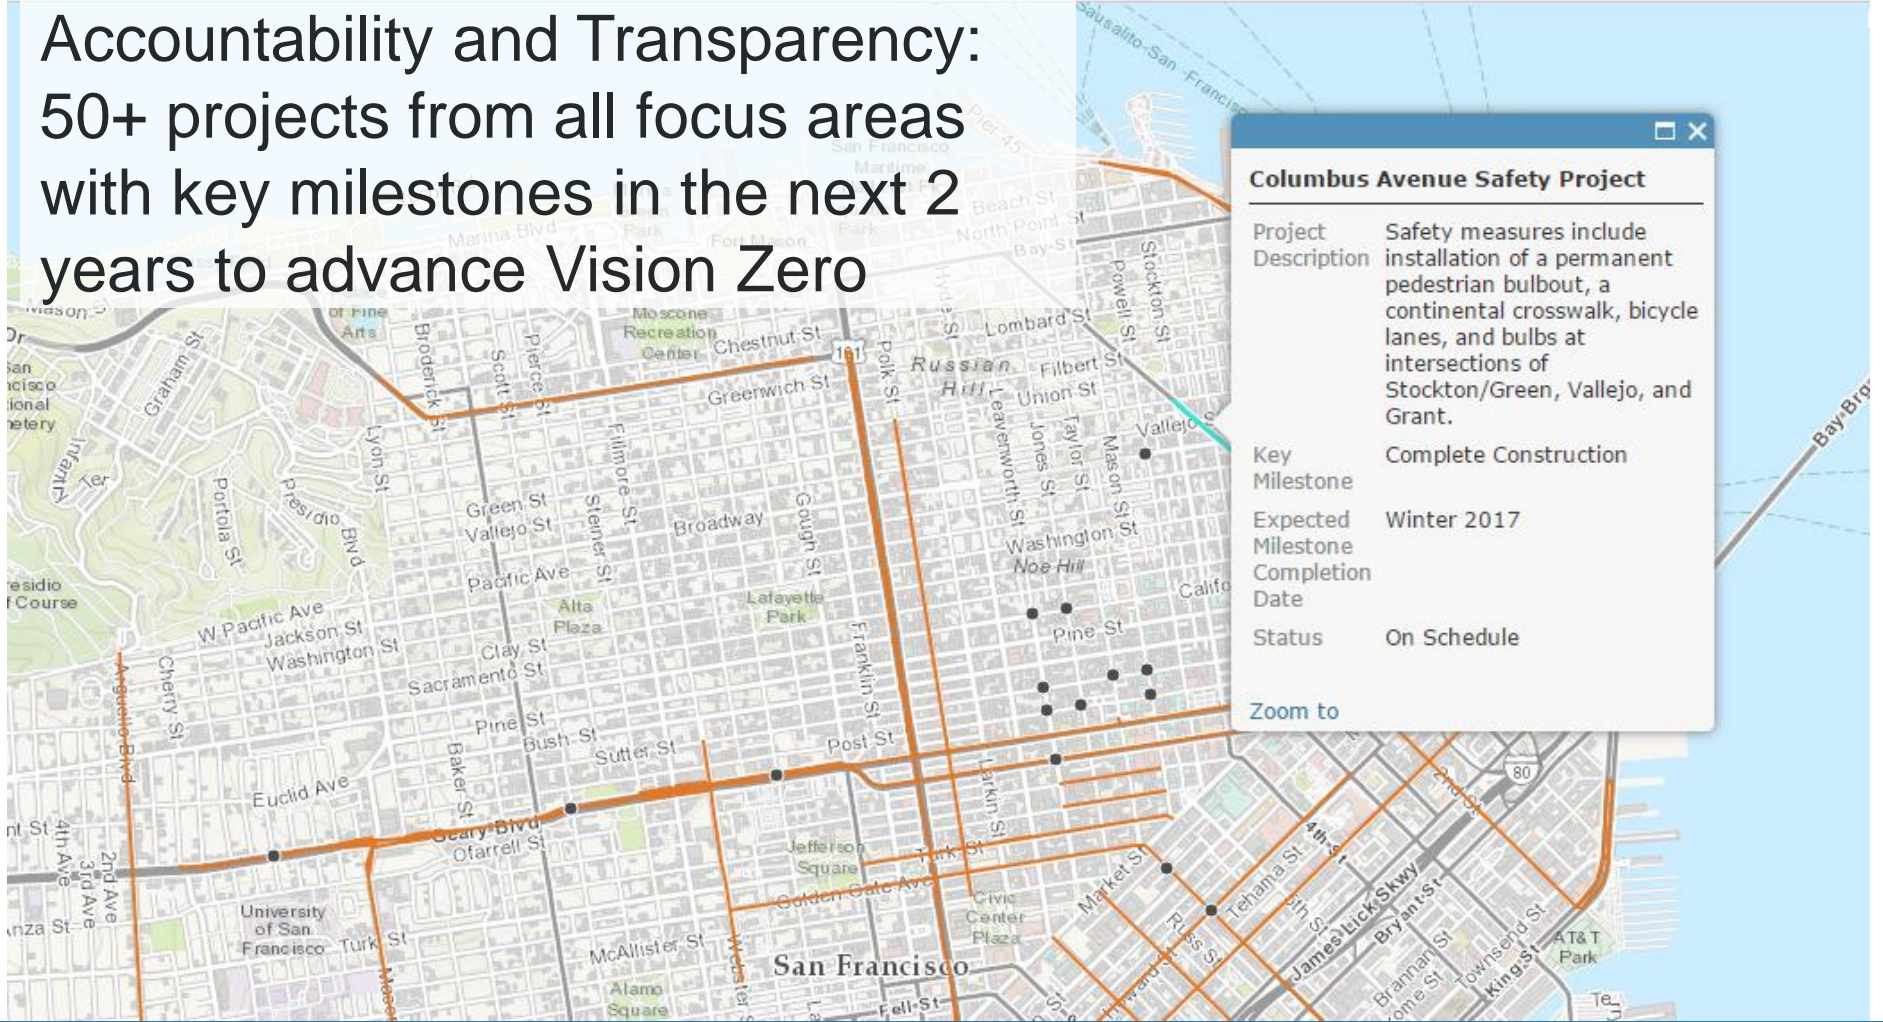

## INFRASTRUCTURE MILESTONES ACHIEVED

- 28 19<sup>th</sup> Ave Rapid Project, completed conceptual design
- Masonic Avenue, began construction



- Radar speed feedback signs, completed construction
- Golden Gate Ave (Polk to Market), completed construction

## INFRASTRUCTURE SCHEDULE UPDATES

- Broadway Streetscape, begin construction
  - Original schedule: Spring 2016 >> Current: Summer 2016
- WalkFirst New Signals, complete design
  - Original schedule: Summer 2016 >> Current: Fall 2016
- WalkFirst PCS, complete design
  - Original schedule: Summer 2016 >> Current: Fall 2016
- Van Ness, begin construction
  - Original schedule: Summer 2016 >> Current: Fall 2016
- Palou Streetscape, complete design
  - Original schedule: Summer 2016 >> Current: Fall 2016
- Sutter Street @ Mason, Taylor and Leavenworth, complete construction
  - Original schedule: Fall 2016 >> Current: Winter 2017
- Webster (Fulton to Sutter), complete construction
  - Original schedule: Fall 2016 >> Winter 2016

## UPCOMING INFRASTRUCTURE MILESTONES

- Arguello Blvd Bicycle and Pedestrian Improvements\*, complete construction
- Tenderloin Safe Routes to School, complete construction
- Arguello/Irving Intersection Safety Treatments\*,
- Polk Streetscape Project, begin construction

\*Ahead of schedule



## NON-INFRASTRUCTURE MILESTONES ACHIEVED

- Vision Zero Communications, began program
- Integrate SFPD collision data into TransBaseSF.org, completed program
- Safe Streets for Seniors, began program



## NON-INFRASTRUCTURE SCHEDULE UPDATES

- Develop Dashboard to Summarize Data by Corridor or Intersection, complete program
  - Original schedule: Summer 2016 >> Current: Fall 2016
- SF Street Smarts, begin program
  - Original schedule: Fall 2016 >> Current: Winter 2017
- SFPD e-citations, begin program
  - Original schedule: Fall 2016 >> Current : Winter 2017


## UPCOMING NON-INFRASTRUCTURE MILESTONES

- Severe Injury Tracking, complete program
- Motorcycle Education campaign, begin program
- Update High Injury Network, complete program
- Surveillance System Update, complete program




## POLICY

Secure sponsor for  
**Automated Speed  
Enforcement**  
legislation



Potential collisions  
reduced




Potential injury/fatality  
colisions reduced

## UPDATE ACTION STRATEGY

Keep what works and remove, revise, add elements so 2017-2018 Strategy is a more holistic and constructive tool

Public Meeting October 11<sup>th</sup>  
City Hall, Rm 201 @ 9:30am

Release in January 2017



## UPCOMING MEETINGS

- Vision Zero Task Force Meeting: Sept 20<sup>th</sup>
- Two-Year Action Strategy Public Meeting: October 11<sup>th</sup>
- Vision Zero Committee Meeting: Dec 8<sup>th</sup>
- Vision Zero Task Force Meeting: Dec 13<sup>th</sup>

---

**VISIONZEROSF.ORG**

**Tom Maguire**

Director of Sustainable Streets  
San Francisco Municipal Transportation Agency

*Tom.Maguire@sfmta.com*
