

# Transbay Program Phase 2 Downtown Rail Extension (DTX)

## Tunnel Options Study Briefing



May 23, 2018



# Study Purpose and Goals

---


- Initiated at the request of the SFCTA Board to address concerns about impacts resulting from cut-and-cover construction
- Goals:
  - Minimize surface disruption and socio-economic impacts
  - Reduce cut-and-cover tunnel extent
  - Identify feasible mined tunnel construction methods for further study
  - Identify major infrastructure constraints

# Work Since Last Update to SFCTA Board

---

- Further developed mined Howard Street crossing to balance the surface disruption and cost for the Throat structure
- Refined the constructability and schedule for the options
- Confirmed ventilation requirements
- Reviewed configuration of the TBM + SEM tunneling option

# Throat: North of Clementina St


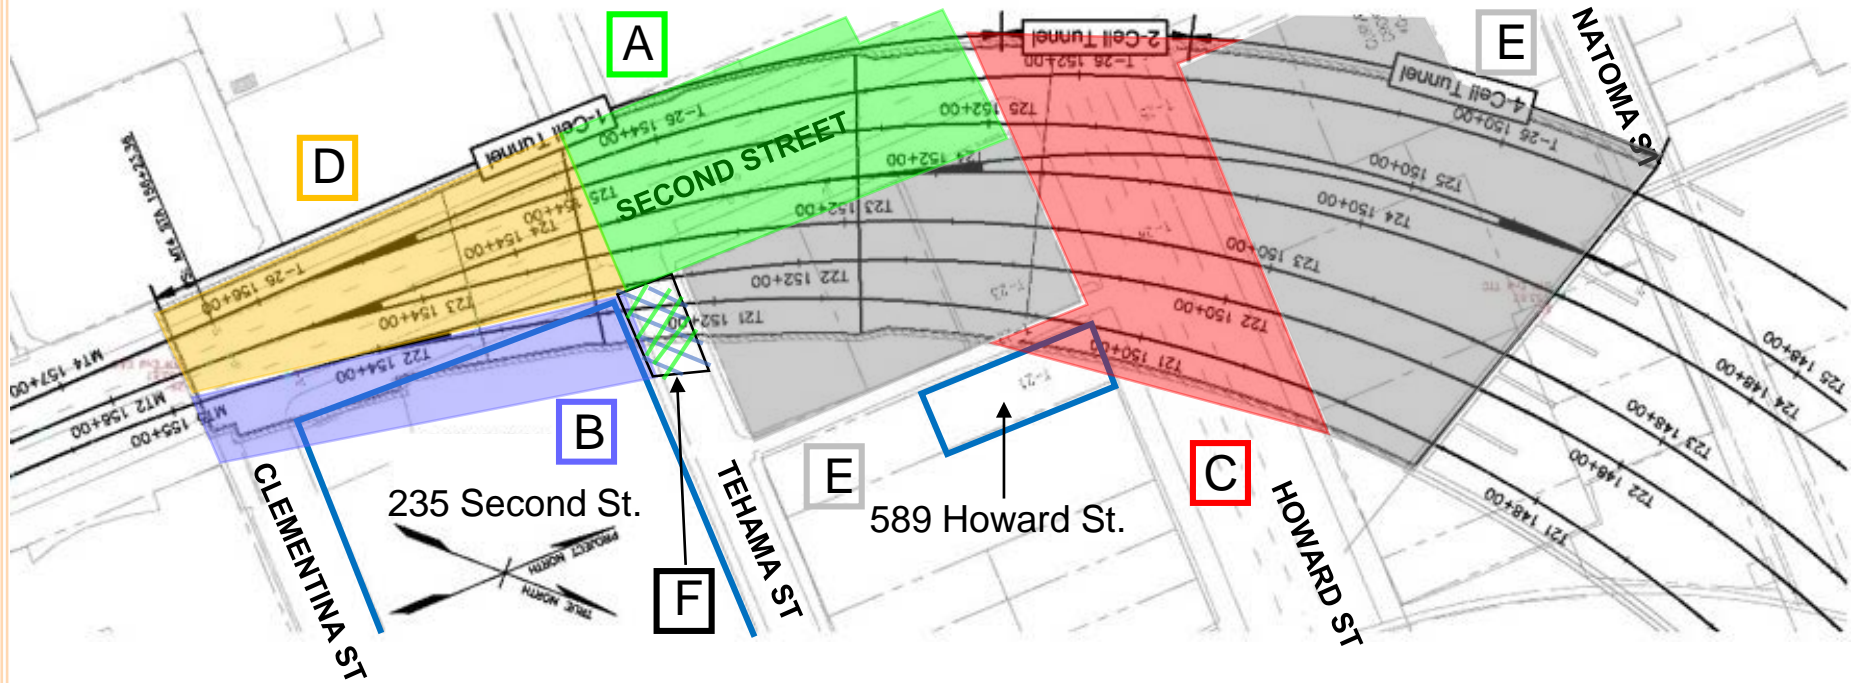


## Options for Partially Mining the Throat

- Add-on Options — [
  - A Pipe Roof Support for Mining under Second Street
  - B Extend TBM Mining Below 235 Second St. (Option 1) or Cut-and-Cover (Option 2)
- Alternate 1 — [
  - C Jacked Box Mining under the Howard Street Crossing
  - D Cut-and-Cover with Decking
  - E Cut-and-Cover outside the public right-of-way (Open Cut)
  - F Cut-and-Cover with Decking (for Add-on Option A) or Extend TBM Mining (for Add-on Option B)


# 2<sup>nd</sup> St. & Townsend St. between 3<sup>rd</sup> – 4<sup>th</sup> Sts.

- Baseline SEM Concept in Preliminary Engineering drawings
- Twin bore Tunnel Boring Machine (TBM) with SEM mining between bores

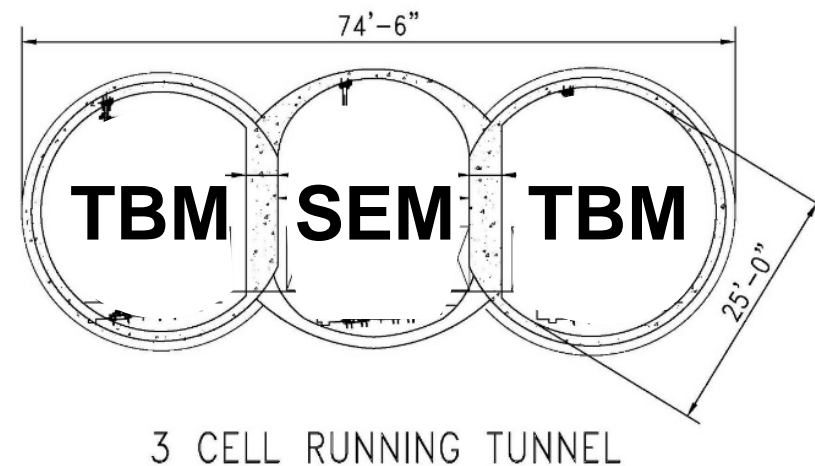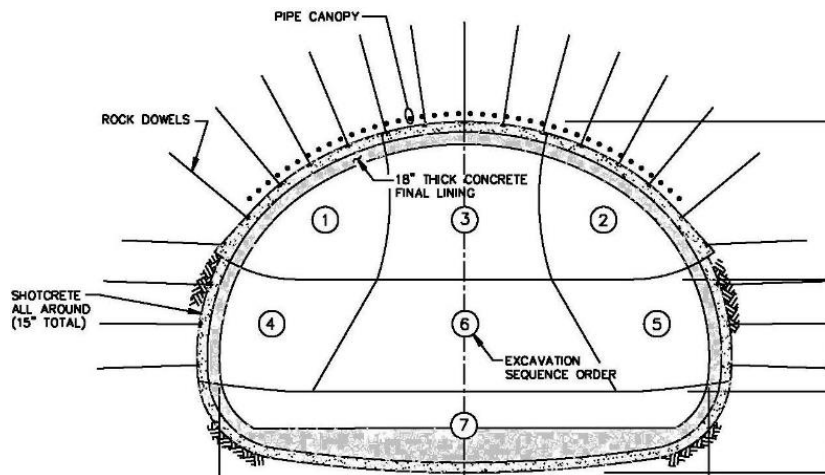

# 4<sup>th</sup> & Townsend Street Station

- Cut-and-cover construction (with decking) necessary due to low ground cover and soil conditions
- Aligned with Townsend St. with a center platform between northernmost tracks and mezzanine connection with surface

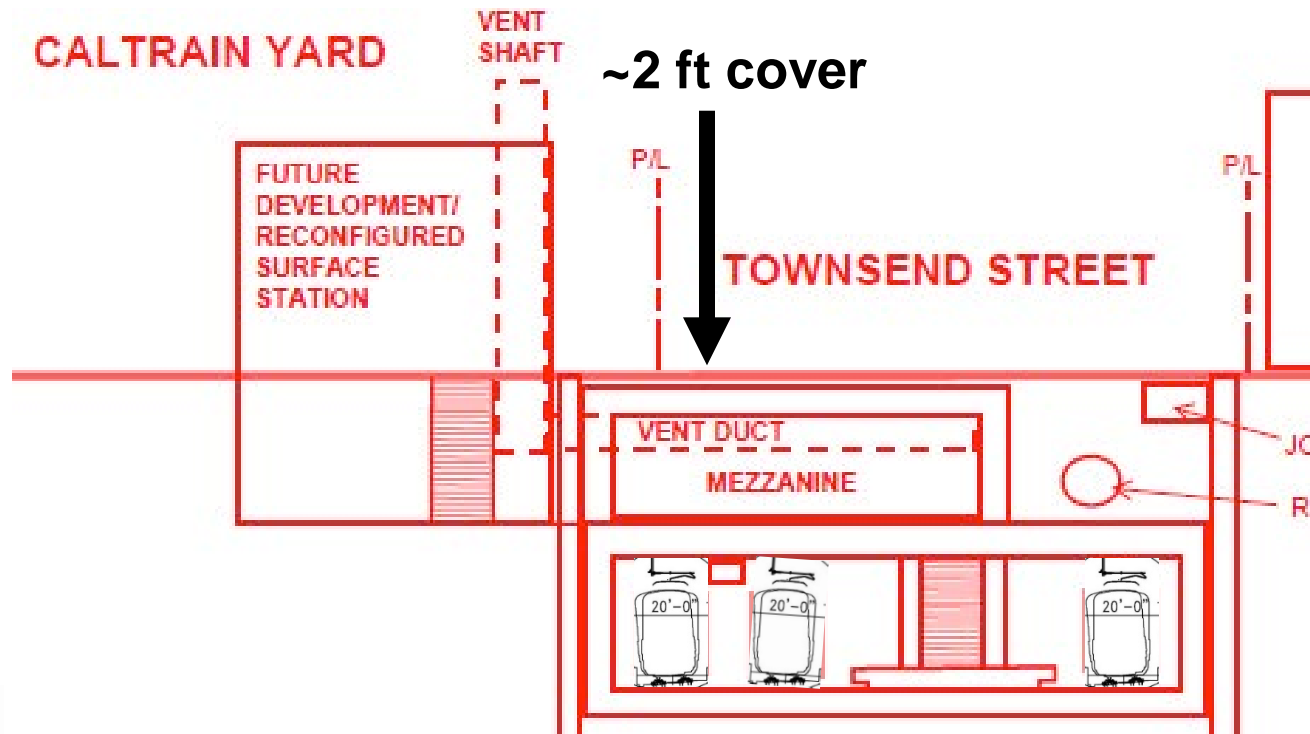

# 4<sup>th</sup> & Townsend Street Station Traffic Decking

- Minimizes traffic disruption during cut-and-cover construction
- Investigating use from 4<sup>th</sup> St. to just west of 5<sup>th</sup> St.
- Installation:
  - Weekends (Fri PM – Mon AM)
  - Nights at non-residential areas
  - Maintain normal traffic flow during week
  - Sequence to maintain local business access



*Hollywood Blvd/Highland, Los Angeles*

# Cost Premium Above Baseline for Maximum Reduction in Cut-and-Cover



Mining b/w 3<sup>rd</sup>-4<sup>th</sup> Sts.:  
 Fully-burdened Cost (YOE\$):  
 +\$71m (TBM+SEM)  
 +\$104m (SEM)

**DTX Elements Phase 1 & 2**

- Phase 1
- Phase 2
- Vent Structure

0 500 1000 2000  
 Scale in feet

Aug 2017




# Cost Premium of Eliminating or Reducing Cut-and-Cover in the Public ROW at the Throat

Location	Direct Construction Cost (2018\$)	Fully-burdened Cost (YOE\$)
Entire Throat (Howard St, 2nd to Clementina St.)	+\$217m	+\$461m
Howard Street Crossing	+\$108m	+\$208m
Howard & 2nd St to Tehama Streets	+\$178m	+\$343m



# Relative Tunneling Schedules (Months)

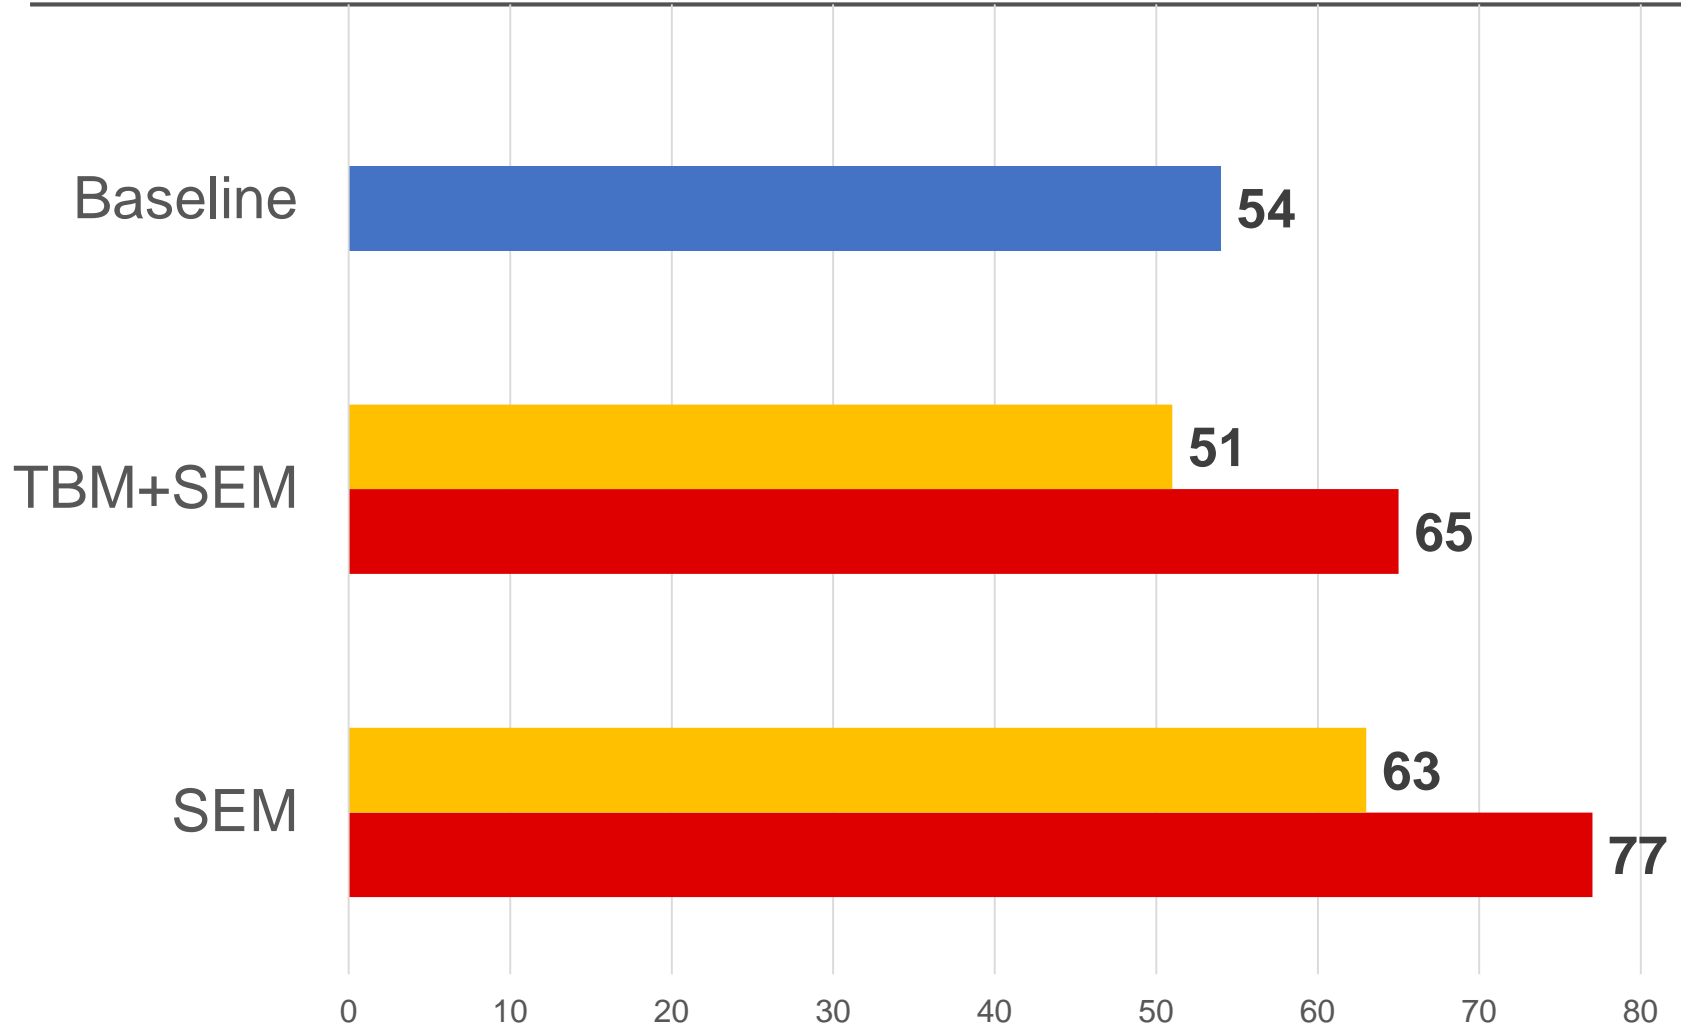

# Recommendations

---

Proceed with 30% Preliminary Engineering for:

- The TBM+SEM concept between Clementina Street and Fourth and Townsend Street Station. (+\$71m)
- Maintain cut-and-cover construction with decking for the Fourth and Townsend Street Station.
- Extending single-bore TBM tunneling beyond 235 Second St., maintaining undisturbed sidewalk and lane of traffic in front of 235 Second Street. (+\$23m)
- Maintaining cut-and-cover construction with decking on Second Street between Howard and Clementina Streets.
- Mining the Howard Street crossing. (+\$208m)
- Performing a value engineering exercise at the conclusion of the 30% design phase.



# Questions?

**TJPA**  
TRANSBAY JOINT POWERS AUTHORITY

201 Mission Street, Suite 2100 San Francisco, CA 94105 • 415.597.4620 • [www.transbaycenter.org](http://www.transbaycenter.org)
