

Prop L and Prop AA Allocation Request Forms
June Board Action
Table of Contents

No.	Fund Source	Project Sponsor ¹	Expenditure Plan Line Item/ Category Description	Project Name	Phase	Funds Requested	Page No.
1	Prop L	SFMTA	Muni Maintenance	40' Hybrid Motor Coach Replacement (94 Vehicles)	Construction	\$ 32,300,000	3
2	Prop L	SFMTA	Muni Maintenance	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)	Construction	\$ 10,000,000	11
3	Prop L	SFPW	Street Resurfacing, Rehabilitation, and Maintenance	Street Repair and Cleaning Equipment	Construction	\$ 435,000	21
4	Prop L	SFPW	Street Resurfacing, Rehabilitation, and Maintenance	Various Locations Pavement Renovation No. 68	Construction	\$ 1,800,000	31
5	Prop L	SFPW	Pedestrian and Bicycle Facilities Maintenance	Public Sidewalk and Curb Repair	Construction	\$ 551,000	41
6	Prop L	SFMTA	Traffic Signs and Signals Maintenance	Traffic Signal Upgrade Contract 36 - Additional Funds	Construction	\$ 1,758,637	85
7	Prop L	SFMTA	Safer and Complete Streets	Central Embarcadero Safety	Design	\$ 200,000	101
8	Prop L	SFMTA	Safer and Complete Streets	Safe Routes to School Non-Infrastructure	Construction	\$ 466,000	113
9	Prop L	SFMTA	Safer and Complete Streets	School Traffic Calming Program	Planning, Design, Construction	\$ 2,000,000	121
10	Prop AA	SFPW	Street Repair and Reconstruction	8th St, Clay St and Leavenworth St Pavement Renovation	Construction	\$ 2,360,572	141
11	Prop AA	SFPW	Pedestrian Safety	Japantown Buchanan Mall Improvements	Design	\$ 100,000	151
Total Requested						\$ 51,971,209	

¹ Acronym: SFCTA (San Francisco County Transportation Authority), SFMTA (San Francisco Municipal Transportation Agency), and SFPW (San Francisco Public Works)

[this page intentionally left blank]

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Muni Maintenance
Current PROP L Request:	\$32,300,000
Supervisory District	Citywide

REQUEST

Brief Project Description

Replace 94 40' hybrid vehicles that were procured in 2013 and have reached the end of their useful life. The original scope of work was to replace these 94 vehicles with zero emission vehicles but due to impacts from COVID, facility upgrade progress is delayed and the SFMTA has to purchase additional hybrid vehicles.

Detailed Scope, Project Benefits and Community Outreach

Prop L funds are requested for the replacement of 94 hybrid 40' vehicles that were procured in 2013 and have reached the end of their useful lives. The original scope of work was to replace these 94 vehicles with zero emission vehicles but due to impacts from COVID, facility upgrade progress is delayed and the SFMTA has to purchase additional hybrid vehicles. The intention of this procurement is to conditionally accept the vehicles in 2 years from start of procurement, which would help to lower the average age of the bus fleet. Vehicles will be procured through a cooperative agreement through a state contract.

Effective October 1, 2019, the Innovative Clean Transit regulation requires all public transit agencies in the state to transition from internal combustion engine buses (ICEBs) to zero-emission buses (ZEBs), such as battery-electric (BEB) or fuel cell electric (FCEB), by 2040. The regulation requires a progressive increase of an agency's new bus purchases to be ZEBs based on its fleet size. The SFMTA submitted the Rollout Plan for the California Air Resources Board's regulation, updated in July 2022, which outlined the procurement schedule for 40' and 60' battery electric buses.

SFMTA intends to purchase vehicle with Bus Original Equipment Manufacture (OEM) recommended options that meets SFMTA service demands and topography. This will avoid costly special customizations involving additional engineering analysis and engineering testing to validate the designs. Prior to mid 2000, SFMTA buses had specified special configurations to meet San Francisco's needs and service demands. An example is wider exit doors to allow for passengers to enter and exit the vehicle with better flow. However, such customization required the Bus OEM to perform additional engineering analysis and Altoona testing which caused additional money, resources, and time. Since mid-2000, SFMTA have applied lessons learned and will purchase

4

vehicles with Bus OEM recommended options to avoid special customizations. These 94 hybrid vehicles are replacing the 2013 New Flyer Xcelsior model XDE 40 purchase using Prop K funds. These new vehicles will be using the latest hybrid technology and components. SFMTA anticipates to have better fuel consumption, reliable, comfortable and safer riding experiences to San Francisco riders. The passenger capacity will remain unchanged.

The Transit industry was impacted heavily by the pandemic on materials supply chain, labor resources and the infrastructure funding availabilities. As SFMTA continues to face the challenges of upgrading the electrification network, the SFMTA needs to continue providing reliable transit service to the San Francisco riders.

Project Location

San Francisco

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$32,300,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)	Jul-Aug-Sep	2023	Jan-Feb-Mar	2024
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)	Jan-Feb-Mar	2024	Oct-Nov-Dec	2024
Advertise Construction				
Start Construction (e.g. Award Contract)	Oct-Nov-Dec	2024		
Operations (OP)				
Open for Use			Oct-Nov-Dec	2026
Project Completion (means last eligible expenditure)			Oct-Nov-Dec	2028

SCHEDULE DETAILS

The project is currently at detail design phase. SFMTA is working with the Bus OEM to finalize the detail design and configurations. SFMTA will use the State of Washington Cooperative Purchase Agreement for this procurement project.

PROJECT SCHEDULE:

SFMTA Board approval of draft contract: September 2024

SF BOS Budget and Finance Committee: October 2024

SF BOS approval of contract: October 2024

Notice to Proceed: November 2024

Vendor advances design to 100%: Dec 2024 -Feb 2025

Vehicle Production/delivery/acceptance: March 2025 – Dec 2026

Warranty: through FY28

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-206: Muni Maintenance	\$0	\$32,300,000	\$0	\$32,300,000
CCSF Transportation Sustainability Fee	\$0	\$843,331	\$0	\$843,331
City General Fund	\$0	\$12,300,496	\$0	\$12,300,496
FTA TCP	\$72,770,654	\$0	\$0	\$72,770,654
MTC RM3	\$0	\$0	\$27,013,000	\$27,013,000
Phases In Current Request Total:	\$72,770,654	\$45,443,827	\$27,013,000	\$145,227,481

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP L	\$0	\$32,300,000	\$0	\$32,300,000
CCSF Transportation Sustainability Fee	\$0	\$843,331	\$0	\$843,331
City General Fund	\$0	\$12,300,496	\$0	\$12,300,496
City General Fund Prop B	\$0	\$0	\$30,500	\$30,500
City Operating Fund	\$0	\$2,165,279	\$0	\$2,165,279
Dev-Fee-Mission Rock	\$0	\$0	\$0	\$0
FTA TCP	\$72,770,654	\$0	\$0	\$72,770,654
MTC RM3	\$0	\$0	\$27,013,000	\$27,013,000
Funding Plan for Entire Project Total:	\$72,770,654	\$47,609,106	\$27,043,500	\$147,423,260

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$461,000		Previous Contract
Environmental Studies	\$0		
Right of Way	\$0		

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Design Engineering	\$1,730,000		Previous Contract
Construction	\$145,147,000	\$32,300,000	Previous Contract
Operations	\$0		
Total:	\$147,338,000	\$32,300,000	

% Complete of Design:	50.0%
As of Date:	05/08/2024
Expected Useful Life:	12 Years

San Francisco County Transportation Authority

Prop L/Prop AA Allocation Request Form

MAJOR LINE ITEM BUDGET

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)					
Budget Line Item	Totals	% of contract	Consultant	SFMTA	Contractor
1. Contract	\$ 133,077,505				
Vehicles (94)					\$ 108,100,000
Training, Spare Parts, Special Tools, Manuals, and Licences					\$ 6,178,000
Sales Tax					\$ 10,093,500
Escalation					\$ 8,706,005
Subtotal	\$ 133,077,505				\$ 133,077,505
2. OCS Replacement					
3. Soft Cost					
Project Management	\$ 665,388	0.50%		\$ 665,388	
Engineering Supports	\$ 1,197,698	0.90%		\$ 1,197,698	
Maintenance Supports	\$ 1,663,469	1.25%		\$ 1,663,469	
Contracting Costs	\$ 39,923	0.03%		\$ 39,923	
Consultant Services	\$ 399,233	0.30%	\$ 399,233		
4. Other Direct Costs *	\$ 199,616	0.15%		\$ 199,616	
5. Contingency	\$ 7,984,650.30	6.00%		\$ 7,984,650	
TOTAL CONSTRUCTION PHASE	\$ 145,227,481		\$ 399,233	\$ 11,750,744	\$ 133,077,505

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$32,300,000	Total PROP L Recommended	\$32,300,000

SGA Project Number:		Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	12/31/2027
Phase:	Construction	Fundshare:	22.25%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2025/26	FY2026/27	FY2027/28	Total
PROP L EP-206	\$20,000,000	\$10,500,000	\$1,800,000	\$32,300,000

Deliverables

1. Quarterly progress reports (QPRs) shall include % complete to date, photos of vehicles received, upcoming project milestones (e.g. pilot vehicle, delivery, acceptance, revenue service), and delivery updates including work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, number of vehicles received or placed in service, and any issues that could impact delivery, in addition to all other requirements described in the Standard Grant Agreement.

2. Upon receipt of the first vehicle, provide two digital photos of the new vehicle, with at least one photo showing the Prop L decal affixed to the vehicle. See SGA for guidance.

Special Conditions

1. The recommendation is contingent upon a commitment by the SFMTA to maintain the new motor coaches in a state of good repair, including a mid-life overhaul program to allow them to meet or exceed expectations for their useful lives per FTA guidelines.

2. Our recommendation is contingent upon a waiver to the Prop L policy that at the time of a Prop L allocation request, all funding for the subject project phase(s) are committed to the project. SFMTA's funding plan has \$72,770,654 in planned federal transit formula funds that they anticipate MTC will program by December 2024 and MTC staff has indicated that this is a reasonable assumption.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	77.76%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	78.09%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	40' Hybrid Motor Coach Replacement (94 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$32,300,000
--------------------------------	--------------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

ML

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Gary Chang	Joel C Goldberg
Title:	Project Manager	Grants Procurement Manager
Phone:	555-5555	555-5555
Email:	gary.chang@sfmta.com	joel.goldberg@sfmta.com

San Francisco County Transportation Authority

Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Muni Maintenance
Current PROP L Request:	\$10,000,000
Supervisory District	Citywide

REQUEST

Brief Project Description

Purchase 6 60' and 12 40' Battery Electric Buses and all required accessories, and deploy the vehicles in revenue service as replacements for 18 40' diesel electric hybrid buses. Replacing vehicles at the end of their useful life will keep the average fleet age down, which increases the reliability of service. Battery Electric Buses also generate zero greenhouse gas emissions because they are powered by a battery in their operating system rather than fuel and don't produce harmful exhaust.

Detailed Scope, Project Benefits and Community Outreach

Purchase 6 60' and 12 40' battery electric buses, along with all required accessories (Tools & Equipment, Spare Parts, Training, and Data Monitoring subscription), and deploy the vehicles in revenue service as replacements for 18 40' diesel-electric hybrid buses. Vehicles are anticipated to be procured from two manufacturers, Gillig and New Flyer vehicles.

- For Gillig, the estimated procurement is 5 x 40' buses and will be procured with a Virginia state consortium contract
- For New Flyer, the estimated procurement is 6 x 60' and 7 x 40' buses and will be procured using a Washington state consortium contract
- For both manufacturers, 40' buses are estimated to cost \$1.5M and 60' buses are estimated to cost \$1.9M

The SFMTA is working on producing a report outlining the findings of the 40' battery electric bus pilot program that is anticipated to be available in July 2024. This evaluation of the suitability of battery electric buses will allow SFMTA to develop future procurement strategies for battery electric buses at scale. The requested vehicles are not meant to extend the pilot since SFMTA has determined that all buses tested can meet the SFMTA's performance requirements, but that reliability of battery buses is expected to improve in the next generation of buses. As determined during the pilot program, the SFMTA desires to procure and evaluate BEBs from Gillig in the near term to increase competition and ensure the SFMTA has multiple options for its future procurement strategy. Gillig is a local bus manufacturer, and the SFMTA would like to establish a long-term partnership with them. New Flyer

12

has demonstrated the best overall performance in the battery bus pilot program. This necessitates using two separate contracts for New Flyer and Gillig.

The 18 battery electric buses are replacing 18 New Flyer 2013 XDE40 diesel-hybrid coaches that were procured using Prop K funds in 2012 and delivered to the SFMTA in 2013. The diesel-hybrid buses will have reached the end of their useful lives when they are replaced. The battery buses will offer similar performance, capacity, and service capability to the replaced diesel-hybrid buses and will be configured to match existing buses in important aspects like the onboard signage, CAD/AVL system, passenger counter system, doors, seating, interior trim, and paint schemes. The SFMTA will work with the bus manufacturers to incorporate necessary systems and components while utilizing as many standard options as possible to reduce unnecessary costs.

This project is currently in the Design Engineering phase. SFMTA has anticipated MTAB approval of Gillig contract in July and delivery of buses in 2025, with New Flyer MTAB approval in February 2025 and delivery of buses in 2026/2027.

The 60' battery electric buses shall be stored and operated out of the Islais Creek bus facility, and the 40' battery electric buses shall be stored and operated out of the Woods bus facility. This procurement aligns with the SFMTA's Zero Emission Bus Rollout Plan. This procurement is an important step to replacing diesel/hybrid buses with battery electric buses and achieving a complete zero-emissions fleet as highlighted in the Rollout Plan. The SFMTA will use onboard vehicle telematics systems to capture data on the vehicles and perform an evaluation of the suitability of 60' battery electric buses for the SFMTA, which will allow the development of future procurement strategies for battery electric buses at scale.

The project scope does not include the charging infrastructure needed to accommodate the 18 battery electric buses, which will need to be installed prior to their arrival. The current request will allow the SFMTA to issue NTP to the bus manufacturer(s) to begin the construction of battery buses.

Effective October 1, 2019, the Innovative Clean Transit regulation requires all public transit agencies in the state to transition from internal combustion engine buses (ICEBs) to zero-emission buses (ZEBs), such as battery-electric (BEB) or fuel cell electric (FCEB), by 2040. The regulation requires a progressive increase of an agency's new bus purchases to be ZEBs based on its fleet size. The SFMTA submitted the Rollout Plan for the California Air Resources Board's regulation, updated in July 2022, which outlined the procurement schedule for 40' and 60' battery electric buses.

Project Location

Citywide

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

Justification for Multi-phase Request

Fleet capital projects have 4 phases: Planning, Contracting, Design & Procurement, and Warranty Close-Out.

*Planning covers what is for other projects two phases, Planning & Preliminary Engineering.

*Contracting covers what for other projects is Detail Design.

*Design & Procurement is what is called Construction in other projects.

*Warranty & Closeout covers what is Administrative Closure for other projects.

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$10,000,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)	Jan-Feb-Mar	2023	Jul-Aug-Sep	2024
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)	Jul-Aug-Sep	2023	Apr-May-Jun	2025
Advertise Construction				
Start Construction (e.g. Award Contract)	Jan-Feb-Mar	2025		
Operations (OP)				
Open for Use			Apr-May-Jun	2026
Project Completion (means last eligible expenditure)			Oct-Nov-Dec	2030

SCHEDULE DETAILS

GILLIG PROJECT SCHEDULE:

SFMTA Board: approval of consortium: July 2024
 Notice to Proceed: August 2024
 Vehicle delivery/acceptance starts: Q3 FY 2024/25
 Vehicle delivery completion: Q1 FY 2025/26
 Contract: Virginia State

NEW FLYER PROJECT SCHEDULE

SFMTA Board: approval of consortium: February 2025
 SF BOS approval of contract: March 2025
 Notice to Proceed: April 2025
 Vehicle delivery/acceptance starts: Q3 FY 2025/26
 Vehicle delivery completion: Q3 FY 2026/2027
 Contract: Washington State

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-206: Muni Maintenance	\$0	\$10,000,000	\$0	\$10,000,000
GeneralFundPopBaseTransitFY26	\$0	\$48,610	\$0	\$48,610
MTCRM3FleetFacilityFY24	\$0	\$12,374,000	\$0	\$12,374,000
TBD: TCP/Prop B/TSF	\$497,272	\$0	\$0	\$497,272
TCPFleetPlanned_FFIFY25	\$18,378,528	\$0	\$0	\$18,378,528
Phases In Current Request Total:	\$18,875,800	\$22,422,610	\$0	\$41,298,410

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP L	\$0	\$10,000,000	\$0	\$10,000,000
CCSF-LCFS-FY22	\$0	\$0	\$316,648	\$316,648
CCSF-TSF-expansion-FY22	\$0	\$0	\$387,862	\$387,862
GeneralFundPopBaseTransitFY26	\$0	\$48,610	\$0	\$48,610
MTCRM3FleetFacilityFY24	\$0	\$14,755,000	\$0	\$14,755,000
MTCRM3FleetFacilityFY25	\$250,234	\$0	\$0	\$250,234
TBD: TCP/Prop B/TSF	\$497,272	\$0	\$0	\$497,272
TCPFleetPlanned_FFIFY25	\$18,378,528	\$0	\$0	\$18,378,528
Funding Plan for Entire Project Total:	\$19,126,034	\$24,803,610	\$704,510	\$44,634,154

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$574,489		Previous Contract
Environmental Studies	\$0		

16

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Right of Way	\$0		
Design Engineering	\$2,761,255		
Construction	\$41,048,176	\$10,000,000	
Operations	\$0		
Total:	\$44,383,920	\$10,000,000	

% Complete of Design:	25.0%
As of Date:	04/10/2024
Expected Useful Life:	12 Years

San Francisco County Transportation Authority

Prop K/Prop AA Allocation Request Form

MAJOR LINE ITEM BUDGET

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)				
Budget Line Item	Totals	% of contract	SFMTA	Contractor
1. Hard Costs	\$ 37,063,816.13			\$ 37,063,816
60-ft Battery Buses (6)	\$ 11,400,000.00			\$ 11,400,000.00
40-ft Battery Buses (12)	\$ 18,000,000.00			\$ 18,000,000.00
Spare Parts, Tools, Training, Manuals, and Licenses	\$ 3,870,000.00			\$ 3,870,000.00
Sales Tax	\$ 2,714,287.50			\$ 2,714,287.50
Escalation	\$ 1,079,528.64	3%		\$ 1,079,528.64
2. Project Management	\$ 926,595.40		\$ 926,595	
3. Maintenance Support	\$ 185,319.08		\$ 185,319	
4. On-site Inspector Support	\$ 555,957.24		\$ 555,957	
5. Engineering Services	\$ 926,595.40		\$ 926,595	
6. Transit Operations Support (Bus/Rail)	\$ 185,319.08		\$ 185,319	
7. Consultant Services	\$ 370,638.16		\$ 370,638	
8. Administrative Support	\$ 185,319.08		\$ 185,319	
9. Other Direct Costs	\$ 92,659.54		\$ 92,660	
10. Contingency	\$ 555,957.24		\$ 555,957	
TOTAL CONSTRUCTION PHASE	\$ 41,048,176		\$ 3,984,360	\$ 37,063,816

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$10,000,000	Total PROP L Recommended	\$10,000,000

SGA Project Number:		Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	06/30/2027
Phase:	Construction	Fundshare:	24.36%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2025/26	FY2026/27	FY2027/28	Total
PROP L EP-206	\$4,000,000	\$5,000,000	\$1,000,000	\$10,000,000

Deliverables

1. Quarterly progress reports (QPRs) shall include % complete to date, photos of vehicles received, upcoming project milestones (e.g. pilot vehicle, delivery, acceptance, revenue service), and delivery updates including work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, number of vehicles received or placed in service, and any issues that could impact delivery, in addition to all other requirements described in the Standard Grant Agreement.
2. Upon receipt of the first vehicle, provide two digital photos of the new vehicle, with at least one photo showing the Prop L decal affixed to the vehicle. See SGA for guidance.

Special Conditions

1. The recommendation is contingent upon a commitment by the SFMTA to maintain the new vehicles in a state of good repair, including a mid-life overhaul program to allow them to meet or exceed expectations for their useful lives per FTA guidelines.
2. Our recommendation is contingent upon a waiver to the Prop L policy that at the time of a Prop L allocation request, all funding for the subject project phase(s) are committed to the project. SFMTA's funding plan has \$18,378,528 in planned federal transit formula funds that they anticipate MTC will program by December 2024 and MTC staff has indicated that this is a reasonable assumption.. The funding plan also includes TBD funding in the amount of \$497,272. SFMTA will not seek additional Prop L funds to fulfill this TBD amount.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	75.79%

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - This Project	No PROP AA	No TNC TAX	77.6%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	60' and 40' Battery Electric Bus Procurement Replacing Motor Coaches (18 Vehicles)
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$10,000,000
--------------------------------	--------------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

ML

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Bhavin Katri	Joel C Goldberg
Title:	Transit Engineer	Grants Procurement Manager
Phone:	(415) 206-4625 x 86	555-5555
Email:	bhavin.khatri@sfmta.com	joel.goldberg@sfmta.com

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Street Repair and Cleaning Equipment
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Street Resurfacing
Current PROP L Request:	\$435,000
Supervisorial District	Citywide

REQUEST

Brief Project Description

Purchase 1 piece of street repair and cleaning equipment to replace equipment that has exceeded its useful life - 1 Asphalt Utility Truck. This requested equipment is California Air Resources Board compliant and will meet current emissions standards.

Detailed Scope, Project Benefits and Community Outreach

San Francisco Public Works requests \$435,000 from the Prop L Street Repair and Cleaning Equipment program which funds replacement of street repair and cleaning equipment such as asphalt pavers, dump trucks, street sweepers, front-end loaders and other equipment for street repair and maintenance. The Fiscal Year 2024/25 request would fund purchase of the following Street Repair and Cleaning Equipment:

- 1 Asphalt Utility Truck

The truck being replaced is used by SFPW Street and Sewer Repair's (SSR) pothole crew (see attached pictures). It is 16 years old, has over 81,000 miles on it and is frequently out of service. The heated bed fails often, causing the asphalt material to get cold and become unusable. This results in lost time for the crew, wasted material, and increased costs. Replacing this truck will provide SSR with a dependable vehicle that keeps the asphalt material hot, is safer to operate because it is equipped with current safety features, and will improve fuel consumption, thereby reducing fuel costs for the bureau.

22

Project Location

Citywide

Is this project in an Equity Priority Community?	No
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$435,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Street Repair and Cleaning Equipment
Primary Sponsor:	Department of Public Works

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)				
Advertise Construction				
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2024		
Operations (OP)				
Open for Use			Oct-Nov-Dec	2024
Project Completion (means last eligible expenditure)			Jan-Feb-Mar	2025

SCHEDULE DETAILS

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Street Repair and Cleaning Equipment
Primary Sponsor:	Department of Public Works

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-215: Street Resurfacing	\$0	\$435,000	\$0	\$435,000
Phases In Current Request Total:	\$0	\$435,000	\$0	\$435,000

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$0		
Construction	\$435,000	\$435,000	SFPW recent purchases/quotes
Operations	\$0		
Total:	\$435,000	\$435,000	

% Complete of Design:	N/A
As of Date:	N/A
Expected Useful Life:	10 Years

**San Francisco County Transportation Authority
Prop L/Prop AA/TNC Tax Allocation Request Form**

**MAJOR LINE ITEM BUDGET
STREET REPAIR AND CLEANING EQUIPMENT**

SUMMARY BY MAJOR LINE ITEM			
Budget Line Item	Unit Cost	Quantity	Total Cost
Asphalt Utility Truck	435,000	1	435,000
TOTAL CONSTRUCTION PHASE	\$ 435,000	\$ 1	\$ 435,000

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Street Repair and Cleaning Equipment
Primary Sponsor:	Department of Public Works

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$435,000	Total PROP L Recommended	\$435,000

SGA Project Number:	215-908003	Name:	Street Repair and Cleaning Equipment
Sponsor:	Department of Public Works	Expiration Date:	12/31/2026
Phase:	Construction	Fundshare:	100.0%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2025/26	Total
PROP L EP-215	\$435,000	\$435,000

Deliverables

1. Quarterly progress reports shall provide the status of this purchase, including whether the equipment has been ordered, received, or placed into service as of the end of the previous quarter.
2. Quarterly progress reports shall include 2-3 digital photos of the piece of equipment approved for service during the prior quarter, including at least one photo showing the Prop L logo affixed to the equipment.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	0.0%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	0.0%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Street Repair and Cleaning Equipment
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$435,000
--------------------------------	-----------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

JLY

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	John Leal	Victoria Chan
Title:	Heavy Equipment Operations Supervisor	Budget Manager
Phone:	555-5555	(415) 205-6316
Email:	john.leal@sfdpw.org	victoria.w.chan@sfdpw.org

Attachment 1 - Photos of Equipment

1. New truck:



3, 4, 5 Yard Models

Single axel production pothole patcher.

2. Existing truck:



3. Existing Truck:



[this page intentionally left blank]

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Various Locations Pavement Renovation No. 68
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Street Resurfacing
Current PROP L Request:	\$1,800,000
Supervisorial Districts	District 01, District 05, District 07, District 10, District 11

REQUEST

Brief Project Description

The Prop L funds requested will fund the paving scope of work which includes demolition, pavement renovation of 38 blocks, construction and retrofit of approximately 140 curb ramps, new sidewalk construction, traffic control, and all related and incidental work within project limits.

Detailed Scope, Project Benefits and Community Outreach

Public Works (DPW) requests FY 2024/25 Prop L funds for the construction of the Various Locations Pavement Renovation No. 68 project. The Prop L funds requested will fund the paving scope of work which includes demolition, pavement renovation of 38 blocks, construction and retrofit of approximately 140 curb ramps, new sidewalk construction, traffic control, and all related and incidental work within project limits.

The project schedule will be coordinated with other projects and agencies as work programs are determined to minimize construction impacts to the City.

DPW inspects each of the City's blocks and assigns a Pavement Condition Index (PCI) score every two years. The PCI score ranges from a low of 0 to a high of 100. These scores assist DPW with implementing the pavement management strategy of aiming to preserve streets by applying the right treatment to the right roadway at the right time. Streets are selected based on PCI scores as well as the presence of transit and bicycle routes, street clearance (i.e., coordination with utilities) and geographic equity. The average PCI score within the project limits is upper 40's.

Project candidates:

Anza St from Parker Ave to Stanyan Blvd - 2 Blocks
 Arellano Ave from Serrano Dr to Holloway Ave - 1 Block
 Buchanan St from Fell St to Hayes St - 2 Blocks
 Cardenas Ave from Gonzalez Dr to Cambon Dr - 1 Block
 Crespi Dr from Gonzalez Dr to Juan Bautista Cir - 6 Blocks
 Faxon Ave from Grafton Ave to Holloway Ave - 1 Block
 Gonzalez Dr from Crespi Dr to Crespi Dr - 1 Block

32

Holloway Ave from Arellano Ave Tapia Dr - 3 Blocks

Jennings St from Cargo Way to Evans Ave - 3 blocks

Juan Bautista Cir from Fuente Ave to Font Blvd, Crespi Dr to Bucareli Dr - 9 Blocks

Lake St from Arguello Blvd to 2nd Ave - 1 Block

Sargent St from Bright St to Head St, Ramsell St to Arch St - 2 Blocks

Varela Ave from Holloway Ave to Crespi Dr - 1 Block

Winston Dr from Junipero Serra Blvd to 19th Ave, Buckingham Way to Lake Merced Blvd - 5 Blocks

All candidates are subject to substitution and schedule changes pending , visual confirmation, utility clearances and coordination with other agencies. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the candidates to be postponed.

Project Location

Project Locations in District 1, 5, 7, 10, 11 (see details in Scope)

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$1,800,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Various Locations Pavement Renovation No. 68
Primary Sponsor:	Department of Public Works

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)	Jul-Aug-Sep	2021	Oct-Nov-Dec	2023
Advertise Construction	Apr-May-Jun	2024		
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2024		
Operations (OP)				
Open for Use			Jan-Feb-Mar	2026
Project Completion (means last eligible expenditure)			Apr-May-Jun	2026

SCHEDULE DETAILS

The project was coordinated via the City's 5 Year Plan (<https://sanfrancisco.dotmapsapp.com/map/>) and no other agency decided to join the project.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Various Locations Pavement Renovation No. 68
Primary Sponsor:	Department of Public Works

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-215: Street Resurfacing	\$0	\$1,800,000	\$0	\$1,800,000
Road Maintenance and Rehabilitation (RMRA)	\$0	\$5,629,549	\$0	\$5,629,549
Phases In Current Request Total:	\$0	\$7,429,549	\$0	\$7,429,549

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP L	\$0	\$1,800,000	\$0	\$1,800,000
Highway Users Tax (HUTA)	\$0	\$0	\$630,000	\$630,000
Road Maintenance and Rehabilitation (RMRA)	\$0	\$5,629,549	\$0	\$5,629,549
Funding Plan for Entire Project Total:	\$0	\$7,429,549	\$630,000	\$8,059,549

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$630,000		Actual costs
Construction	\$7,429,549	\$1,800,000	Actual low bid received
Operations	\$0		
Total:	\$8,059,549	\$1,800,000	

% Complete of Design:	100.0%
As of Date:	12/31/2023
Expected Useful Life:	15 Years

San Francisco County Transportation Authority
Prop L/Prop AA/TNC Tax Allocation Request Form

MAJOR LINE ITEM BUDGET - VARIOUS LOCATIONS PAVEMENT RENOVATION NO. 68

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)					
Budget Line Item	Totals	% of contract	SFPW	SFMTA	Contractor
1. Contract					
Traffic Control/ Pavement Markings	\$ 848,673				\$ 848,673
Planing	\$ 522,440				\$ 522,440
Asphalt Concrete	\$ 1,501,500				\$ 1,501,500
Concrete Base/Pavement	\$ 574,050				\$ 574,050
Concrete Curb	\$ 1,021,330				\$ 1,021,330
Concrete Sidewalk	\$ 260,370				\$ 260,370
Hydrant and Watermain Valve Box	\$ 11,292				\$ 11,292
Pull Box/Adjust Manhole	\$ 9,240				\$ 9,240
Culvert and Catch Basin Inlets	\$ 23,760				\$ 23,760
Mobilization/Demobilization	\$ 159,500				\$ 159,500
Excavation and Backfill Support	\$ 12,100				\$ 12,100
Allowance for Partnering Req and Fees	\$ 30,000				\$ 30,000
Sewer Related Work	\$ 437,520				\$ 437,520
Traffic Signal Related Work	\$ 54,184				\$ 54,184
Landscaping and Tree Protection	\$ 37,411				\$ 37,411
Subtotal	\$ 5,503,370				\$ 5,503,370
2. Construction Management/Support	\$ 1,375,842	25%	\$ 1,100,674	\$ 275,168	
3. Contingency	\$ 550,337	10%			
TOTAL CONSTRUCTION PHASE	\$ 7,429,549		\$ 1,100,674	\$ 275,168	\$ 5,503,370

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Various Locations Pavement Renovation No. 68
Primary Sponsor:	Department of Public Works

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$1,800,000	Total PROP L Recommended	\$1,800,000

SGA Project Number:	215-908004	Name:	Various Locations Pavement Renovation No. 68
Sponsor:	Department of Public Works	Expiration Date:	03/31/2027
Phase:	Construction	Fundshare:	24.23%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	Total
PROP L EP-215	\$1,260,000	\$540,000	\$1,800,000

Deliverables

1. Quarterly progress reports (QPRs) shall include % complete to date, photos of work being performed, upcoming project milestones (e.g. ground-breaking, ribbon-cutting), and delivery updates including work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, and any issues that may impact delivery, in addition to all other requirements described in the Standard Grant Agreement.
2. With the first QPR (July 2024) SFPW shall provide 2-3 photos of typical before conditions; with the first quarterly report following initiation of fieldwork Sponsor shall provide a photo documenting compliance with the Prop L attribution requirements as described in the SGA; and on completion of the project Sponsor shall provide 2-3 photos of completed work.

Notes

1. Reminder: All construction signage, project fact sheets, websites and other similar materials shall comply with the attribution requirements established in the Standard Grant Agreement.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	75.77%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	77.67%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Various Locations Pavement Renovation No. 68
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$1,800,000
--------------------------------	-------------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.






Initials of sponsor staff member verifying the above statement:

JLY


CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Paul Barradas	Victoria Chan
Title:	Project Manager	Budget Manager
Phone:	(415) 554-8249	(415) 205-6316
Email:	paul.barradas@sfdpw.org	victoria.w.chan@sfdpw.org

38 Street Resurfacing Program: Various Locations Pavement Renovation No 68

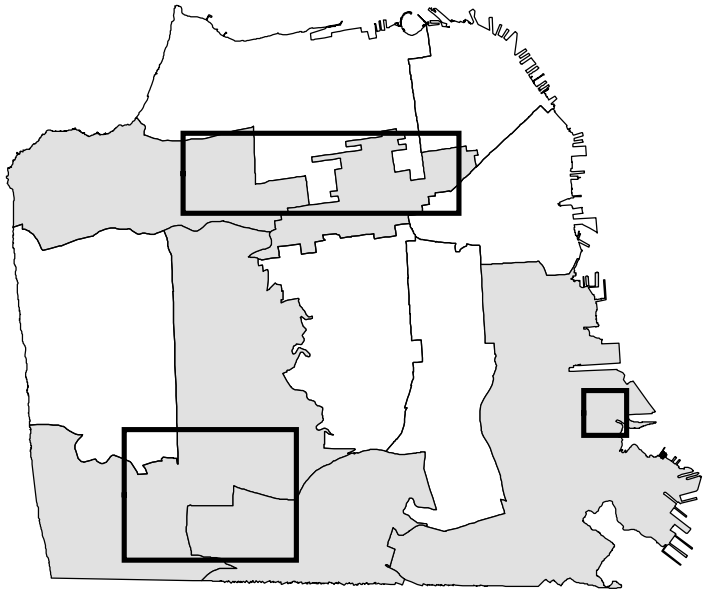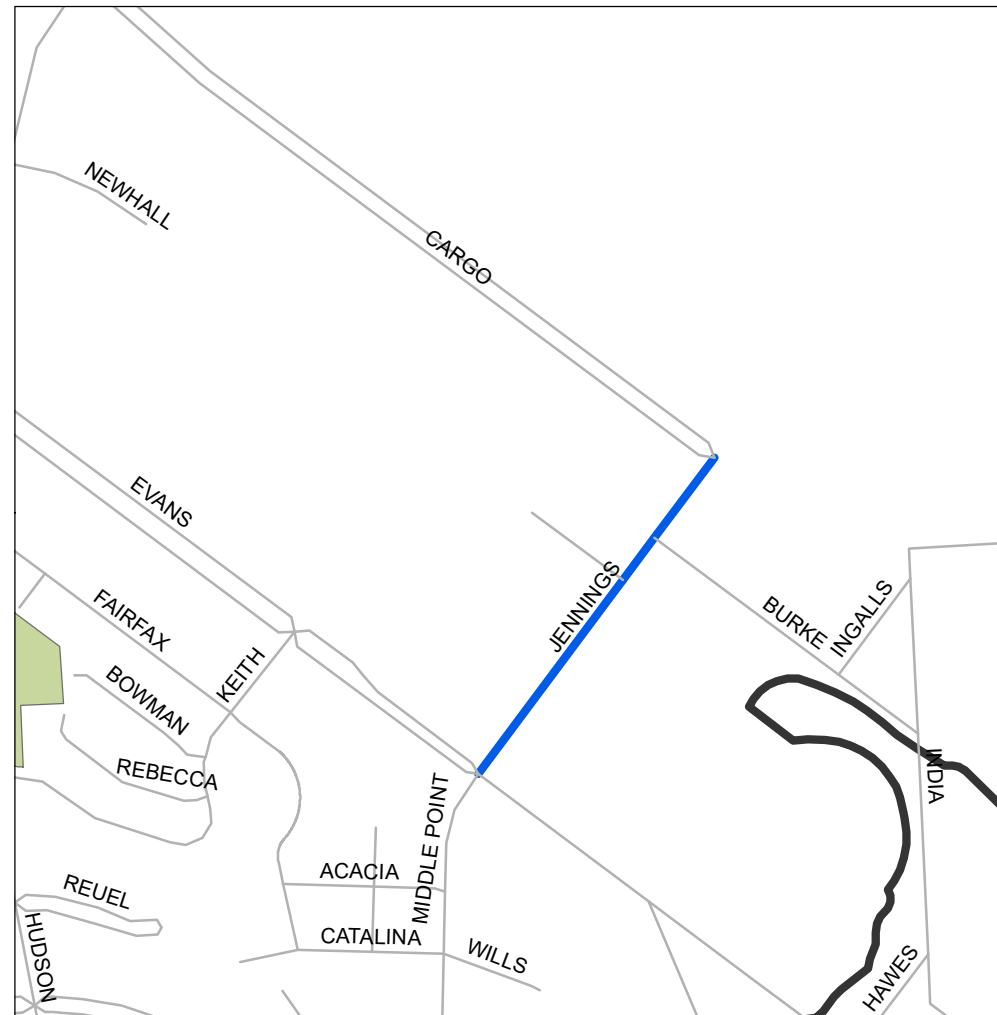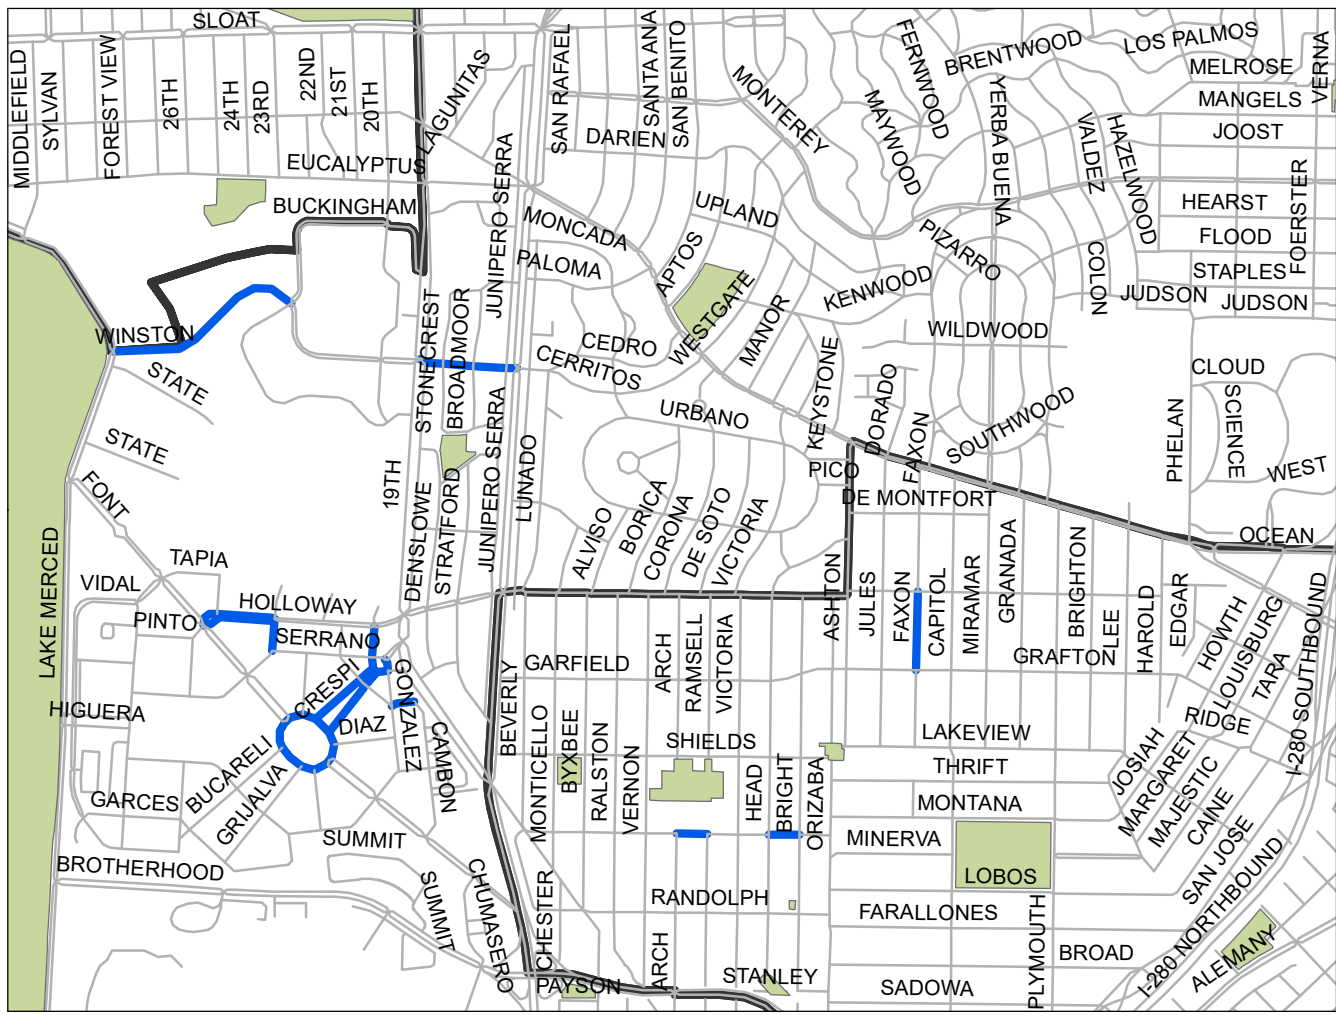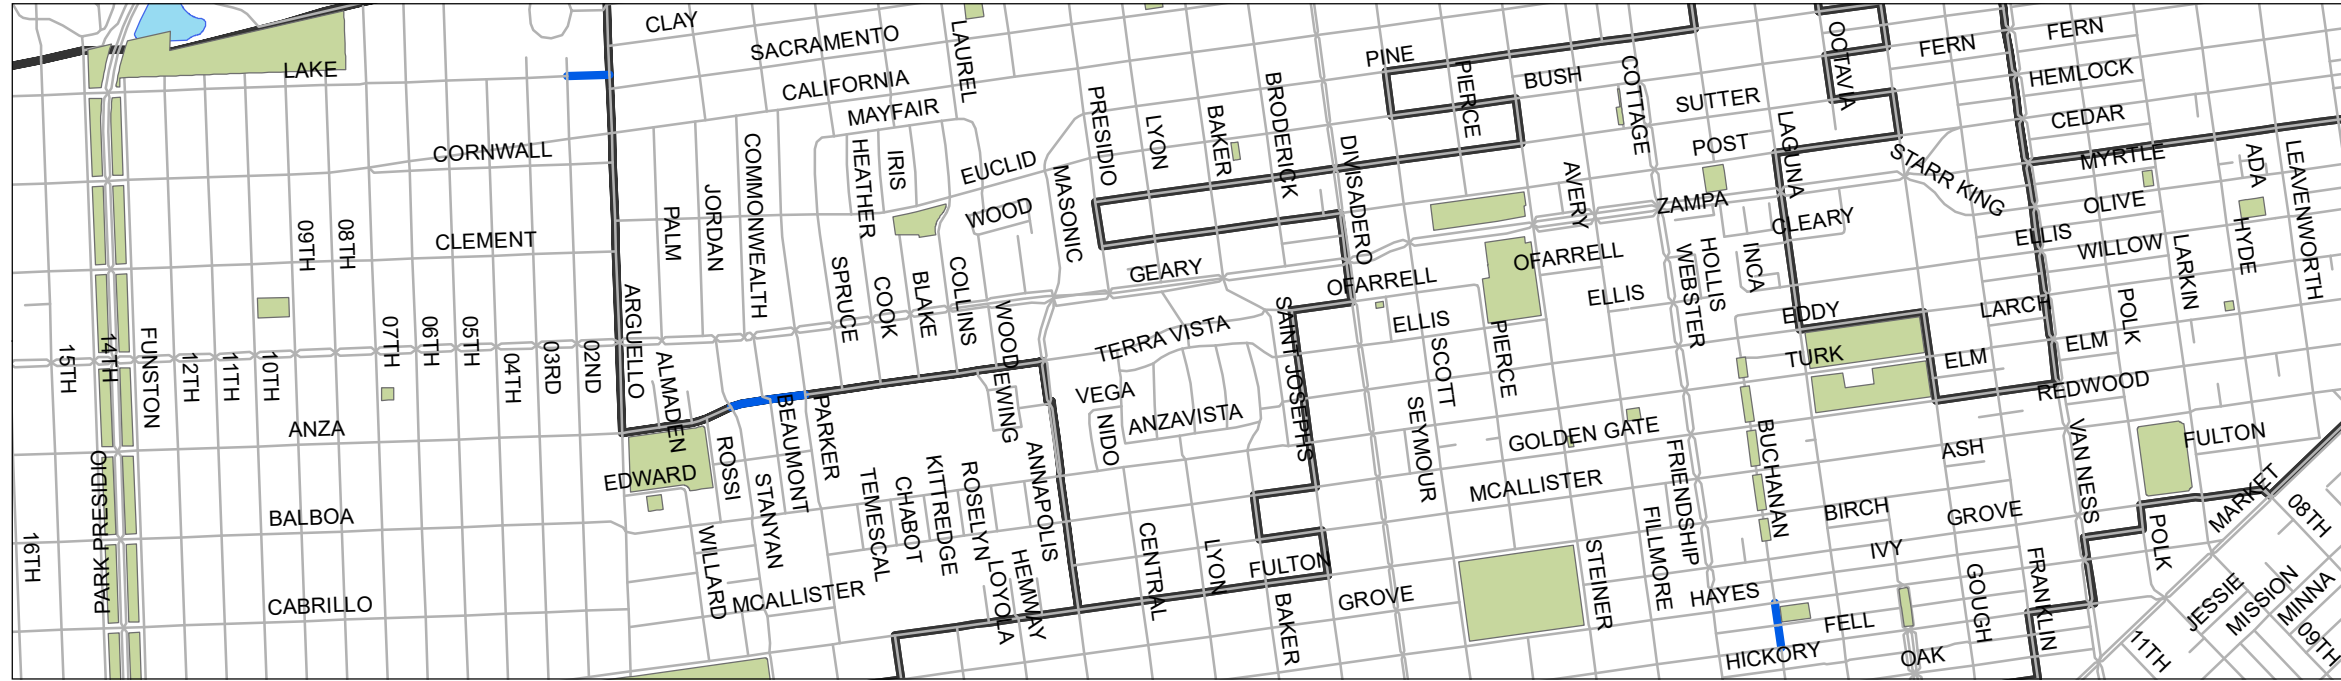

Legend

 Various Locations Pavement Renovation No 68

NOTES:
Information as of March 2024


All Public Works Street Resurfacing Program candidates are subject to substitution and schedule changes pending available funding, visual confirmation, utility clearances and coordination with other agencies and are NOT guaranteed to be moved forward to construction. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the Public Works street Resurfacing Program candidates to be postponed or dropped from consideration.

Various Locations Pavement Renovation No 68

Project Location Candidates

Note: All Public Works Street Resurfacing Program candidates are subject to substitution and schedule changes pending available funding, visual confirmation, utility clearances and coordination with other agencies and are NOT guaranteed to be moved forward to construction. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the Public Works Street Resurfacing Program candidates to be postponed or dropped from consideration.

On Street	From Street	To Street	BOS
ANZA ST	PARKER AVE	BEAUMONT AVE	1
ANZA ST	BEAUMONT AVE	STANYAN BLVD	1
ARELLANO AVE	SERRANO DR	HOLLOWAY AVE	7
BUCHANAN ST	FELL ST	LINDEN ST	5
BUCHANAN ST	LINDEN ST	HAYES ST	5
CARDENAS AVE	GONZALEZ DR	CAMBON DR	7
CRESPI DR	GONZALEZ DR \ UNNAMED 106	END	7
CRESPI DR	SERRANO DR \ VARELA AVE	END	7
CRESPI DR	END	CARDENAS AVE	7
CRESPI DR	END	CARDENAS AVE	7
CRESPI DR	CARDENAS AVE	JUAN BAUTISTA CIR	7
CRESPI DR	CARDENAS AVE	JUAN BAUTISTA CIR	7
FAXON AVE	GRAFTON AVE	HOLLOWAY AVE	11
GONZALEZ DR	CRESPI DR \ SERRANO DR	CRESPI DR \ UNNAMED 106	7
HOLLOWAY AVE	ARELLANO AVE	FONT BLVD \ TAPIA DR	7
HOLLOWAY AVE	ARELLANO AVE	TAPIA DR	7
HOLLOWAY AVE	TAPIA DR	FONT BLVD \ TAPIA DR	7
JENNINGS ST	CARGO WAY	BURKE AVE	10
JENNINGS ST	BURKE AVE	NEWHALL ST	10
JENNINGS ST	NEWHALL ST	EVANS AVE \ MIDDLE POINT RD	10
JUAN BAUTISTA CIR	FUENTE AVE	FONT BLVD	7
JUAN BAUTISTA CIR	CRESPI DR	FUENTE AVE	7
JUAN BAUTISTA CIR	CRESPI DR	CRESPI DR	7
JUAN BAUTISTA CIR	DIAZ AVE	CRESPI DR	7
JUAN BAUTISTA CIR	FONT BLVD	DIAZ AVE	7
JUAN BAUTISTA CIR	JOSEPHA AVE	FONT BLVD	7
JUAN BAUTISTA CIR	GRIJALVA DR	JOSEPHA AVE	7
JUAN BAUTISTA CIR	BUCARELI DR	GRIJALVA DR	7
JUAN BAUTISTA CIR	FONT BLVD	BUCARELI DR	7
LAKE ST	ARGUELLO BLVD	02ND AVE	1
SARGENT ST	BRIGHT ST	HEAD ST	11
SARGENT ST	RAMSELL ST	ARCH ST	11
VARELA AVE	HOLLOWAY AVE	CRESPI DR \ SERRANO DR	7
WINSTON DR	JUNIPERO SERRA BLVD \ MERCEDES WAY	JUNIPERO SERRA BLVD	7
WINSTON DR	JUNIPERO SERRA BLVD	BROADMOOR DR	7
WINSTON DR	BROADMOOR DR	STONECREST DR	7
WINSTON DR	STONECREST DR	19TH AVE	7
WINSTON DR	BUCKINGHAM WAY	LAKE MERCED BLVD	7

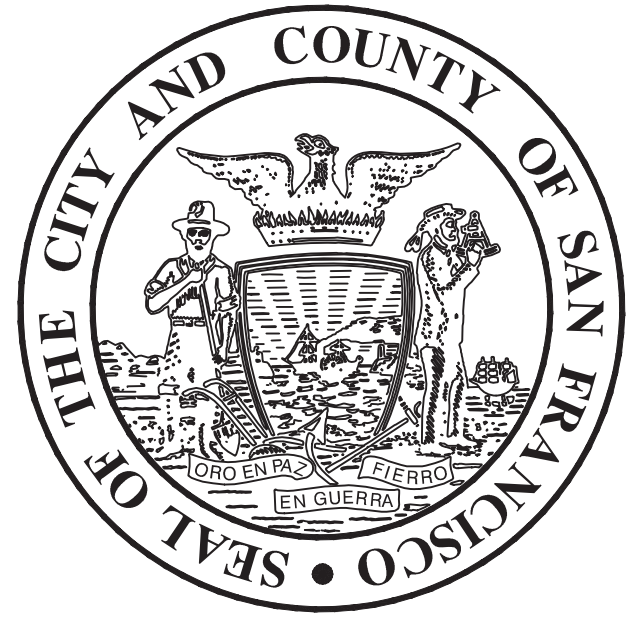

VARIOUS LOCATIONS PAVEMENT RENOVATION NO. 68

SOURCING EVENT ID. 0000005635



City and County of San Francisco

London Breed, Mayor
Carla Short, Director

Public Works
Infrastructure Design & Construction

Albert Ko, P.E.
City Engineer & Deputy Director



JUAN BAUTISTA CIRCLE LOOKING TOWARDS CRESPI DR (GOOGLE MAR 2022)



ANZA ST
LAKE ST

BUCHANAN ST

JUAN BAUTISTA CIR
HOLLOWAY AVE
SARGENT ST
STONECREST DR
WINSTON DR
CARDENAS AVE
ARELLANO AVE
CRESPI DR
FAXON AVE
BROADMOOR DR



JENNINGS ST

LOCATION MAP

REQUIREMENTS TO BIDDERS

- IN ACCORDANCE WITH THE PROVISIONS OF THE CALIFORNIA PUBLIC CONTRACT CODE SECTION 3300, A BID SUBMITTED TO A PUBLIC AGENCY BY A CONTRACTOR WHO IS NOT LICENSED IN ACCORDANCE WITH CHAPTER 9 OF THE BUSINESS AND PROFESSIONS CODE SHALL BE CONSIDERED NON-RESPONSIVE AND SHALL BE REJECTED BY THE PUBLIC AGENCY.
- AT THE TIME OF BID OPENING, THE CONTRACTOR SHALL POSSESS A VALID CLASS "A" CALIFORNIA GENERAL ENGINEERING CONTRACTOR'S LICENSE.

Bid Set: December 2023

REFERENCE INFORMATION & FILE NO. OF SURVEYS							BUREAU OF ENGINEERING CITY & COUNTY OF SAN FRANCISCO SAN FRANCISCO PUBLIC WORKS 49 SOUTH VAN NESS AVENUE, Suite 800 SAN FRANCISCO, CA 94103	Acting Section Mgr: <i>Deanna Calleros</i> DEANNA CALLEROS Date: 12/15/2023	DESIGNED: DATE: A.PERUFFO 09/23		SCALE: N.T.S.	VARIOUS LOCATIONS PAVEMENT RENOVATION NO. 68	SOURCING EVENT ID: 0000005635
TABLE OF REVISIONS								Deputy Bureau Mgr: <i>Fernando Cisneros</i> FERNANDO CISNEROS Date: 12/21/2023	DRAWN: DATE: M.BAUTISTA 09/23		SHEET OF SHEETS 01 OF 95		COVER PAGE REQUIREMENT FOR BIDDERS LOCATION MAP
NO.	DATE	DESCRIPTION	BY	APP.				Bureau Mgr: <i>Patrick Rivera</i> PATRICK RIVERA Date: 12/22/2023	CHECKED: DATE: R.CHIRCOP 09/23			FILE NO. 123,736	REV. NO. 0

THIS DRAWING WAS LAST MODIFIED: 12/04/23 09:02, BY: MBautist

Drawing Path: V:\19471_Various_Locations_Pavement_Renovation_No.68_10037805\2_Design\Working_Drawings\1 - Designs\VI66 - Working Drawings_2022\40.0\BIDDING\0000005635\BIDDING.dwg
 Plot Time: Wed, 06 Dec 2023 7:39am
 Model Units: Feet
 Measurement Units are English

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Public Sidewalk and Curb Repair
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Pedestrian and Bicycle Facilities Maintenance
Current PROP L Request:	\$551,000
Supervisory District	Citywide

REQUEST

Brief Project Description

Repair of damaged public sidewalk, curb and gutters, and angular returns not related to street tree damage.

Detailed Scope, Project Benefits and Community Outreach

Public Works is responsible for repairing sidewalks around City-maintained trees, adjacent to City properties, and at the angular returns of all intersections. The passage of Proposition E in November 2016 resulted in annual funding set-aside to maintain all street trees in the public right-of-way. Tree Maintenance Fund (TMF) funds for sidewalk repairs due to City-maintained trees. Any other damaged public sidewalks, curb and gutters, and angular returns, not due to tree damage, will be repaired with Prop L funds and State Transportation Development Act, Article 3 (TDA-3) funds.

SFPW currently has a backlog of over 1,000 requested repairs to damaged public sidewalks, curb and gutters, and angular returns not related to street tree damage. Instead, damage at these locations is typically caused by trucks driving up on curbs, old age, heavy equipment, vehicular accidents, poor original construction. Provided is a list of outstanding repair locations, which will be used to identify work for this funding request. At an average cost of \$85 per square foot, and \$335 per linear foot, SFPW expects to address approximately 200 sidewalk and curb repair requests on an annual basis with Prop L and TDA funds.

Locations are determined by a combination of SFPW inspection and public complaints, and will be prioritized based on project readiness, community support, and time sensitive urgency. In addition to these locations, SFPW anticipates that emergency response may be required at locations fronting federal, state, school, and housing authority properties, undeveloped lands, roadway structures (i.e. stairways, tunnels, bridges, and retaining walls), as well as locations with special surface sidewalks such as Market Street bricks and Mission Street tiles. Any substitutions of locations would be made in accordance with the 5YPP prioritization criteria.

New locations continuously become priorities as a result of SFPW's ongoing inspections, daily complaints, and reports of trip-and-fall accidents. The locations identified in the current prioritized

42

sidewalk repair list may change based on higher-need locations that cannot be anticipated at this time. SFPW has the flexibility to prioritize and complete locations on an expedited basis if there is potential significant impact to pedestrian access and/or have the highest likelihood of generating claims against the City and County of San Francisco (CCSF). However, failure to correct sidewalk deficiencies, whether they front public or private properties, increases CCSF's exposure to claims and lawsuits resulting from trip-and-fall injuries.

Project Location

Citywide

Is this project in an Equity Priority Community?	TBD
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$551,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Public Sidewalk and Curb Repair
Primary Sponsor:	Department of Public Works

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)				
Advertise Construction				
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2024		
Operations (OP)				
Open for Use			Apr-May-Jun	2024
Project Completion (means last eligible expenditure)			Apr-May-Jun	2024

SCHEDULE DETAILS

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Public Sidewalk and Curb Repair
Primary Sponsor:	Department of Public Works

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-216: Pedestrian and Bicycle Facilities Maintenance	\$0	\$551,000	\$0	\$551,000
Transportation Development Act, Article 3 (TDA-3)	\$0	\$391,760	\$0	\$391,760
Phases In Current Request Total:	\$0	\$942,760	\$0	\$942,760

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$0		
Construction	\$942,760	\$551,000	SFPW Program Cost Estimate
Operations	\$0		
Total:	\$942,760	\$551,000	

% Complete of Design:	N/A
As of Date:	N/A
Expected Useful Life:	15 Years

**San Francisco County Transportation Authority
Prop L/Prop AA/TNC Tax Allocation Request Form**

**MAJOR LINE ITEM BUDGET
PUBLIC SIDEWALK AND CURB REPAIR**

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)		
Budget Line Item	Totals	SFPW
Labor	803,112	803,112
Materials	139,648	139,648
TOTAL CONSTRUCTION PHASE	\$ 942,760	\$ 942,760

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Public Sidewalk and Curb Repair
Primary Sponsor:	Department of Public Works

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$551,000	Total PROP L Recommended	\$551,000

SGA Project Number:	216-908002	Name:	Public Sidewalk and Curb Repair
Sponsor:	Department of Public Works	Expiration Date:	06/30/2025
Phase:	Construction	Fundshare:	58.45%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	Total
PROP L EP-216	\$165,000	\$386,000	\$551,000

Deliverables

1. Quarterly progress reports shall provide the number of sidewalk repairs completed for the quarter and a list of completed repair locations.
2. With quarterly progress reports and at project completion, provide 2- 3 digital photos of construction work in progress and completed projects.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	41.55%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	41.55%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Public Sidewalk and Curb Repair
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$551,000
--------------------------------	-----------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

JLY

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Marianna Williams	Victoria Chan
Title:	Acting Assistant Superintendent, Cement Shop	Budget Manager
Phone:	(415) 695-2049	(415) 205-6316
Email:	marianna.williams@sfdpw.org	victoria.w.chan@sfdpw.org

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 301 25TH AVE	25TH AVE	CALIFORNIA ST	01
Concrete Curb/Sidewalk Repair - 747 23RD AVE	23RD AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 3199 CLEMENT ST	CLEMENT ST	32ND AVE	01
Concrete Curb/Sidewalk Repair - 561 34TH AVE	34TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 121 07TH AVE	07TH AVE	LAKE ST	01
Concrete Curb/Sidewalk Repair - 3910 GEARY BLVD	GEARY BLVD	03RD AVE	01
Concrete Curb/Sidewalk Repair - 132 10TH AVE	10TH AVE	LAKE ST	01
Concrete Curb/Sidewalk Repair - 472 22ND AVE	22ND AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 4725 ANZA ST	ANZA ST	38TH AVE	01
Concrete Curb/Sidewalk Repair - 728 44TH AVE	44TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 554 33RD AVE	33RD AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 750 25TH AVE	25TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 828 26TH AVE	26TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 818 28TH AVE	28TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 6300 FULTON ST	FULTON ST	39TH AVE	01
Concrete Curb/Sidewalk Repair - 1308 CLEMENT ST	CLEMENT ST	14TH AVE	01
Concrete Curb/Sidewalk Repair - 225 STANYAN ST	STANYAN ST	GOLDEN GATE AVE	01
Concrete Curb/Sidewalk Repair - 651 06TH AVE	06TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 4355 CALIFORNIA ST	CALIFORNIA ST	05TH AVE	01
Concrete Curb/Sidewalk Repair - 825 LA PLAYA	LA PLAYA	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 4150 GEARY BLVD	GEARY BLVD	05TH AVE	01
Concrete Curb/Sidewalk Repair - 120 32ND AVE	32ND AVE	EL CAMINO DEL MAR	01
Concrete Curb/Sidewalk Repair - 169 02ND AVE	02ND AVE	LAKE ST	01
Concrete Curb/Sidewalk Repair - 770 22ND AVE	22ND AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 5059 GEARY BLVD	GEARY BLVD	14TH AVE	01
Concrete Curb/Sidewalk Repair - 5059 GEARY BLVD	GEARY BLVD	14TH AVE	01
Concrete Curb/Sidewalk Repair - 778 43RD AVE	43RD AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 117 STANYAN BLVD	STANYAN BLVD	ANZA ST	01
Concrete Curb/Sidewalk Repair - 2521 MCALLISTER ST	MCALLISTER ST	PARKER AVE	01
Concrete Curb/Sidewalk Repair - 750 44TH AVE	44TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 500 39TH AVE	39TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 3700 CLEMENT ST	CLEMENT ST	38TH AVE	01
Concrete Curb/Sidewalk Repair - 3100 FULTON ST	FULTON ST	07TH AVE	01
Concrete Curb/Sidewalk Repair - 787 25TH AVE	25TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 1300 CABRILLO ST	CABRILLO ST	14TH AVE	01
Concrete Curb/Sidewalk Repair - 4455 GEARY BLVD	GEARY BLVD	08TH AVE	01
Concrete Curb/Sidewalk Repair - 719 30TH AVE	30TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 401 41ST AVE	41ST AVE	CLEMENT ST	01
Concrete Curb/Sidewalk Repair - 5500 GEARY BLVD	GEARY BLVD	19TH AVE	01
Concrete Curb/Sidewalk Repair - 4900 FULTON ST	FULTON ST	25TH AVE \ CROSSOVER DR	01
Concrete Curb/Sidewalk Repair - 606 36TH AVE	36TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 646 36TH AVE	36TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 4455 GEARY BLVD	GEARY BLVD	08TH AVE	01
Concrete Curb/Sidewalk Repair - 3829 GEARY BLVD	GEARY BLVD	02ND AVE	01
Concrete Curb/Sidewalk Repair - 2843 BALBOA ST	BALBOA ST	29TH AVE	01
Concrete Curb/Sidewalk Repair - 322 STANYAN ST	STANYAN ST	MCALLISTER ST	01
Concrete Curb/Sidewalk Repair - 219 STANYAN ST	STANYAN ST	STANYAN BLVD \ TURK BLVD	01
Concrete Curb/Sidewalk Repair - 863 ARGUELLO BLVD	ARGUELLO BLVD	MCALLISTER ST	01
Concrete Curb/Sidewalk Repair - 2545 TURK BLVD	TURK BLVD	TAMALPAIS TER	01
Concrete Curb/Sidewalk Repair - 2008 BALBOA ST	BALBOA ST	21ST AVE	01
Concrete Curb/Sidewalk Repair - 639 21ST AVE	21ST AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 201 ARGUELLO BLVD	ARGUELLO BLVD	LAKE ST	01
Concrete Curb/Sidewalk Repair - 588 34TH AVE	34TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 495 39TH AVE	39TH AVE	CLEMENT ST	01
Concrete Curb/Sidewalk Repair - 701 ANZA ST	ANZA ST	PARKER AVE	01
Concrete Curb/Sidewalk Repair - 641 48TH AVE	48TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 671 19TH AVE	19TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 300 16TH AVE	16TH AVE	CLEMENT ST	01

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 49

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 32 SUTRO HEIGHTS AVE	SUTRO HEIGHTS AVE	46TH AVE	01
Concrete Curb/Sidewalk Repair - 419 07TH AVE	07TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 614 FUNSTON AVE	FUNSTON AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 618 FUNSTON AVE	FUNSTON AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 654 FUNSTON AVE	FUNSTON AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 157 16TH AVE	16TH AVE	LAKE ST	01
Concrete Curb/Sidewalk Repair - 4350 GEARY BLVD	GEARY BLVD	07TH AVE	01
Concrete Curb/Sidewalk Repair - 2636 FULTON ST	FULTON ST	02ND AVE	01
Concrete Curb/Sidewalk Repair - 627 37TH AVE	37TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 631 37TH AVE	37TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 635 37TH AVE	37TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 4710 CABRILLO ST	CABRILLO ST	48TH AVE	01
Concrete Curb/Sidewalk Repair - 834 24TH AVE	24TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 599 CLEMENT ST	CLEMENT ST	06TH AVE	01
Concrete Curb/Sidewalk Repair - 4540 FULTON ST	FULTON ST	21ST AVE	01
Concrete Curb/Sidewalk Repair - 876 31ST AVE	31ST AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 771 30TH AVE	30TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 6555 GEARY BLVD	GEARY BLVD	29TH AVE	01
Concrete Curb/Sidewalk Repair - 4141 GEARY BLVD	GEARY BLVD	05TH AVE	01
Concrete Curb/Sidewalk Repair - 790 06TH AVE	06TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 495 39TH AVE	39TH AVE	CLEMENT ST	01
Concrete Curb/Sidewalk Repair - 2250 CLEMENT ST	CLEMENT ST	23RD AVE	01
Concrete Curb/Sidewalk Repair - 850 LA PLAYA	LA PLAYA	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 444 10TH AVE	10TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 305 CLEMENT ST	CLEMENT ST	04TH AVE	01
Concrete Curb/Sidewalk Repair -	FULTON ST	GREAT HWY	01
Concrete Curb/Sidewalk Repair - 409 10TH AVE	10TH AVE	GEARY BLVD	01
Concrete Curb/Sidewalk Repair - 701 ANZA ST	ANZA ST	PARKER AVE	01
Concrete Curb/Sidewalk Repair - 790 22ND AVE	22ND AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 701 11TH AVE	11TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 0000	FUNSTON AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 714 48TH AVE	48TH AVE	BALBOA ST	01
Concrete Curb/Sidewalk Repair - 608 44TH AVE	44TH AVE	ANZA ST	01
Concrete Curb/Sidewalk Repair - 738 09TH AVE	09TH AVE	CABRILLO ST	01
Concrete Curb/Sidewalk Repair - 4420 BALBOA ST	BALBOA ST	45TH AVE	01
Concrete Curb/Sidewalk Repair - 1738 LOMBARD ST	LOMBARD ST	OCTAVIA ST	02
Concrete Curb/Sidewalk Repair - 900 NORTH POINT ST	NORTH POINT ST	LARKIN ST	02
Concrete Curb/Sidewalk Repair - 503 EUCLID AVE	EUCLID AVE	PARKER AVE	02
Concrete Curb/Sidewalk Repair - 55 RETIRO WAY	RETIRO WAY	RICO WAY	02
Concrete Curb/Sidewalk Repair - 3572 PIERCE ST	PIERCE ST	CAPRA WAY	02
Concrete Curb/Sidewalk Repair - 37 CERVANTES BLVD	CERVANTES BLVD	ALHAMBRA ST	02
Concrete Curb/Sidewalk Repair - 3228 CLAY ST	CLAY ST	LYON ST	02
Concrete Curb/Sidewalk Repair - 35 CERVANTES BLVD	CERVANTES BLVD	ALHAMBRA ST	02
Concrete Curb/Sidewalk Repair - 890 MARINA BLVD	MARINA BLVD	LYON ST	02
Concrete Curb/Sidewalk Repair - 2701 JACKSON ST	JACKSON ST	SCOTT ST	02
Concrete Curb/Sidewalk Repair - 2251 GREEN ST	GREEN ST	FILLMORE ST	02
Concrete Curb/Sidewalk Repair - 2427 GREEN ST	GREEN ST	PIERCE ST	02
Concrete Curb/Sidewalk Repair - 66 CLEARY CT	CLEARY CT	GEARY BLVD	02
Concrete Curb/Sidewalk Repair - 2010 EDDY ST	EDDY ST	BRODERICK ST	02
Concrete Curb/Sidewalk Repair - 2887 GREEN ST	GREEN ST	BAKER ST	02
Concrete Curb/Sidewalk Repair - 1800 LOMBARD ST	LOMBARD ST	LAGUNA ST	02
Concrete Curb/Sidewalk Repair - 3460 GEARY BLVD	GEARY BLVD	STANYAN BLVD	02
Concrete Curb/Sidewalk Repair - 38 PALM AVE	PALM AVE	CALIFORNIA ST	02
Concrete Curb/Sidewalk Repair - 3500 GEARY BLVD	GEARY BLVD	JORDAN AVE	02
Concrete Curb/Sidewalk Repair - 2101 LOMBARD ST	LOMBARD ST	FILLMORE ST	02
Concrete Curb/Sidewalk Repair - 2599 SACRAMENTO ST	SACRAMENTO ST	FILLMORE ST	02
Concrete Curb/Sidewalk Repair - 2710 PINE ST	PINE ST	DIVISADERO ST	02
Concrete Curb/Sidewalk Repair - 1963 MCALLISTER ST	MCALLISTER ST	LYON ST	02

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 3731 FILLMORE ST	FILLMORE ST	BEACH ST	02
Concrete Curb/Sidewalk Repair - 1475 LOMBARD ST	LOMBARD ST	VAN NESS AVE	02
Concrete Curb/Sidewalk Repair - 2240 FRANCISCO ST	FRANCISCO ST	ALHAMBRA ST \ SCOTT ST	02
Concrete Curb/Sidewalk Repair - 250 CHERRY ST	CHERRY ST	WASHINGTON ST	02
Concrete Curb/Sidewalk Repair - 3201 OCTAVIA ST	OCTAVIA ST	CHESTNUT ST	02
Concrete Curb/Sidewalk Repair - 1836 MCALLISTER ST	MCALLISTER ST	BAKER ST	02
Concrete Curb/Sidewalk Repair - 2438 JACKSON ST	JACKSON ST	FILLMORE ST	02
Concrete Curb/Sidewalk Repair - 2956 BUSH ST	BUSH ST	LYON ST	02
Concrete Curb/Sidewalk Repair - 3141 JACKSON ST	JACKSON ST	LYON ST	02
Concrete Curb/Sidewalk Repair - 800 TURK ST	TURK ST	FRANKLIN ST	02
Concrete Curb/Sidewalk Repair - 2670 GEARY BLVD	GEARY BLVD	MASONIC AVE	02
Concrete Curb/Sidewalk Repair - 1940 BROADWAY	BROADWAY	OCTAVIA ST	02
Concrete Curb/Sidewalk Repair - 2820 BAKER ST	BAKER ST	FILBERT ST	02
Concrete Curb/Sidewalk Repair - 3447 CLAY ST	CLAY ST	WALNUT ST	02
Concrete Curb/Sidewalk Repair - 1 DANIEL BURNHAM CT	DANIEL BURNHAM CT	VAN NESS AVE	02
Concrete Curb/Sidewalk Repair - 2401 SACRAMENTO ST	SACRAMENTO ST	WEBSTER ST	02
Concrete Curb/Sidewalk Repair - 3650 GEARY BLVD	GEARY BLVD	PALM AVE	02
Concrete Curb/Sidewalk Repair - 3666 BAKER ST	BAKER ST	JEFFERSON ST	02
Concrete Curb/Sidewalk Repair - 1500 FRANKLIN ST	FRANKLIN ST	BUSH ST	02
Concrete Curb/Sidewalk Repair - 164 COLLINS ST	COLLINS ST	EUCLID AVE	02
Concrete Curb/Sidewalk Repair - 201 LAKE ST	LAKE ST	03RD AVE	02
Concrete Curb/Sidewalk Repair - 10 CAPRA WAY	CAPRA WAY	MALLORCA WAY	02
Concrete Curb/Sidewalk Repair - 3555 BRODERICK ST	BRODERICK ST	NORTH POINT ST	02
Concrete Curb/Sidewalk Repair - 1851 DIVISADERO ST	DIVISADERO ST	BUSH ST	02
Concrete Curb/Sidewalk Repair - 1812 DIVISADERO ST	DIVISADERO ST	BUSH ST	02
Concrete Curb/Sidewalk Repair - 900 BEACH ST	BEACH ST	POLK ST	02
Concrete Curb/Sidewalk Repair - 100 CAPRA WAY	CAPRA WAY	PIERCE ST	02
Concrete Curb/Sidewalk Repair - 478 EUCLID AVE	EUCLID AVE	SPRUCE ST	02
Concrete Curb/Sidewalk Repair - 2425 GEARY BLVD	GEARY BLVD	BAKER ST \ SAINT JOSEPHS AVE	02
Concrete Curb/Sidewalk Repair - 96 TOLEDO WAY	TOLEDO WAY	MALLORCA WAY	02
Concrete Curb/Sidewalk Repair - 2080 WASHINGTON ST	WASHINGTON ST	GOUGH ST	02
Concrete Curb/Sidewalk Repair - 1660 NORTH POINT ST	NORTH POINT ST	BUCHANAN ST	02
Concrete Curb/Sidewalk Repair - 1940 VALLEJO ST	VALLEJO ST	OCTAVIA ST	02
Concrete Curb/Sidewalk Repair - 2590 UNION ST	UNION ST	SCOTT ST	02
Concrete Curb/Sidewalk Repair - 2901 LYON ST	LYON ST	GREENWICH ST	02
Concrete Curb/Sidewalk Repair - 3600 JACKSON ST	JACKSON ST	SPRUCE ST	02
Concrete Curb/Sidewalk Repair - 251 RICHARDSON AVE	RICHARDSON AVE	FRANCISCO ST	02
Concrete Curb/Sidewalk Repair - 2200 SCOTT ST	SCOTT ST	CLAY ST	02
Concrete Curb/Sidewalk Repair - 1360 FRANKLIN ST	FRANKLIN ST	DANIEL BURNHAM CT	02
Concrete Curb/Sidewalk Repair - 257 29TH AVE	29TH AVE	LAKE ST	02
Concrete Curb/Sidewalk Repair - 2978 PINE ST	PINE ST	BAKER ST	02
Concrete Curb/Sidewalk Repair - 1028 LOMBARD ST	LOMBARD ST	LEAVENWORTH ST	02
Concrete Curb/Sidewalk Repair - 2358 LOMBARD ST	LOMBARD ST	PIERCE ST	02
Concrete Curb/Sidewalk Repair - 2140 SUTTER ST	SUTTER ST	STEINER ST	02
Concrete Curb/Sidewalk Repair - 2 MARINA BLVD	MARINA BLVD	LAGUNA ST	02
Concrete Curb/Sidewalk Repair - 1815 JACKSON ST	JACKSON ST	FRANKLIN ST	02
Concrete Curb/Sidewalk Repair - 7070 CALIFORNIA ST	CALIFORNIA ST	32ND AVE	02
Concrete Curb/Sidewalk Repair - 1995 CHESTNUT ST	CHESTNUT ST	WEBSTER ST	02
Concrete Curb/Sidewalk Repair - 1800 CHESTNUT ST	CHESTNUT ST	BUCHANAN ST	02
Concrete Curb/Sidewalk Repair - 201 ARGUELLO BLVD	ARGUELLO BLVD	LAKE ST	02
Concrete Curb/Sidewalk Repair - 1388 SUTTER ST	SUTTER ST	VAN NESS AVE	02
Concrete Curb/Sidewalk Repair - 3574 PIERCE ST	PIERCE ST	CAPRA WAY	02
Concrete Curb/Sidewalk Repair - 2901 SACRAMENTO ST	SACRAMENTO ST	DIVISADERO ST	02
Concrete Curb/Sidewalk Repair - 283 31ST AVE	31ST AVE	SEA VIEW TER	02
Concrete Curb/Sidewalk Repair - 3140 GEARY BLVD	GEARY BLVD	COOK ST	02
Concrete Curb/Sidewalk Repair - 1462 LAKE ST	LAKE ST	15TH AVE	02
Concrete Curb/Sidewalk Repair - 27 27TH AVE	27TH AVE	SEACLIFF AVE	02
Concrete Curb/Sidewalk Repair - 1898 UNION ST	UNION ST	OCTAVIA ST	02

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 2460 LARKIN ST	LARKIN ST	FILBERT ST	02
Concrete Curb/Sidewalk Repair - 1000 UNION ST	UNION ST	JONES ST	02
Concrete Curb/Sidewalk Repair - 3765 CALIFORNIA ST	CALIFORNIA ST	COMMONWEALTH AVE	02
Concrete Curb/Sidewalk Repair - 2490 GEARY BLVD	GEARY BLVD	BAKER ST \ SAINT JOSEPHS AVE	02
Concrete Curb/Sidewalk Repair - 2001 UNION ST	UNION ST	BUCHANAN ST	02
Concrete Curb/Sidewalk Repair - 40 VEGA ST	VEGA ST	ANZAVISTA AVE	02
Concrete Curb/Sidewalk Repair - 237 29TH AVE	29TH AVE	LAKE ST	02
Concrete Curb/Sidewalk Repair - 2350 GEARY BLVD	GEARY BLVD	BRODERICK ST	02
Concrete Curb/Sidewalk Repair - 2100 WASHINGTON ST	WASHINGTON ST	OCTAVIA ST	02
Concrete Curb/Sidewalk Repair - 1801 BEACH ST	BEACH ST	CERVANTES BLVD \ MALLORCA WAY	02
Concrete Curb/Sidewalk Repair - 101 CLAY ST	CLAY ST	DRUMM ST	03
Concrete Curb/Sidewalk Repair - 1600 STOCKTON ST	STOCKTON ST	UNION ST	03
Concrete Curb/Sidewalk Repair - 200 WASHINGTON ST	WASHINGTON ST	DAVIS ST	03
Concrete Curb/Sidewalk Repair - 890 JACKSON ST	JACKSON ST	ADELE CT	03
Concrete Curb/Sidewalk Repair - 458 JACKSON ST	JACKSON ST	BALANCE ST	03
Concrete Curb/Sidewalk Repair - 1 MARKET ST	MARKET ST	STEUART ST	03
Concrete Curb/Sidewalk Repair - 201 CLAY ST	CLAY ST	DAVIS ST	03
Concrete Curb/Sidewalk Repair - 7 VARENNES ST	VARENNES ST	GREEN ST	03
Concrete Curb/Sidewalk Repair - 1650 JACKSON ST	JACKSON ST	POLK ST	03
Concrete Curb/Sidewalk Repair - 45 KEARNY ST	KEARNY ST	MAIDEN LN	03
Concrete Curb/Sidewalk Repair - 500 GEARY ST	GEARY ST	TAYLOR ST	03
Concrete Curb/Sidewalk Repair - 115 SANSOME ST	SANSOME ST	BUSH ST	03
Concrete Curb/Sidewalk Repair - 1298 UNION ST	UNION ST	MOORE PL	03
Concrete Curb/Sidewalk Repair - 663 UNION ST	UNION ST	COLUMBUS AVE	03
Concrete Curb/Sidewalk Repair - 1165 KEARNY ST	KEARNY ST	FRESNO ST	03
Concrete Curb/Sidewalk Repair - 2323 HYDE ST	HYDE ST	LOMBARD ST	03
Concrete Curb/Sidewalk Repair - 2455 LEAVENWORTH ST	LEAVENWORTH ST	FRANCISCO ST	03
Concrete Curb/Sidewalk Repair - 850 COLUMBUS AVE	COLUMBUS AVE	MASON ST	03
Concrete Curb/Sidewalk Repair - 1200 BUSH ST	BUSH ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 222 FRONT ST	FRONT ST	CALIFORNIA ST	03
Concrete Curb/Sidewalk Repair - 1200 UNION ST	UNION ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 1227 MONTGOMERY ST	MONTGOMERY ST	GREEN ST	03
Concrete Curb/Sidewalk Repair - 1122 VAN NESS AVE	VAN NESS AVE	GEARY BLVD \ GEARY ST	03
Concrete Curb/Sidewalk Repair - 1560 POWELL ST	POWELL ST	VALLEJO ST	03
Concrete Curb/Sidewalk Repair - 366 COLUMBUS AVE	COLUMBUS AVE	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 155 PFEIFFER ST	PFEIFFER ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 1701 JACKSON ST	JACKSON ST	VAN NESS AVE	03
Concrete Curb/Sidewalk Repair - 2390 POWELL ST	POWELL ST	BAY ST	03
Concrete Curb/Sidewalk Repair - 1323 COLUMBUS AVE	COLUMBUS AVE	LEAVENWORTH ST	03
Concrete Curb/Sidewalk Repair - 19 MEDAU PL	MEDAU PL	FILBERT ST	03
Concrete Curb/Sidewalk Repair - 165 BERNARD ST	BERNARD ST	JONES ST	03
Concrete Curb/Sidewalk Repair - 1111 STOCKTON ST	STOCKTON ST	JACKSON ST	03
Concrete Curb/Sidewalk Repair - 480 SUTTER ST	SUTTER ST	STOCKTON ST \ STOCKTON TUNL	03
Concrete Curb/Sidewalk Repair - 1200 STOCKTON ST	STOCKTON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 50 BROADWAY		DAVIS ST	03
Concrete Curb/Sidewalk Repair - 301 VALLEJO ST	VALLEJO ST	SANSOME ST	03
Concrete Curb/Sidewalk Repair - 1005 HYDE ST	HYDE ST	PINE ST	03
Concrete Curb/Sidewalk Repair - 233 GREENWICH ST	GREENWICH ST	MONTGOMERY ST	03
Concrete Curb/Sidewalk Repair - 823 WASHINGTON ST	WASHINGTON ST	WAVERLY PL	03
Concrete Curb/Sidewalk Repair - 549 CHESTNUT ST	CHESTNUT ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 2155 POWELL ST	POWELL ST	CHESTNUT ST	03
Concrete Curb/Sidewalk Repair - 2015 HYDE ST	HYDE ST	HASTINGS TER	03
Concrete Curb/Sidewalk Repair - 800 GRANT AVE	GRANT AVE	CLAY ST	03
Concrete Curb/Sidewalk Repair - 750 GRANT AVE	GRANT AVE	COMMERCIAL ST	03
Concrete Curb/Sidewalk Repair - 1600 STOCKTON ST	STOCKTON ST	UNION ST	03
Concrete Curb/Sidewalk Repair - 996 PINE ST	PINE ST	VINE TER	03
Concrete Curb/Sidewalk Repair - 1201 STOCKTON ST	STOCKTON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 352 GRANT AVE	GRANT AVE	HARLAN PL	03

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 711 PACIFIC AVE	PACIFIC AVE	PELTON PL	03
Concrete Curb/Sidewalk Repair - 1001 GRANT AVE	GRANT AVE	JACKSON ST	03
Concrete Curb/Sidewalk Repair - 450 PACIFIC AVE	PACIFIC AVE	OSGOOD PL	03
Concrete Curb/Sidewalk Repair - 750 KEARNY ST	KEARNY ST	MERCHANT ST	03
Concrete Curb/Sidewalk Repair - 432 POWELL ST	POWELL ST	POST ST	03
Concrete Curb/Sidewalk Repair - 827 STOCKTON ST	STOCKTON ST	SACRAMENTO ST \ STOCKTON TUNL	03
Concrete Curb/Sidewalk Repair - 925 STOCKTON ST	STOCKTON ST	CLAY ST	03
Concrete Curb/Sidewalk Repair -	CALIFORNIA ST	VAN NESS AVE	03
Concrete Curb/Sidewalk Repair - 1500 CLAY ST	CLAY ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 2390 HYDE ST	HYDE ST	LOMBARD ST	03
Concrete Curb/Sidewalk Repair - 537 SACRAMENTO ST	SACRAMENTO ST	SANSOME ST	03
Concrete Curb/Sidewalk Repair - 2323 HYDE ST	HYDE ST	LOMBARD ST	03
Concrete Curb/Sidewalk Repair - 275 POST ST	POST ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 340 STOCKTON ST	STOCKTON ST	CAMPTON PL	03
Concrete Curb/Sidewalk Repair - 101 NORTH POINT ST	NORTH POINT ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 848 STOCKTON ST	STOCKTON ST	SACRAMENTO ST \ STOCKTON TUNL	03
Concrete Curb/Sidewalk Repair - 485 SACRAMENTO ST	SACRAMENTO ST	BATTERY ST	03
Concrete Curb/Sidewalk Repair - 50 CALIFORNIA ST	CALIFORNIA ST	DRUMM ST	03
Concrete Curb/Sidewalk Repair - 1556 TAYLOR ST	TAYLOR ST	BERNARD ST	03
Concrete Curb/Sidewalk Repair - 600 THE EMBARCADERO	THE EMBARCADERO	GREEN ST	03
Concrete Curb/Sidewalk Repair - 620 JONES ST	JONES ST	GEARY ST	03
Concrete Curb/Sidewalk Repair - 2262 MASON ST	MASON ST	WATER ST	03
Concrete Curb/Sidewalk Repair - 800 BUSH ST	BUSH ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 808 SUTTER ST	SUTTER ST	JONES ST	03
Concrete Curb/Sidewalk Repair - 265 UNION ST	UNION ST	CALHOUN TER	03
Concrete Curb/Sidewalk Repair - 1359 PINE ST	PINE ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 720 PACIFIC AVE	PACIFIC AVE	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 801 GRANT AVE	GRANT AVE	CLAY ST	03
Concrete Curb/Sidewalk Repair - 838 STOCKTON ST	STOCKTON ST	SACRAMENTO ST \ STOCKTON TUNL	03
Concrete Curb/Sidewalk Repair -	STOCKTON ST	STOCKTON TUNL \ SUTTER ST	03
Concrete Curb/Sidewalk Repair - 507 BUSH ST	BUSH ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 300 BAY ST	BAY ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 60 BROADWAY		DAVIS ST	03
Concrete Curb/Sidewalk Repair - 275 SACRAMENTO ST	SACRAMENTO ST	DAVIS ST	03
Concrete Curb/Sidewalk Repair - 57 POST ST	POST ST	LICK PL	03
Concrete Curb/Sidewalk Repair - 2168 MASON ST	MASON ST	LOMBARD ST	03
Concrete Curb/Sidewalk Repair - 840 TAYLOR ST	TAYLOR ST	MULFORD ALY	03
Concrete Curb/Sidewalk Repair - 1808 LARKIN ST	LARKIN ST	JACKSON ST	03
Concrete Curb/Sidewalk Repair - 123 OFARRELL ST	OFARRELL ST	STOCKTON ST	03
Concrete Curb/Sidewalk Repair - 498 JACKSON ST	JACKSON ST	HOTALING PL	03
Concrete Curb/Sidewalk Repair - 417 STOCKTON ST	STOCKTON ST	STOCKTON TUNL \ SUTTER ST	03
Concrete Curb/Sidewalk Repair - 200 POWELL ST	POWELL ST	OFARRELL ST	03
Concrete Curb/Sidewalk Repair - 200 KEARNY ST	KEARNY ST	SUTTER ST	03
Concrete Curb/Sidewalk Repair - 1201 STOCKTON ST	STOCKTON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 180 SUTTER ST	SUTTER ST	LICK PL	03
Concrete Curb/Sidewalk Repair - 50 BAY ST	BAY ST	KEARNY ST	03
Concrete Curb/Sidewalk Repair - 1100 SACRAMENTO ST	SACRAMENTO ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 200 POWELL ST	POWELL ST	OFARRELL ST	03
Concrete Curb/Sidewalk Repair - 301 GEARY ST	GEARY ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 990 VALLEJO ST	VALLEJO ST	ALTA VISTA TER	03
Concrete Curb/Sidewalk Repair - 760 FILBERT ST	FILBERT ST	COLUMBUS AVE \ VIA BUFANO	03
Concrete Curb/Sidewalk Repair - 1821 GRANT AVE	GRANT AVE	LOMBARD ST	03
Concrete Curb/Sidewalk Repair - 1570 STOCKTON ST	STOCKTON ST	COLUMBUS AVE \ GREEN ST	03
Concrete Curb/Sidewalk Repair - 32 LOMBARD ST	LOMBARD ST	BATTERY ST \ THE EMBARCADERO	03
Concrete Curb/Sidewalk Repair - 100 BUSH ST	BUSH ST	BATTERY ST	03
Concrete Curb/Sidewalk Repair - 1900 POLK ST	POLK ST	JACKSON ST	03
Concrete Curb/Sidewalk Repair - 450 POWELL ST	POWELL ST	POST ST	03
Concrete Curb/Sidewalk Repair - 1300 COLUMBUS AVE	COLUMBUS AVE	NORTH POINT ST	03

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 20 OFARRELL ST	OFARRELL ST	SECURITY PACIFIC PL	03
Concrete Curb/Sidewalk Repair - 225 BATTERY ST	BATTERY ST	CALIFORNIA ST	03
Concrete Curb/Sidewalk Repair - 1100 SACRAMENTO ST	SACRAMENTO ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 1122 POWELL ST	POWELL ST	WASHINGTON ST	03
Concrete Curb/Sidewalk Repair - 924 GRANT AVE	GRANT AVE	WASHINGTON ST	03
Concrete Curb/Sidewalk Repair - 301 GEARY ST	GEARY ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 1100 GRANT AVE	GRANT AVE	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 381 BUSH ST	BUSH ST	BELDEN ST	03
Concrete Curb/Sidewalk Repair - 1208 STOCKTON ST	STOCKTON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 895 PACIFIC AVE	PACIFIC AVE	TRENTON ST	03
Concrete Curb/Sidewalk Repair - 943 FILBERT ST	FILBERT ST	REDFIELD ALY	03
Concrete Curb/Sidewalk Repair - 659 COLUMBUS AVE	COLUMBUS AVE	POWELL ST	03
Concrete Curb/Sidewalk Repair - 52 CALIFORNIA ST	CALIFORNIA ST	DRUMM ST	03
Concrete Curb/Sidewalk Repair - 1706 HYDE ST	HYDE ST	BROADWAY	03
Concrete Curb/Sidewalk Repair - 279 COLUMBUS AVE	COLUMBUS AVE	JACK KEROUAC ALY \ SAROYAN PL	03
Concrete Curb/Sidewalk Repair -	LARKIN ST	ROCKLAND ST	03
Concrete Curb/Sidewalk Repair - 1200 STOCKTON ST	STOCKTON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 733 GRANT AVE	GRANT AVE	COMMERCIAL ST	03
Concrete Curb/Sidewalk Repair - 430 CALIFORNIA ST	CALIFORNIA ST	SANSOME ST	03
Concrete Curb/Sidewalk Repair - 670 DAVIS ST	DAVIS ST	DAVIS CT \ JACKSON ST	03
Concrete Curb/Sidewalk Repair -	CLAY ST	WALTER U LUM PL	03
Concrete Curb/Sidewalk Repair - 1400 BROADWAY	BROADWAY	LARKIN ST \ ROBERT C LEVY TUNL	03
Concrete Curb/Sidewalk Repair - 586 BUSH ST	BUSH ST	CHATHAM PL	03
Concrete Curb/Sidewalk Repair - 699 SUTTER ST	SUTTER ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 1800 HYDE ST	HYDE ST	VALLEJO ST	03
Concrete Curb/Sidewalk Repair - 1483 MASON ST	MASON ST	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 398 GEARY ST	GEARY ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 200 COLUMBUS AVE	COLUMBUS AVE	PACIFIC AVE	03
Concrete Curb/Sidewalk Repair - 380 BEACH ST	BEACH ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 1653 GRANT AVE	GRANT AVE	JACK MICHELINE ALY	03
Concrete Curb/Sidewalk Repair - 929 PINE ST	PINE ST	VINE TER	03
Concrete Curb/Sidewalk Repair - 240 FRONT ST	FRONT ST	HALLECK ST	03
Concrete Curb/Sidewalk Repair - 220 GEARY ST	GEARY ST	STOCKTON ST	03
Concrete Curb/Sidewalk Repair -	BROADWAY	KEARNY ST	03
Concrete Curb/Sidewalk Repair - 924 GRANT AVE	GRANT AVE	WASHINGTON ST	03
Concrete Curb/Sidewalk Repair - 852 STOCKTON ST	STOCKTON ST	SACRAMENTO ST \ STOCKTON TUNL	03
Concrete Curb/Sidewalk Repair - 1301 MASON ST	MASON ST	JACKSON ST	03
Concrete Curb/Sidewalk Repair - 1701 MASON ST	MASON ST	GREEN ST	03
Concrete Curb/Sidewalk Repair - 529 POWELL ST	POWELL ST	SUTTER ST	03
Concrete Curb/Sidewalk Repair - 8 MISSION ST	MISSION ST	THE EMBARCADERO	03
Concrete Curb/Sidewalk Repair - 420 TAYLOR ST	TAYLOR ST	OFARRELL ST	03
Concrete Curb/Sidewalk Repair - 80 ELLIS ST	ELLIS ST	04TH ST \ MARKET ST \ STOCKTON ST	03
Concrete Curb/Sidewalk Repair - 1221 JONES ST	JONES ST	SACRAMENTO ST	03
Concrete Curb/Sidewalk Repair - 1085 SUTTER ST	SUTTER ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 929 PINE ST	PINE ST	VINE TER	03
Concrete Curb/Sidewalk Repair - 698 POST ST	POST ST	OPHIR ALY	03
Concrete Curb/Sidewalk Repair - 186 FRANCISCO ST	FRANCISCO ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 1123 SUTTER ST	SUTTER ST	LARKIN ST	03
Concrete Curb/Sidewalk Repair - 1316 PINE ST	PINE ST	HYDE ST	03
Concrete Curb/Sidewalk Repair - 301 GEARY ST	GEARY ST	POWELL ST	03
Concrete Curb/Sidewalk Repair - 501 GREENWICH ST	GREENWICH ST	GRANT AVE	03
Concrete Curb/Sidewalk Repair - 400 CALIFORNIA ST	CALIFORNIA ST	SANSOME ST	03
Concrete Curb/Sidewalk Repair - 835 PACIFIC AVE	PACIFIC AVE	CORDELIA ST	03
Concrete Curb/Sidewalk Repair - 1299 CALIFORNIA ST	CALIFORNIA ST	JONES ST	03
Concrete Curb/Sidewalk Repair - 68 BAY ST	BAY ST	KEARNY ST	03
Concrete Curb/Sidewalk Repair - 1423 POWELL ST	POWELL ST	BROADWAY \ ROBERT C LEVY TUNL	03
Concrete Curb/Sidewalk Repair - 1118 POWELL ST	POWELL ST	WASHINGTON ST	03
Concrete Curb/Sidewalk Repair - 100 POWELL ST	POWELL ST	ELLIS ST	03

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1 POST ST	POST ST	MONTGOMERY ST	03
Concrete Curb/Sidewalk Repair - 565 GRANT AVE	GRANT AVE	VINTON CT	03
Concrete Curb/Sidewalk Repair - 495 GEARY ST	GEARY ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 44 MONTGOMERY ST	MONTGOMERY ST	POST ST	03
Concrete Curb/Sidewalk Repair - 693 SUTTER ST	SUTTER ST	MASON ST	03
Concrete Curb/Sidewalk Repair - 854 GRANT AVE	GRANT AVE	CLAY ST	03
Concrete Curb/Sidewalk Repair - 1101 SUTTER ST	SUTTER ST	LARKIN ST	03
Concrete Curb/Sidewalk Repair - 100 POWELL ST	POWELL ST	ELLIS ST	03
Concrete Curb/Sidewalk Repair - 1560 VAN NESS AVE	VAN NESS AVE	PINE ST	03
Concrete Curb/Sidewalk Repair - 460 BUSH ST	BUSH ST	MARK LN	03
Concrete Curb/Sidewalk Repair - 1 CALIFORNIA ST	CALIFORNIA ST	DRUMM ST	03
Concrete Curb/Sidewalk Repair - 1380 SLOAT BLVD	SLOAT BLVD	EL MIRASOL PL	04
Concrete Curb/Sidewalk Repair - 2626 38TH AVE	38TH AVE	VICENTE ST	04
Concrete Curb/Sidewalk Repair - 1317 37TH AVE	37TH AVE	IRVING ST	04
Concrete Curb/Sidewalk Repair - 1801 VICENTE ST	VICENTE ST	28TH AVE	04
Concrete Curb/Sidewalk Repair - 2372 22ND AVE	22ND AVE	SANTIAGO ST	04
Concrete Curb/Sidewalk Repair - 1733 19TH AVE	19TH AVE	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 1 CONSTANSO WAY	CONSTANSO WAY	CRESTLAKE DR	04
Concrete Curb/Sidewalk Repair - 1383 41ST AVE	41ST AVE	IRVING ST	04
Concrete Curb/Sidewalk Repair - 2200 46TH AVE	46TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 2667 47TH AVE	47TH AVE	CUTLER AVE	04
Concrete Curb/Sidewalk Repair - 1238 23RD AVE	23RD AVE	LINCOLN WAY	04
Concrete Curb/Sidewalk Repair - 2010 46TH AVE	46TH AVE	PACHECO ST	04
Concrete Curb/Sidewalk Repair - 850 VICENTE ST	VICENTE ST	19TH AVE	04
Concrete Curb/Sidewalk Repair -	LAKESHORE PLZ	SLOAT BLVD	04
Concrete Curb/Sidewalk Repair - 1825 21ST AVE	21ST AVE	NORIEGA ST	04
Concrete Curb/Sidewalk Repair - 2124 TARAVAL ST	TARAVAL ST	31ST AVE	04
Concrete Curb/Sidewalk Repair - 2075 21ST AVE	21ST AVE	PACHECO ST	04
Concrete Curb/Sidewalk Repair - 2435 46TH AVE	46TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 3246 JUDAH ST	JUDAH ST	37TH AVE	04
Concrete Curb/Sidewalk Repair - 4145 LAWTON ST	LAWTON ST	47TH AVE	04
Concrete Curb/Sidewalk Repair - 2671 21ST AVE	21ST AVE	VICENTE ST	04
Concrete Curb/Sidewalk Repair - 1300 QUINTARA ST	QUINTARA ST	22ND AVE	04
Concrete Curb/Sidewalk Repair - 1337 ORTEGA ST	ORTEGA ST	20TH AVE	04
Concrete Curb/Sidewalk Repair - 1474 40TH AVE	40TH AVE	JUDAH ST	04
Concrete Curb/Sidewalk Repair - 2701 SUNSET BLVD	SUNSET BLVD	WAWONA ST	04
Concrete Curb/Sidewalk Repair - 1238 28TH AVE	28TH AVE	LINCOLN WAY	04
Concrete Curb/Sidewalk Repair - 1763 23RD AVE	23RD AVE	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 2130 34TH AVE	34TH AVE	QUINTARA ST	04
Concrete Curb/Sidewalk Repair - 1830 MORAGA ST	MORAGA ST	24TH AVE	04
Concrete Curb/Sidewalk Repair - 1030 TARAVAL ST	TARAVAL ST	20TH AVE	04
Concrete Curb/Sidewalk Repair - 2900 21ST AVE	21ST AVE	SLOAT BLVD	04
Concrete Curb/Sidewalk Repair - 3427 IRVING ST	IRVING ST	35TH AVE	04
Concrete Curb/Sidewalk Repair - 2200 47TH AVE	47TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 171 LAKESHORE DR	LAKESHORE DR	COUNTRY CLUB DR	04
Concrete Curb/Sidewalk Repair - 601 EUCALYPTUS DR	EUCALYPTUS DR	MELBA AVE	04
Concrete Curb/Sidewalk Repair - 2278 46TH AVE	46TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 1206 47TH AVE	47TH AVE	LINCOLN WAY	04
Concrete Curb/Sidewalk Repair - 2040 GREAT HWY	GREAT HWY	PACHECO ST	04
Concrete Curb/Sidewalk Repair - 4641 LINCOLN WAY	LINCOLN WAY	47TH AVE	04
Concrete Curb/Sidewalk Repair - 1245 VICENTE ST	VICENTE ST	23RD AVE	04
Concrete Curb/Sidewalk Repair - 2500 25TH AVE	25TH AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 1351 31ST AVE	31ST AVE	IRVING ST	04
Concrete Curb/Sidewalk Repair - 1571 43RD AVE	43RD AVE	KIRKHAM ST	04
Concrete Curb/Sidewalk Repair - 1033 TARAVAL ST	TARAVAL ST	20TH AVE	04
Concrete Curb/Sidewalk Repair - 555 CRESTLAKE DR	CRESTLAKE DR	YORBA ST	04
Concrete Curb/Sidewalk Repair - 560 CRESTLAKE DR	CRESTLAKE DR	YORBA ST	04
Concrete Curb/Sidewalk Repair - 595 CRESTLAKE DR	CRESTLAKE DR	YORBA ST	04

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 2482 47TH AVE	47TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 2494 47TH AVE	47TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 1663 30TH AVE	30TH AVE	LAWTON ST	04
Concrete Curb/Sidewalk Repair - 1774 GREAT HWY	GREAT HWY	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 2520 22ND AVE	22ND AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 2526 22ND AVE	22ND AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 2540 22ND AVE	22ND AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 2546 22ND AVE	22ND AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 2570 22ND AVE	22ND AVE	ULLOA ST	04
Concrete Curb/Sidewalk Repair - 1444 TARAVAL ST	TARAVAL ST	24TH AVE	04
Concrete Curb/Sidewalk Repair - 1040 VICENTE ST	VICENTE ST	21ST AVE	04
Concrete Curb/Sidewalk Repair - 2200 46TH AVE	46TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 2243 24TH AVE	24TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 2255 24TH AVE	24TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 2401 24TH AVE	24TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 1900 SUNSET BLVD	SUNSET BLVD	ORTEGA ST	04
Concrete Curb/Sidewalk Repair - 1771 21ST AVE	21ST AVE	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 1530 VICENTE ST	VICENTE ST	26TH AVE	04
Concrete Curb/Sidewalk Repair - 2470 GREAT HWY	GREAT HWY	48TH AVE \ TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 1755 20TH AVE	20TH AVE	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 2195 28TH AVE	28TH AVE	QUINTARA ST	04
Concrete Curb/Sidewalk Repair - 2050 IRVING ST	IRVING ST	21ST AVE	04
Concrete Curb/Sidewalk Repair - 2430 29TH AVE	29TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 2214 NORIEGA ST	NORIEGA ST	29TH AVE	04
Concrete Curb/Sidewalk Repair - 1150 TARAVAL ST	TARAVAL ST	21ST AVE	04
Concrete Curb/Sidewalk Repair -	41ST AVE	MORAGA ST	04
Concrete Curb/Sidewalk Repair - 1392 GREAT HWY	GREAT HWY	IRVING ST	04
Concrete Curb/Sidewalk Repair - 1463 19TH AVE	19TH AVE	JUDAH ST	04
Concrete Curb/Sidewalk Repair - 1125 QUINTARA ST	QUINTARA ST	20TH AVE	04
Concrete Curb/Sidewalk Repair - 1135 QUINTARA ST	QUINTARA ST	20TH AVE	04
Concrete Curb/Sidewalk Repair - 1406 25TH AVE	25TH AVE	JUDAH ST	04
Concrete Curb/Sidewalk Repair - 2833 NORIEGA ST	NORIEGA ST	35TH AVE	04
Concrete Curb/Sidewalk Repair - 1883 19TH AVE	19TH AVE	NORIEGA ST	04
Concrete Curb/Sidewalk Repair - 2279 37TH AVE	37TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 1033 VICENTE ST	VICENTE ST	21ST AVE	04
Concrete Curb/Sidewalk Repair - 2254 31ST AVE	31ST AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 3010 NORIEGA ST	NORIEGA ST	37TH AVE	04
Concrete Curb/Sidewalk Repair - 3400 LAWTON ST	LAWTON ST	40TH AVE	04
Concrete Curb/Sidewalk Repair - 2267 27TH AVE	27TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 3645 SANTIAGO ST	SANTIAGO ST	47TH AVE	04
Concrete Curb/Sidewalk Repair - 2471 28TH AVE	28TH AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 3622 RIVERA ST	RIVERA ST	46TH AVE	04
Concrete Curb/Sidewalk Repair - 1271 38TH AVE	38TH AVE	LINCOLN WAY	04
Concrete Curb/Sidewalk Repair - 2700 40TH AVE	40TH AVE	WAWONA ST	04
Concrete Curb/Sidewalk Repair - 2458 33RD AVE	33RD AVE	TARAVAL ST	04
Concrete Curb/Sidewalk Repair - 2123 28TH AVE	28TH AVE	QUINTARA ST	04
Concrete Curb/Sidewalk Repair - 1201 36TH AVE	36TH AVE	LINCOLN WAY	04
Concrete Curb/Sidewalk Repair - 899 WAWONA ST	WAWONA ST	19TH AVE	04
Concrete Curb/Sidewalk Repair - 1210 ORTEGA ST	ORTEGA ST	19TH AVE	04
Concrete Curb/Sidewalk Repair - 2695 19TH AVE	19TH AVE	VICENTE ST	04
Concrete Curb/Sidewalk Repair - 2191 30TH AVE	30TH AVE	QUINTARA ST	04
Concrete Curb/Sidewalk Repair - 2286 25TH AVE	25TH AVE	RIVERA ST	04
Concrete Curb/Sidewalk Repair - 1200 TARAVAL ST	TARAVAL ST	22ND AVE	04
Concrete Curb/Sidewalk Repair - 2603 21ST AVE	21ST AVE	VICENTE ST	04
Concrete Curb/Sidewalk Repair -	GREAT HWY	JUDAH ST	04
Concrete Curb/Sidewalk Repair -	GREAT HWY	CUTLER AVE	04
Concrete Curb/Sidewalk Repair - 1 DR CARLTON B GOODLETT PL	DR CARLTON B GOODLETT PL	GROVE ST \ POLK ST	05
Concrete Curb/Sidewalk Repair - 900 VAN NESS AVE	VAN NESS AVE	ELLIS ST	05

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 330 ELLIS ST	ELLIS ST	TAYLOR ST	05
Concrete Curb/Sidewalk Repair - 455 GOLDEN GATE AVE	GOLDEN GATE AVE	LARKIN ST	05
Concrete Curb/Sidewalk Repair - 500 EDDY ST	EDDY ST	HYDE ST	05
Concrete Curb/Sidewalk Repair - 1101 GEARY BLVD	GEARY BLVD	GEARY ST \ VAN NESS AVE	05
Concrete Curb/Sidewalk Repair - 489 HAYES ST	HAYES ST	GOUGH ST	05
Concrete Curb/Sidewalk Repair - 793 DIVISADERO ST	DIVISADERO ST	GROVE ST	05
Concrete Curb/Sidewalk Repair - 17 CHARLES J BRENHAM PL	CHARLES J BRENHAM PL	07TH ST \ MARKET ST	05
Concrete Curb/Sidewalk Repair - 1700 ELLIS ST	ELLIS ST	STEINER ST	05
Concrete Curb/Sidewalk Repair - 1101 VAN NESS AVE	VAN NESS AVE	GEARY BLVD \ GEARY ST	05
Concrete Curb/Sidewalk Repair - 1700 ELLIS ST	ELLIS ST	STEINER ST	05
Concrete Curb/Sidewalk Repair - 155 FULTON ST	FULTON ST	HYDE ST \ UNITED NATIONS PLZ	05
Concrete Curb/Sidewalk Repair - 599 DIVISADERO ST	DIVISADERO ST	FELL ST	05
Concrete Curb/Sidewalk Repair - 1709 OAK ST	OAK ST	ASHBURY ST	05
Concrete Curb/Sidewalk Repair - 1235 FELL ST	FELL ST	DIVISADERO ST	05
Concrete Curb/Sidewalk Repair - 1626 HAYES ST	HAYES ST	LYON ST	05
Concrete Curb/Sidewalk Repair -	GROVE ST	SCOTT ST	05
Concrete Curb/Sidewalk Repair -	GROVE ST	STEINER ST	05
Concrete Curb/Sidewalk Repair - 500 STANYAN ST	STANYAN ST	HAYES ST	05
Concrete Curb/Sidewalk Repair - 2198 FELL ST	FELL ST	SHRADER ST	05
Concrete Curb/Sidewalk Repair - 300 LARKIN ST	LARKIN ST	MCALLISTER ST	05
Concrete Curb/Sidewalk Repair - 500 GROVE ST	GROVE ST	OCTAVIA ST	05
Concrete Curb/Sidewalk Repair - 1698 FELL ST	FELL ST	CENTRAL AVE	05
Concrete Curb/Sidewalk Repair - 835 OFARRELL ST	OFARRELL ST	LARKIN ST	05
Concrete Curb/Sidewalk Repair - 1825 POST ST	POST ST	WEBSTER ST	05
Concrete Curb/Sidewalk Repair - 1455 FILLMORE ST	FILLMORE ST	ELLIS ST	05
Concrete Curb/Sidewalk Repair - 664 LARKIN ST	LARKIN ST	WILLOW ST	05
Concrete Curb/Sidewalk Repair - 1101 LAGUNA ST		TURK ST	05
Concrete Curb/Sidewalk Repair - 1330 FILLMORE ST	FILLMORE ST	EDDY ST	05
Concrete Curb/Sidewalk Repair - 201 LINDEN ST	LINDEN ST	FRANKLIN ST	05
Concrete Curb/Sidewalk Repair - 498 HAYES ST	HAYES ST	GOUGH ST	05
Concrete Curb/Sidewalk Repair - 100 GROVE ST	GROVE ST	DR CARLTON B GOODLETT PL \ POLK ST	05
Concrete Curb/Sidewalk Repair - 940 HAYES ST	HAYES ST	FILLMORE ST	05
Concrete Curb/Sidewalk Repair - 1482 PAGE ST	PAGE ST	CENTRAL AVE	05
Concrete Curb/Sidewalk Repair - 135 BUCHANAN ST	BUCHANAN ST	HERMANN ST	05
Concrete Curb/Sidewalk Repair - 927 DIVISADERO ST	DIVISADERO ST	MCALLISTER ST	05
Concrete Curb/Sidewalk Repair - 861 DIVISADERO ST	DIVISADERO ST	FULTON ST	05
Concrete Curb/Sidewalk Repair - 1301 FILLMORE ST	FILLMORE ST	EDDY ST	05
Concrete Curb/Sidewalk Repair - 545 OAK ST	OAK ST	BUCHANAN ST	05
Concrete Curb/Sidewalk Repair - 666 ELLIS ST	ELLIS ST	HYDE ST	05
Concrete Curb/Sidewalk Repair - 1776 SUTTER ST	SUTTER ST	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 301 SCOTT ST	SCOTT ST	PAGE ST	05
Concrete Curb/Sidewalk Repair - 400 POLK ST	POLK ST	DR CARLTON B GOODLETT PL \ MCALLISTER ST	05
Concrete Curb/Sidewalk Repair - 1424 PAGE ST	PAGE ST	CENTRAL AVE	05
Concrete Curb/Sidewalk Repair - 142 CENTRAL AVE	CENTRAL AVE	HAIGHT ST	05
Concrete Curb/Sidewalk Repair - 1921 FILLMORE ST	FILLMORE ST	WILMOT ST	05
Concrete Curb/Sidewalk Repair - 146 CENTRAL AVE	CENTRAL AVE	HAIGHT ST	05
Concrete Curb/Sidewalk Repair - 1672 GROVE ST	GROVE ST	LYON ST	05
Concrete Curb/Sidewalk Repair - 450 OFARRELL ST	OFARRELL ST	SHANNON ST	05
Concrete Curb/Sidewalk Repair - 2000 ELLIS ST	ELLIS ST	DIVISADERO ST	05
Concrete Curb/Sidewalk Repair - 231 FRANKLIN ST	FRANKLIN ST	LINDEN ST	05
Concrete Curb/Sidewalk Repair - 301 VAN NESS AVE	VAN NESS AVE	GROVE ST	05
Concrete Curb/Sidewalk Repair - 1699 POST ST	POST ST	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 455 GOLDEN GATE AVE	GOLDEN GATE AVE	LARKIN ST	05
Concrete Curb/Sidewalk Repair - 1450 POST ST	POST ST	GOUGH ST	05
Concrete Curb/Sidewalk Repair - 320 OCTAVIA ST	OCTAVIA ST	OAK ST	05
Concrete Curb/Sidewalk Repair - 185 FRANKLIN ST	FRANKLIN ST	HICKORY ST	05
Concrete Curb/Sidewalk Repair - 628 ELLIS ST	ELLIS ST	HYDE ST	05

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1001 EDDY ST	EDDY ST	GOUGH ST	05
Concrete Curb/Sidewalk Repair - 101 GROVE ST	GROVE ST	DR CARLTON B GOODLETT PL \ POLK ST	05
Concrete Curb/Sidewalk Repair - 201 ELLIS ST	ELLIS ST	MASON ST	05
Concrete Curb/Sidewalk Repair - 57 TAYLOR ST	TAYLOR ST	06TH ST \ GOLDEN GATE AVE \ MARKET ST	05
Concrete Curb/Sidewalk Repair -	CHARLES J BRENHAM PL	07TH ST \ MARKET ST	05
Concrete Curb/Sidewalk Repair - 1114 MARKET ST	MARKET ST	JONES ST	05
Concrete Curb/Sidewalk Repair - 1640 STEINER ST	STEINER ST	GEARY BLVD	05
Concrete Curb/Sidewalk Repair - 500 LARKIN ST	LARKIN ST	TURK ST	05
Concrete Curb/Sidewalk Repair - 23 FRANKLIN ST	FRANKLIN ST	PAGE ST	05
Concrete Curb/Sidewalk Repair - 340 GROVE ST	GROVE ST	FRANKLIN ST	05
Concrete Curb/Sidewalk Repair - 490 FRANKLIN ST	FRANKLIN ST	FULTON ST	05
Concrete Curb/Sidewalk Repair - 200 MCALLISTER ST	MCALLISTER ST	HYDE ST	05
Concrete Curb/Sidewalk Repair - 450 IRVING ST	IRVING ST	05TH AVE	05
Concrete Curb/Sidewalk Repair - 1611 POST ST	POST ST	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 783 DIVISADERO ST	DIVISADERO ST	GROVE ST	05
Concrete Curb/Sidewalk Repair - 1545 DIVISADERO ST	DIVISADERO ST	GARDEN ST	05
Concrete Curb/Sidewalk Repair - 600 DIVISADERO ST	DIVISADERO ST	HAYES ST	05
Concrete Curb/Sidewalk Repair - 1640 STEINER ST	STEINER ST	GEARY BLVD	05
Concrete Curb/Sidewalk Repair - 501 OAK ST	OAK ST	BUCHANAN ST	05
Concrete Curb/Sidewalk Repair - 701 FILLMORE ST	FILLMORE ST	HAYES ST	05
Concrete Curb/Sidewalk Repair - 98 CLARENDON AVE	CLARENDON AVE	BIGLER AVE \ TWIN PEAKS BLVD	05
Concrete Curb/Sidewalk Repair - 1737 WEBSTER ST	WEBSTER ST	SUTTER ST	05
Concrete Curb/Sidewalk Repair -	GROVE ST	STEINER ST	05
Concrete Curb/Sidewalk Repair - 2050 BUCHANAN ST	BUCHANAN ST	PINE ST	05
Concrete Curb/Sidewalk Repair - 1720 GEARY BLVD	GEARY BLVD	WEBSTER ST	05
Concrete Curb/Sidewalk Repair - 1001 FRANKLIN ST	FRANKLIN ST	ELLIS ST	05
Concrete Curb/Sidewalk Repair - 4958 17TH ST	17TH ST	SHRADER ST	05
Concrete Curb/Sidewalk Repair - 1698 POST ST	POST ST	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 940 HAYES ST	HAYES ST	FILLMORE ST	05
Concrete Curb/Sidewalk Repair - 1701 FILLMORE ST	FILLMORE ST	POST ST	05
Concrete Curb/Sidewalk Repair - 1965 PAGE ST	PAGE ST	SHRADER ST	05
Concrete Curb/Sidewalk Repair - 500 FREDERICK ST	FREDERICK ST	STANYAN ST	05
Concrete Curb/Sidewalk Repair - 626 HAIGHT ST	HAIGHT ST	STEINER ST	05
Concrete Curb/Sidewalk Repair - 1720 GEARY BLVD	GEARY BLVD	WEBSTER ST	05
Concrete Curb/Sidewalk Repair - 610 IVY ST	IVY ST	BUCHANAN ST	05
Concrete Curb/Sidewalk Repair - 1420 TURK ST	TURK ST	FILLMORE ST	05
Concrete Curb/Sidewalk Repair - 360 GROVE ST	GROVE ST	FRANKLIN ST	05
Concrete Curb/Sidewalk Repair - 630 GOUGH ST	GOUGH ST	ASH ST	05
Concrete Curb/Sidewalk Repair - 1899 FILLMORE ST	FILLMORE ST	SUTTER ST	05
Concrete Curb/Sidewalk Repair - 1691 LAGUNA ST	LAGUNA ST	HEMLOCK ST	05
Concrete Curb/Sidewalk Repair - 1284 03RD AVE	03RD AVE	HUGO ST	05
Concrete Curb/Sidewalk Repair - 1795 POST ST	POST ST	BUCHANAN ST	05
Concrete Curb/Sidewalk Repair - 387 HAIGHT ST	HAIGHT ST	BUCHANAN ST	05
Concrete Curb/Sidewalk Repair - 890 FULTON ST	FULTON ST	FRIENDSHIP CT	05
Concrete Curb/Sidewalk Repair - 1223 WEBSTER ST	WEBSTER ST	EDDY ST	05
Concrete Curb/Sidewalk Repair - 1600 GEARY BLVD	GEARY BLVD	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 1425 IRVING ST	IRVING ST	15TH AVE	05
Concrete Curb/Sidewalk Repair - 1392 FUNSTON AVE	FUNSTON AVE	IRVING ST	05
Concrete Curb/Sidewalk Repair - 908 JUDAH ST	JUDAH ST	14TH AVE	05
Concrete Curb/Sidewalk Repair - 1301 FILLMORE ST	FILLMORE ST	EDDY ST	05
Concrete Curb/Sidewalk Repair - 1510 EDDY ST	EDDY ST	FILLMORE ST	05
Concrete Curb/Sidewalk Repair - 2238 GEARY BLVD	GEARY BLVD	DIVISADERO ST	05
Concrete Curb/Sidewalk Repair - 1111 GOUGH ST	GOUGH ST	ELLIS ST	05
Concrete Curb/Sidewalk Repair -	BRODERICK ST	TURK ST	05
Concrete Curb/Sidewalk Repair - 1590 GEARY BLVD	GEARY BLVD	LAGUNA ST	05
Concrete Curb/Sidewalk Repair - 251 OCTAVIA ST	OCTAVIA ST	LILY ST	05
Concrete Curb/Sidewalk Repair - 127 BUCHANAN ST	BUCHANAN ST	HERMANN ST	05
Concrete Curb/Sidewalk Repair - 1362 03RD AVE	03RD AVE	IRVING ST	05

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 37 CLEARY CT	CLEARY CT	GEARY BLVD	05
Concrete Curb/Sidewalk Repair - 145 IRVING ST	IRVING ST	02ND AVE	05
Concrete Curb/Sidewalk Repair - 503 DIVISADERO ST	DIVISADERO ST	FELL ST	05
Concrete Curb/Sidewalk Repair - 855 LINCOLN WAY	LINCOLN WAY	09TH AVE	05
Concrete Curb/Sidewalk Repair - 184 ROSE ST	ROSE ST	GOUGH ST	05
Concrete Curb/Sidewalk Repair - 756 IRVING ST	IRVING ST	08TH AVE	05
Concrete Curb/Sidewalk Repair - 1300 08TH AVE	08TH AVE	IRVING ST	05
Concrete Curb/Sidewalk Repair - 693 MISSION ST	MISSION ST	ANNIE ST	06
Concrete Curb/Sidewalk Repair - 49 SOUTH VAN NESS AVE	SOUTH VAN NESS AVE	MARKET ST \ VAN NESS AVE	06
Concrete Curb/Sidewalk Repair - 16 SHERMAN ST	SHERMAN ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 580 07TH ST	07TH ST	BRYANT ST	06
Concrete Curb/Sidewalk Repair - 75 ESSEX ST	ESSEX ST	LANSING ST	06
Concrete Curb/Sidewalk Repair - 165 08TH ST	08TH ST	MINNA ST	06
Concrete Curb/Sidewalk Repair - 895 HARRISON ST	HARRISON ST	04TH ST \ I-80 W ON RAMP	06
Concrete Curb/Sidewalk Repair - 41 HALLAM ST	HALLAM ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 1650 03RD ST	03RD ST	WARRIORS WAY	06
Concrete Curb/Sidewalk Repair - 689 03RD ST	03RD ST	BRANNAN ST	06
Concrete Curb/Sidewalk Repair - 316 06TH ST	06TH ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 1004 16TH ST	16TH ST	MISSOURI ST	06
Concrete Curb/Sidewalk Repair - 171 RHODE ISLAND ST	RHODE ISLAND ST	ALAMEDA ST	06
Concrete Curb/Sidewalk Repair - 690 MARKET ST	MARKET ST	GEARY ST	06
Concrete Curb/Sidewalk Repair - 1280 04TH ST	04TH ST	MISSION ROCK ST	06
Concrete Curb/Sidewalk Repair - 326 BRYANT ST	BRYANT ST	BEALE ST \ DELANCEY ST	06
Concrete Curb/Sidewalk Repair - 655 05TH ST	05TH ST	BLUXOME ST	06
Concrete Curb/Sidewalk Repair -	08TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair - 1298 MARKET ST	MARKET ST	08TH ST \ GROVE ST \ HYDE ST	06
Concrete Curb/Sidewalk Repair - 135 VERMONT ST	VERMONT ST	ALAMEDA ST	06
Concrete Curb/Sidewalk Repair - 1067 FOLSOM ST	FOLSOM ST	SHERMAN ST	06
Concrete Curb/Sidewalk Repair - 1390 MARKET ST	MARKET ST	09TH ST \ LARKIN ST	06
Concrete Curb/Sidewalk Repair - 1201 08TH ST	08TH ST	IRWIN ST \ WISCONSIN ST	06
Concrete Curb/Sidewalk Repair - 422 11TH ST	11TH ST	HARRISON ST	06
Concrete Curb/Sidewalk Repair - 1325 03RD ST	03RD ST	CHINA BASIN ST	06
Concrete Curb/Sidewalk Repair - 316 CLEMENTINA ST	CLEMENTINA ST	04TH ST	06
Concrete Curb/Sidewalk Repair - 808 BRANNAN ST	BRANNAN ST	07TH ST	06
Concrete Curb/Sidewalk Repair - 333 BRYANT ST	BRYANT ST	RINCON ST	06
Concrete Curb/Sidewalk Repair - 329 BRYANT ST	BRYANT ST	BEALE ST \ DELANCEY ST	06
Concrete Curb/Sidewalk Repair - 105 FREELON ST	FREELON ST	04TH ST	06
Concrete Curb/Sidewalk Repair - 1380 HOWARD ST	HOWARD ST	GRACE ST	06
Concrete Curb/Sidewalk Repair - 1 02ND ST	02ND ST	MARKET ST	06
Concrete Curb/Sidewalk Repair - 35 02ND ST	02ND ST	MARKET ST	06
Concrete Curb/Sidewalk Repair - 266 04TH ST	04TH ST	CLEMENTINA ST	06
Concrete Curb/Sidewalk Repair - 530 BRYANT ST	BRYANT ST	RITCH ST	06
Concrete Curb/Sidewalk Repair - 201 KING ST		03RD ST	06
Concrete Curb/Sidewalk Repair - 1435 FOLSOM ST	FOLSOM ST	10TH ST	06
Concrete Curb/Sidewalk Repair - 201 11TH ST	11TH ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 1101 MARKET ST	MARKET ST	07TH ST \ CHARLES J BRENNAM PL	06
Concrete Curb/Sidewalk Repair - 190 10TH ST	10TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair - 45 SOUTH PARK	SOUTH PARK	JACK LONDON ALY	06
Concrete Curb/Sidewalk Repair - 231 09TH ST	09TH ST	TEHAMA ST	06
Concrete Curb/Sidewalk Repair - 324 12TH ST	12TH ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 120 04TH ST	04TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 720 HOWARD ST	HOWARD ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 790 TEHAMA ST	TEHAMA ST	08TH ST	06
Concrete Curb/Sidewalk Repair - 81 LANSING ST	LANSING ST	GUY PL	06
Concrete Curb/Sidewalk Repair - 600 06TH ST	06TH ST	BRANNAN ST \ I-280 NORTHBOUND \ I-280 SOUTHBOUND	06
Concrete Curb/Sidewalk Repair - 33 FALMOUTH ST	FALMOUTH ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 1400 FOLSOM ST	FOLSOM ST	10TH ST	06

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 678 MISSION ST	MISSION ST	ANNIE ST	06
Concrete Curb/Sidewalk Repair - 1550 HOWARD ST	HOWARD ST	LAFAYETTE ST	06
Concrete Curb/Sidewalk Repair - 190 10TH ST	10TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair - 8 10TH ST	10TH ST	FELL ST \ MARKET ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 512 BRANNAN ST	BRANNAN ST	04TH ST	06
Concrete Curb/Sidewalk Repair - 1400 MISSION ST	MISSION ST	10TH ST	06
Concrete Curb/Sidewalk Repair -	08TH ST	BRYANT ST	06
Concrete Curb/Sidewalk Repair - 828 BRANNAN ST	BRANNAN ST	LANGTON ST	06
Concrete Curb/Sidewalk Repair - 625 MARKET ST	MARKET ST	02ND ST	06
Concrete Curb/Sidewalk Repair - 895 HARRISON ST	HARRISON ST	04TH ST \ I-80 W ON RAMP	06
Concrete Curb/Sidewalk Repair - 260 TOWNSEND ST	TOWNSEND ST	LUSK ST	06
Concrete Curb/Sidewalk Repair - 450 06TH ST	06TH ST	AHERN WAY	06
Concrete Curb/Sidewalk Repair - 388 BEALE ST	BEALE ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 1325 03RD ST	03RD ST	CHINA BASIN ST	06
Concrete Curb/Sidewalk Repair - 532 JESSIE ST	JESSIE ST	06TH ST	06
Concrete Curb/Sidewalk Repair - 303 02ND ST	02ND ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair -	BEALE ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 975 HOWARD ST	HOWARD ST	MARY ST	06
Concrete Curb/Sidewalk Repair - 171 GROVE ST	GROVE ST	DR CARLTON B GOODLETT PL \ POLK ST	06
Concrete Curb/Sidewalk Repair - 155 09TH ST	09TH ST	MINNA ST	06
Concrete Curb/Sidewalk Repair - 337 03RD ST	03RD ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 100 VAN NESS AVE	VAN NESS AVE	FELL ST	06
Concrete Curb/Sidewalk Repair - 162 LANGTON ST	LANGTON ST	DECKER ALY	06
Concrete Curb/Sidewalk Repair - 1023 MISSION ST	MISSION ST	06TH ST	06
Concrete Curb/Sidewalk Repair - 200 KING ST	KING ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 88 SPEAR ST	SPEAR ST	MARKET ST	06
Concrete Curb/Sidewalk Repair - 114 07TH ST	07TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 555 POLK ST	POLK ST	ELM ST	06
Concrete Curb/Sidewalk Repair - 1128 MARKET ST	MARKET ST	07TH ST \ CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 750 NATOMA ST	NATOMA ST	08TH ST	06
Concrete Curb/Sidewalk Repair - 201 MISSION ST	MISSION ST	MAIN ST	06
Concrete Curb/Sidewalk Repair - 451 06TH ST	06TH ST	AHERN WAY	06
Concrete Curb/Sidewalk Repair - 233 BEALE ST	BEALE ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 132 PERRY ST	PERRY ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 62 MOSS ST	MOSS ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 29 03RD ST	03RD ST	KEARNY ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 1200 MISSION ST	MISSION ST	08TH ST	06
Concrete Curb/Sidewalk Repair - 55 HAWTHORNE ST	HAWTHORNE ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 455 08TH ST	08TH ST	I-80 W OFF RAMP	06
Concrete Curb/Sidewalk Repair -	CHINA BASIN ST	TERRY A FRANCOIS BLVD	06
Concrete Curb/Sidewalk Repair - 14 ISIS ST	ISIS ST	12TH ST	06
Concrete Curb/Sidewalk Repair - 1144 MISSION ST	MISSION ST	07TH ST	06
Concrete Curb/Sidewalk Repair - 1550 HOWARD ST	HOWARD ST	LAFAYETTE ST	06
Concrete Curb/Sidewalk Repair - 33 GOUGH ST	GOUGH ST	MCCOPPIN ST \ OTIS ST	06
Concrete Curb/Sidewalk Repair - 39 JONES ST	JONES ST	MCALLISTER ST	06
Concrete Curb/Sidewalk Repair - 1200 MISSION ST	MISSION ST	08TH ST	06
Concrete Curb/Sidewalk Repair - 143 SOUTH VAN NESS AVE	SOUTH VAN NESS AVE	12TH ST	06
Concrete Curb/Sidewalk Repair - 450 10TH ST	10TH ST	HARRISON ST	06
Concrete Curb/Sidewalk Repair - 199 NEW MONTGOMERY ST		NATOMA ST	06
Concrete Curb/Sidewalk Repair - 175 06TH ST	06TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair - 230 HYDE ST	HYDE ST	TURK ST	06
Concrete Curb/Sidewalk Repair - 301 EDDY ST	EDDY ST	JONES ST	06
Concrete Curb/Sidewalk Repair - 380 ELLIS ST	ELLIS ST	TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 41 GROVE ST	GROVE ST	08TH ST \ HYDE ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 360 04TH ST	04TH ST	SHIPLEY ST	06
Concrete Curb/Sidewalk Repair -	HARRISON ST	MAIN ST	06
Concrete Curb/Sidewalk Repair - 1375 03RD ST	03RD ST	CHINA BASIN ST	06
Concrete Curb/Sidewalk Repair - 50 FREMONT ST	FREMONT ST	FRONT ST \ MARKET ST	06

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 350 MCALLISTER ST	MCALLISTER ST	LARKIN ST	06
Concrete Curb/Sidewalk Repair - 1407 MARKET ST	MARKET ST	10TH ST \ FELL ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 30 FELL ST	FELL ST	10TH ST \ MARKET ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 72 TOWNSEND ST	TOWNSEND ST	COLIN P KELLY JR ST	06
Concrete Curb/Sidewalk Repair - 1256 MARKET ST	MARKET ST	08TH ST \ GROVE ST \ HYDE ST	06
Concrete Curb/Sidewalk Repair - 1089 MISSION ST	MISSION ST	06TH ST	06
Concrete Curb/Sidewalk Repair - 1402 MARKET ST	MARKET ST	10TH ST \ FELL ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 1188 FOLSOM ST	FOLSOM ST	RODGERS ST	06
Concrete Curb/Sidewalk Repair - 25 JESSIE ST	JESSIE ST	ECKER ST	06
Concrete Curb/Sidewalk Repair - 600 16TH ST	16TH ST	04TH ST	06
Concrete Curb/Sidewalk Repair - 121 SPEAR ST		MISSION ST	06
Concrete Curb/Sidewalk Repair - 1001 HARRISON ST	HARRISON ST	06TH ST	06
Concrete Curb/Sidewalk Repair - 360 04TH ST	04TH ST	SHIPLEY ST	06
Concrete Curb/Sidewalk Repair - 260 KING ST	KING ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 351 ELLIS ST	ELLIS ST	TAYLOR ST	06
Concrete Curb/Sidewalk Repair -	11TH ST	KISSLING ST	06
Concrete Curb/Sidewalk Repair - 1411 MARKET ST	MARKET ST	10TH ST \ FELL ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 252 12TH ST	12TH ST	KISSLING ST	06
Concrete Curb/Sidewalk Repair - 753 MISSION ST	MISSION ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 260 08TH ST	08TH ST	TEHAMA ST	06
Concrete Curb/Sidewalk Repair - 199 GROVE ST	GROVE ST	DR CARLTON B GOODLETT PL \ POLK ST	06
Concrete Curb/Sidewalk Repair -	AHERN WAY	HARRIET ST	06
Concrete Curb/Sidewalk Repair - 160 SOUTH VAN NESS AVE	SOUTH VAN NESS AVE	12TH ST	06
Concrete Curb/Sidewalk Repair - 110 12TH ST	12TH ST	SOUTH VAN NESS AVE	06
Concrete Curb/Sidewalk Repair - 81 LANSING ST	LANSING ST	GUY PL	06
Concrete Curb/Sidewalk Repair - 94 TURK ST	TURK ST	MARKET ST \ MASON ST	06
Concrete Curb/Sidewalk Repair - 455 09TH ST	09TH ST	HARRISON ST	06
Concrete Curb/Sidewalk Repair - 36 VALENCIA ST	VALENCIA ST	MARKET ST	06
Concrete Curb/Sidewalk Repair - 777 HARRISON ST	HARRISON ST	LAPU-LAPU ST	06
Concrete Curb/Sidewalk Repair - 402 ELLIS ST	ELLIS ST	JONES ST	06
Concrete Curb/Sidewalk Repair - 405 TAYLOR ST	TAYLOR ST	OFARRELL ST	06
Concrete Curb/Sidewalk Repair - 405 TAYLOR ST	TAYLOR ST	OFARRELL ST	06
Concrete Curb/Sidewalk Repair - 301 MISSION ST	MISSION ST	BEALE ST	06
Concrete Curb/Sidewalk Repair - 70 04TH ST	04TH ST	JESSIE ST	06
Concrete Curb/Sidewalk Repair -	04TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 85 MCALLISTER ST	MCALLISTER ST	CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 180 HOWARD ST	HOWARD ST	SPEAR ST	06
Concrete Curb/Sidewalk Repair - 255 10TH ST	10TH ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 450 HARRISON ST	HARRISON ST	FREMONT ST \ I-80 W OFF RAMP	06
Concrete Curb/Sidewalk Repair - 650 DELANCEY ST	DELANCEY ST	BRANNAN ST	06
Concrete Curb/Sidewalk Repair - 1049 MARKET ST	MARKET ST	06TH ST \ GOLDEN GATE AVE \ TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 890 GEARY ST	GEARY ST	HYDE ST	06
Concrete Curb/Sidewalk Repair - 193 06TH ST	06TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair - 301 MISSION ST	MISSION ST	BEALE ST	06
Concrete Curb/Sidewalk Repair - 1468 FOLSOM ST	FOLSOM ST	JUNIPER ST	06
Concrete Curb/Sidewalk Repair - 450 10TH ST	10TH ST	HARRISON ST	06
Concrete Curb/Sidewalk Repair -	11TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 489 TERRY A FRANCOIS BLVD	TERRY A FRANCOIS BLVD	CHINA BASIN ST	06
Concrete Curb/Sidewalk Repair - 450 10TH ST	10TH ST	HARRISON ST	06
Concrete Curb/Sidewalk Repair - 300 TURK ST	TURK ST	LEAVENWORTH ST	06
Concrete Curb/Sidewalk Repair - 25 ESSEX ST	ESSEX ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 77 MCALLISTER ST	MCALLISTER ST	CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 87 MCALLISTER ST	MCALLISTER ST	CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 930 BRYANT ST	BRYANT ST	LANGTON ST	06
Concrete Curb/Sidewalk Repair - 151 ALICE B TOKLAS PL	ALICE B TOKLAS PL	MYRTLE ST \ POLK ST	06
Concrete Curb/Sidewalk Repair - 1450 FOLSOM ST	FOLSOM ST	JUNIPER ST	06
Concrete Curb/Sidewalk Repair - 118 02ND ST	02ND ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 120 11TH ST	11TH ST	MISSION ST	06

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 388 ELLIS ST	ELLIS ST	TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 1208 MARKET ST	MARKET ST	08TH ST \ GROVE ST \ HYDE ST	06
Concrete Curb/Sidewalk Repair - 121 07TH ST	07TH ST	MINNA ST	06
Concrete Curb/Sidewalk Repair - 360 04TH ST	04TH ST	SHIPLEY ST	06
Concrete Curb/Sidewalk Repair - 606 NATOMA ST	NATOMA ST	07TH ST	06
Concrete Curb/Sidewalk Repair - 810 HOWARD ST		04TH ST	06
Concrete Curb/Sidewalk Repair - 163 MAIN ST	MAIN ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 50 SOUTH VAN NESS AVE	SOUTH VAN NESS AVE	MARKET ST \ VAN NESS AVE	06
Concrete Curb/Sidewalk Repair - 149 BRANNAN ST	BRANNAN ST	THE EMBARCADERO	06
Concrete Curb/Sidewalk Repair - 564 04TH ST	04TH ST	WELSH ST	06
Concrete Curb/Sidewalk Repair - 465 STEVENSON ST	STEVENSON ST	05TH ST	06
Concrete Curb/Sidewalk Repair - 845 MARKET ST		04TH ST \ ELLIS ST \ STOCKTON ST	06
Concrete Curb/Sidewalk Repair - 1017 MARKET ST	MARKET ST	06TH ST \ GOLDEN GATE AVE \ TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 1450 03RD ST	03RD ST	MISSION BAY BLVD	06
Concrete Curb/Sidewalk Repair - 1700 04TH ST	04TH ST	CAMPUS WAY	06
Concrete Curb/Sidewalk Repair - 385 TAYLOR ST	TAYLOR ST	ELLIS ST	06
Concrete Curb/Sidewalk Repair - 33 08TH ST	08TH ST	GROVE ST \ HYDE ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 1095 MARKET ST	MARKET ST	06TH ST \ GOLDEN GATE AVE \ TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 81 05TH ST	05TH ST	JESSIE ST	06
Concrete Curb/Sidewalk Repair - 100 VAN NESS AVE	VAN NESS AVE	FELL ST	06
Concrete Curb/Sidewalk Repair - 70 04TH ST	04TH ST	JESSIE ST	06
Concrete Curb/Sidewalk Repair - 40 LEAVENWORTH ST	LEAVENWORTH ST	UNITED NATIONS PLZ	06
Concrete Curb/Sidewalk Repair - 260 08TH ST	08TH ST	TEHAMA ST	06
Concrete Curb/Sidewalk Repair - 52 GROVE ST	GROVE ST	LARKIN ST	06
Concrete Curb/Sidewalk Repair - 99 GROVE ST	GROVE ST	LARKIN ST	06
Concrete Curb/Sidewalk Repair - 701 LARKIN ST	LARKIN ST	ELLIS ST	06
Concrete Curb/Sidewalk Repair - 120 04TH ST	04TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 200 04TH ST	04TH ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 575 POLK ST	POLK ST	ELM ST	06
Concrete Curb/Sidewalk Repair - 300 TURK ST	TURK ST	LEAVENWORTH ST	06
Concrete Curb/Sidewalk Repair -	LEAVENWORTH ST	UNITED NATIONS PLZ	06
Concrete Curb/Sidewalk Repair -	01ST ST	BUSH ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 1067 MARKET ST	MARKET ST	06TH ST \ GOLDEN GATE AVE \ TAYLOR ST	06
Concrete Curb/Sidewalk Repair -	01ST ST	BUSH ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 500 TERRY A FRANCOIS BLVD	TERRY A FRANCOIS BLVD	MISSION BAY BLVD	06
Concrete Curb/Sidewalk Repair - 310 TOWNSEND ST	TOWNSEND ST	04TH ST	06
Concrete Curb/Sidewalk Repair - 40 LEAVENWORTH ST	LEAVENWORTH ST	UNITED NATIONS PLZ	06
Concrete Curb/Sidewalk Repair - 402 ELLIS ST	ELLIS ST	JONES ST	06
Concrete Curb/Sidewalk Repair - 190 07TH ST	07TH ST	NATOMA ST	06
Concrete Curb/Sidewalk Repair -	ESSEX ST	LANSING ST	06
Concrete Curb/Sidewalk Repair - 540 MISSION BAY BLVD	MISSION BAY BLVD NORTH	03RD ST	06
Concrete Curb/Sidewalk Repair - 680 08TH ST	08TH ST	BRANNAN ST	06
Concrete Curb/Sidewalk Repair -	11TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair -	04TH ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 901 MARKET ST	MARKET ST	05TH ST \ CYRIL MAGNIN ST	06
Concrete Curb/Sidewalk Repair - 790 HOWARD ST	HOWARD ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 69 DR CARLTON B GOODLETT PL	DR CARLTON B GOODLETT PL	GROVE ST \ POLK ST	06
Concrete Curb/Sidewalk Repair -	FOLSOM ST	HAWTHORNE ST	06
Concrete Curb/Sidewalk Repair - 1628 FOLSOM ST	FOLSOM ST	12TH ST	06
Concrete Curb/Sidewalk Repair - 783 MISSION ST	MISSION ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 85 MCALLISTER ST	MCALLISTER ST	CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 643 NATOMA ST	NATOMA ST	07TH ST	06
Concrete Curb/Sidewalk Repair - 1067 MARKET ST	MARKET ST	06TH ST \ GOLDEN GATE AVE \ TAYLOR ST	06
Concrete Curb/Sidewalk Repair - 1209 HOWARD ST	HOWARD ST	08TH ST	06
Concrete Curb/Sidewalk Repair - 120 11TH ST	11TH ST	MISSION ST	06
Concrete Curb/Sidewalk Repair - 1581 MISSION ST	MISSION ST	LAFAYETTE ST	06
Concrete Curb/Sidewalk Repair - 350 SPEAR ST	SPEAR ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 475 MARKET ST	MARKET ST	FREMONT ST \ FRONT ST	06

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 684 LARKIN ST	LARKIN ST	WILLOW ST	06
Concrete Curb/Sidewalk Repair - 1112 HARRISON ST	HARRISON ST	I-80 W ON RAMP	06
Concrete Curb/Sidewalk Repair - 1068 MISSION ST	MISSION ST	06TH ST	06
Concrete Curb/Sidewalk Repair - 241 JONES ST	JONES ST	TURK ST	06
Concrete Curb/Sidewalk Repair - 121 SPEAR ST		MISSION ST	06
Concrete Curb/Sidewalk Repair - 155 MAIN ST	MAIN ST	MISSION ST	06
Concrete Curb/Sidewalk Repair -	01ST ST	BUSH ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 235 MAIN ST	MAIN ST	HOWARD ST	06
Concrete Curb/Sidewalk Repair - 1106 MARKET ST	MARKET ST	JONES ST	06
Concrete Curb/Sidewalk Repair - 3 GROVE ST	GROVE ST	08TH ST \ HYDE ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 345 SPEAR ST	SPEAR ST	FOLSOM ST	06
Concrete Curb/Sidewalk Repair - 150 BERRY ST		03RD ST	06
Concrete Curb/Sidewalk Repair -	01ST ST	BUSH ST \ MARKET ST	06
Concrete Curb/Sidewalk Repair - 1690 FOLSOM ST	FOLSOM ST	12TH ST	06
Concrete Curb/Sidewalk Repair - 750 HOWARD ST	HOWARD ST	03RD ST	06
Concrete Curb/Sidewalk Repair - 87 MCALLISTER ST	MCALLISTER ST	CHARLES J BRENHAM PL	06
Concrete Curb/Sidewalk Repair - 630 08TH ST	08TH ST	BRANNAN ST	06
Concrete Curb/Sidewalk Repair - 901 GEARY ST	GEARY ST	LARKIN ST	06
Concrete Curb/Sidewalk Repair - 555 GEARY ST	GEARY ST	SHANNON ST	06
Concrete Curb/Sidewalk Repair - 100 VAN NESS AVE	VAN NESS AVE	FELL ST	06
Concrete Curb/Sidewalk Repair - 901 MISSION ST	MISSION ST	05TH ST	06
Concrete Curb/Sidewalk Repair -	HARRISON ST	MORRIS ST	06
Concrete Curb/Sidewalk Repair - 601 MARKET ST	MARKET ST	02ND ST	06
Concrete Curb/Sidewalk Repair - 1256 MARKET ST	MARKET ST	08TH ST \ GROVE ST \ HYDE ST	06
Concrete Curb/Sidewalk Repair - 1448 18TH AVE	18TH AVE	JUDAH ST	07
Concrete Curb/Sidewalk Repair - 170 SAINT ELMO WAY	SAINT ELMO WAY	EL VERANO WAY	07
Concrete Curb/Sidewalk Repair - 250 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	CLARENDON AVE	07
Concrete Curb/Sidewalk Repair - 390 SAN BENITO WAY	SAN BENITO WAY	UPLAND DR	07
Concrete Curb/Sidewalk Repair - 490 MAGELLAN AVE	MAGELLAN AVE	MONTALVO AVE	07
Concrete Curb/Sidewalk Repair - 100 FONT BLVD	FONT BLVD	CHUMASERO DR	07
Concrete Curb/Sidewalk Repair - 266 PACHECO ST	PACHECO ST	MARCELA AVE	07
Concrete Curb/Sidewalk Repair - 395 STAPLES AVE	STAPLES AVE	FOERSTER ST	07
Concrete Curb/Sidewalk Repair - 2433 OCEAN AVE	OCEAN AVE	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 264 COLON AVE	COLON AVE	MONTECITO AVE	07
Concrete Curb/Sidewalk Repair - 65 BUCKINGHAM WAY	BUCKINGHAM WAY	19TH AVE	07
Concrete Curb/Sidewalk Repair - 1485 16TH AVE	16TH AVE	JUDAH ST	07
Concrete Curb/Sidewalk Repair - 196 CASTENADA AVE	CASTENADA AVE	FOREST HILL PATH \ MAGELLAN AVE	07
Concrete Curb/Sidewalk Repair - 80 MARCELA AVE	MARCELA AVE	SOLA AVE	07
Concrete Curb/Sidewalk Repair - 75 MARCELA AVE	MARCELA AVE	SOLA AVE	07
Concrete Curb/Sidewalk Repair - 342 MIRAMAR AVE	MIRAMAR AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 733 MIRAMAR AVE	MIRAMAR AVE	EASTWOOD DR \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 739 MIRAMAR AVE	MIRAMAR AVE	EASTWOOD DR \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 365 CASITAS AVE	CASITAS AVE	BAXTER ALY \ CRESTA VISTA DR	07
Concrete Curb/Sidewalk Repair - 670 MIRAMAR AVE	MIRAMAR AVE	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 682 MIRAMAR AVE	MIRAMAR AVE	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 700 MIRAMAR AVE	MIRAMAR AVE	EASTWOOD DR \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 730 MIRAMAR AVE	MIRAMAR AVE	EASTWOOD DR \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 740 MIRAMAR AVE	MIRAMAR AVE	EASTWOOD DR \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 800 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 801 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 815 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 820 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 830 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 885 MIRAMAR AVE	MIRAMAR AVE	NORTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 959 MONTEREY BLVD	MONTEREY BLVD	PLYMOUTH AVE	07
Concrete Curb/Sidewalk Repair - 660 MIRAMAR AVE	MIRAMAR AVE	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 1035 MONTEREY BLVD	MONTEREY BLVD	FAXON AVE	07
Concrete Curb/Sidewalk Repair - 1145 MONTEREY BLVD	MONTEREY BLVD	SAINT ELMO WAY	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 35 AGUA WAY	AGUA WAY	TERESITA BLVD	07
Concrete Curb/Sidewalk Repair - 950 FAXON AVE	FAXON AVE	PIZARRO WAY	07
Concrete Curb/Sidewalk Repair - 1365 MONTEREY BLVD	MONTEREY BLVD	EL VERANO WAY \ NORTHGATE DR \ SAN FELIPE	07
Concrete Curb/Sidewalk Repair - 1375 MONTEREY BLVD	MONTEREY BLVD	EL VERANO WAY \ NORTHGATE DR \ SAN FELIPE	07
Concrete Curb/Sidewalk Repair - 49 MARCELA AVE	MARCELA AVE	SOLA AVE	07
Concrete Curb/Sidewalk Repair - 550 DEWEY BLVD	DEWEY BLVD	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 1800 OCEAN AVE	OCEAN AVE	DORADO TER \ JULES AVE	07
Concrete Curb/Sidewalk Repair - 489 JOOST AVE	JOOST AVE	DETROIT ST	07
Concrete Curb/Sidewalk Repair - 425 WEST PORTAL AVE	WEST PORTAL AVE	15TH AVE	07
Concrete Curb/Sidewalk Repair - 500 KIRKHAM ST	KIRKHAM ST	09TH AVE	07
Concrete Curb/Sidewalk Repair - 40 ENTRADA CT	ENTRADA CT	END	07
Concrete Curb/Sidewalk Repair - 44 ENTRADA CT	ENTRADA CT	END	07
Concrete Curb/Sidewalk Repair - 1 BEACHMONT DR	BEACHMONT DR	SLOAT BLVD	07
Concrete Curb/Sidewalk Repair - 2418 17TH AVE	17TH AVE	TARAVAL ST	07
Concrete Curb/Sidewalk Repair - 247 LANSDALE AVE	LANSDALE AVE	ROBINHOOD DR	07
Concrete Curb/Sidewalk Repair - 29 LOPEZ AVE	LOPEZ AVE	SOTELO AVE	07
Concrete Curb/Sidewalk Repair - 347 JUDAH ST	JUDAH ST	08TH AVE	07
Concrete Curb/Sidewalk Repair - 0801 OCEAN AVE	OCEAN AVE	HOWTH ST	07
Concrete Curb/Sidewalk Repair - 1575 07TH AVE	07TH AVE	KIRKHAM ST	07
Concrete Curb/Sidewalk Repair - 101 EDNA ST	EDNA ST	MARSTON AVE	07
Concrete Curb/Sidewalk Repair - 26 JUDAH ST	JUDAH ST	05TH AVE \ PARNASSUS AVE	07
Concrete Curb/Sidewalk Repair - 10 WESTWOOD DR	WESTWOOD DR	EASTWOOD DR \ MIRAMAR AVE	07
Concrete Curb/Sidewalk Repair - 33 SOTELO AVE	SOTELO AVE	SANTA RITA AVE	07
Concrete Curb/Sidewalk Repair - 369 WEST PORTAL AVE	WEST PORTAL AVE	14TH AVE	07
Concrete Curb/Sidewalk Repair - 109 LAWTON ST	LAWTON ST	07TH AVE \ WARREN DR	07
Concrete Curb/Sidewalk Repair - 31 CLAREMONT BLVD	CLAREMONT BLVD	DEWEY BLVD \ KENSINGTON WAY \ MONTALVO AVE \ TARAVAL ST	07
Concrete Curb/Sidewalk Repair - 78 EASTWOOD DR	EASTWOOD DR	SAN RAMON WAY	07
Concrete Curb/Sidewalk Repair - 1390 15TH AVE	15TH AVE	IRVING ST	07
Concrete Curb/Sidewalk Repair - 1065 MONTEREY BLVD	MONTEREY BLVD	FAXON AVE	07
Concrete Curb/Sidewalk Repair - 160 EASTWOOD DR	EASTWOOD DR	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 398 SAN LEANDRO WAY	SAN LEANDRO WAY	DARIEN WAY	07
Concrete Curb/Sidewalk Repair -	07TH AVE	JUDAH ST	07
Concrete Curb/Sidewalk Repair - 1330 MONTEREY BLVD	MONTEREY BLVD	EL VERANO WAY \ NORTHGATE DR \ SAN FELIPE	07
Concrete Curb/Sidewalk Repair - 888 MONTEREY BLVD	MONTEREY BLVD	HAZELWOOD AVE	07
Concrete Curb/Sidewalk Repair - 1100 MONTEREY BLVD	MONTEREY BLVD	SAINT ELMO WAY	07
Concrete Curb/Sidewalk Repair - 724 IRVING ST	IRVING ST	08TH AVE	07
Concrete Curb/Sidewalk Repair - 925 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	ROCKAWAY AVE \ ULLOA ST	07
Concrete Curb/Sidewalk Repair - 1387 05TH AVE	05TH AVE	IRVING ST	07
Concrete Curb/Sidewalk Repair - 1433 07TH AVE	07TH AVE	JUDAH ST	07
Concrete Curb/Sidewalk Repair - 242 WAWONA ST	WAWONA ST	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 478 HAZELWOOD AVE	HAZELWOOD AVE	GLOBE ALY \ LOS PALMOS DR	07
Concrete Curb/Sidewalk Repair - 1367 06TH AVE	06TH AVE	IRVING ST	07
Concrete Curb/Sidewalk Repair - 100 JUDAH ST	JUDAH ST	06TH AVE	07
Concrete Curb/Sidewalk Repair - 45 SAN ANSELMO AVE	SAN ANSELMO AVE	SAN BENITO WAY	07
Concrete Curb/Sidewalk Repair - 151 BADEN ST	BADEN ST	HEARST AVE	07
Concrete Curb/Sidewalk Repair - 2176 19TH AVE	19TH AVE	QUINTARA ST	07
Concrete Curb/Sidewalk Repair - 1430 MONTEREY BLVD	MONTEREY BLVD	EL VERANO WAY \ NORTHGATE DR \ SAN FELIPE	07
Concrete Curb/Sidewalk Repair - 21 SAN BENITO WAY	SAN BENITO WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 27 SAN BENITO WAY	SAN BENITO WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 701 BROTHERHOOD WAY	BROTHERHOOD WAY	JUNIPERO SERRA BLVD ON RAMP	07
Concrete Curb/Sidewalk Repair - 399 SAN FERNANDO WAY	SAN FERNANDO WAY	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 200 SAN BENITO WAY	SAN BENITO WAY	MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 1647 16TH AVE	16TH AVE	LAWTON ST	07
Concrete Curb/Sidewalk Repair - 266 SANTA PAULA AVE	SANTA PAULA AVE	SAN JACINTO WAY	07
Concrete Curb/Sidewalk Repair - 27 SOTELO AVE	SOTELO AVE	SANTA RITA AVE	07
Concrete Curb/Sidewalk Repair - 75 SANTA MONICA WAY	SANTA MONICA WAY	SAN LORENZO WAY	07
Concrete Curb/Sidewalk Repair - 100 SANTA PAULA AVE	SANTA PAULA AVE	SANTA MONICA WAY	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair -	PORTOLA DR	KENSINGTON WAY \ MIRALOMA DR	07
Concrete Curb/Sidewalk Repair -	SANTA CLARA AVE	TERRACE DR	07
Concrete Curb/Sidewalk Repair - 70 SANTA CLARA AVE	SANTA CLARA AVE	SANTA MONICA WAY \ YERBA BUENA AVE	07
Concrete Curb/Sidewalk Repair - 324 TARAVAL ST	TARAVAL ST	FUNSTON AVE	07
Concrete Curb/Sidewalk Repair - 185 EUCALYPTUS DR	EUCALYPTUS DR	GLADIOLUS LN	07
Concrete Curb/Sidewalk Repair - 801 GONZALEZ DR	GONZALEZ DR	RIVAS AVE	07
Concrete Curb/Sidewalk Repair - 151 OLYMPIA WAY	OLYMPIA WAY	DELLBROOK AVE	07
Concrete Curb/Sidewalk Repair - 172 DELLBROOK AVE	DELLBROOK AVE	OLYMPIA WAY	07
Concrete Curb/Sidewalk Repair - 200 DELLBROOK AVE	DELLBROOK AVE	STARVIEW WAY	07
Concrete Curb/Sidewalk Repair - 209 DELLBROOK AVE	DELLBROOK AVE	STARVIEW WAY	07
Concrete Curb/Sidewalk Repair - 29 DELLBROOK AVE	DELLBROOK AVE	OLYMPIA WAY	07
Concrete Curb/Sidewalk Repair - 111 DELLBROOK AVE	DELLBROOK AVE	OLYMPIA WAY	07
Concrete Curb/Sidewalk Repair - 147 DELLBROOK AVE	DELLBROOK AVE	OLYMPIA WAY	07
Concrete Curb/Sidewalk Repair - 125 MOUNTAIN SPRING AVE	MOUNTAIN SPRING AVE	STANYAN ST	07
Concrete Curb/Sidewalk Repair - 150 SANTA ANA AVE	SANTA ANA AVE	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 1601 MONTEREY BLVD	MONTEREY BLVD	SAN ANSELMO AVE \ SANTA CLARA AVE	07
Concrete Curb/Sidewalk Repair - 530 PARNASSUS AVE	PARNASSUS AVE	HILLWAY AVE	07
Concrete Curb/Sidewalk Repair - 800 ULLOA ST	ULLOA ST	CLAREMONT BLVD	07
Concrete Curb/Sidewalk Repair - 1201 05TH AVE	05TH AVE	LINCOLN WAY	07
Concrete Curb/Sidewalk Repair - 700 VICTORIA ST	VICTORIA ST	URBANO DR	07
Concrete Curb/Sidewalk Repair - 17 JUANITA WAY	JUANITA WAY	TERESITA BLVD	07
Concrete Curb/Sidewalk Repair - 288 EVELYN WAY	EVELYN WAY	TERESITA BLVD	07
Concrete Curb/Sidewalk Repair - 337 WEST PORTAL AVE	WEST PORTAL AVE	14TH AVE	07
Concrete Curb/Sidewalk Repair - 1700 OCEAN AVE	OCEAN AVE	FAXON AVE	07
Concrete Curb/Sidewalk Repair - 360 WEST PORTAL AVE	WEST PORTAL AVE	14TH AVE	07
Concrete Curb/Sidewalk Repair - 95 CRESTMONT DR	CRESTMONT DR	CHRISTOPHER DR \ GLENHAVEN LN	07
Concrete Curb/Sidewalk Repair - 15 MONTALVO AVE	MONTALVO AVE	CASTENADA AVE	07
Concrete Curb/Sidewalk Repair - 2522 OCEAN AVE	OCEAN AVE	JUNIPERO SERRA BLVD	07
Concrete Curb/Sidewalk Repair - 38 HEARST AVE	HEARST AVE	CIRCULAR AVE	07
Concrete Curb/Sidewalk Repair - 101 PINEHURST WAY	PINEHURST WAY	KENWOOD WAY	07
Concrete Curb/Sidewalk Repair - 39 FAIRFIELD WAY	FAIRFIELD WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 47 FAIRFIELD WAY	FAIRFIELD WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 52 FAIRFIELD WAY	FAIRFIELD WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 60 FAIRFIELD WAY	FAIRFIELD WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 67 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 29 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 55 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 73 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 1801 MONTEREY BLVD	MONTEREY BLVD	SANTA ANA AVE	07
Concrete Curb/Sidewalk Repair - 1661 17TH AVE	17TH AVE	LAWTON ST	07
Concrete Curb/Sidewalk Repair - 1900 18TH AVE	18TH AVE	ORTEGA ST	07
Concrete Curb/Sidewalk Repair - 85 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 91 LAKEWOOD AVE	LAKEWOOD AVE	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 160 WESTGATE DR	WESTGATE DR	KENWOOD WAY	07
Concrete Curb/Sidewalk Repair - 2274 16TH AVE	16TH AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair - 288 DENSLOWE DR	DENSLOWE DR	HOLLOWAY AVE	07
Concrete Curb/Sidewalk Repair - 15 WESTGATE DR	WESTGATE DR	CERRITOS AVE \ OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 135 MANOR DR	MANOR DR	FAIRFIELD WAY \ KENWOOD WAY	07
Concrete Curb/Sidewalk Repair - 190 APTOS AVE	APTOS AVE	UPLAND DR	07
Concrete Curb/Sidewalk Repair - 59 MANOR DR	MANOR DR	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 24 MANOR DR	MANOR DR	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 143 DALEWOOD WAY	DALEWOOD WAY	LANSDALE AVE \ MYRA WAY \ SHERWOOD CT	07
Concrete Curb/Sidewalk Repair - 157 DALEWOOD WAY	DALEWOOD WAY	LANSDALE AVE \ MYRA WAY \ SHERWOOD CT	07
Concrete Curb/Sidewalk Repair - 161 DALEWOOD WAY	DALEWOOD WAY	LANSDALE AVE \ MYRA WAY \ SHERWOOD CT	07
Concrete Curb/Sidewalk Repair - 165 DALEWOOD WAY	DALEWOOD WAY	LANSDALE AVE \ MYRA WAY \ SHERWOOD CT	07
Concrete Curb/Sidewalk Repair - 2234 17TH AVE	17TH AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair - 2650 15TH AVE	15TH AVE	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 39 PINEHURST WAY	PINEHURST WAY	OCEAN AVE	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 745 VICENTE ST	VICENTE ST	18TH AVE	07
Concrete Curb/Sidewalk Repair - 2634 15TH AVE	15TH AVE	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 2638 15TH AVE	15TH AVE	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 2642 15TH AVE	15TH AVE	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 320 WAWONA ST	WAWONA ST	14TH AVE	07
Concrete Curb/Sidewalk Repair - 154 PINEHURST WAY	PINEHURST WAY	KENWOOD WAY	07
Concrete Curb/Sidewalk Repair - 236 WEST PORTAL AVE	WEST PORTAL AVE	VICENTE ST	07
Concrete Curb/Sidewalk Repair - 70 PINEHURST WAY	PINEHURST WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 2 PINEHURST WAY	PINEHURST WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 55 PINEHURST WAY	PINEHURST WAY	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 96 MANOR DR	MANOR DR	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 245 KENWOOD WAY	KENWOOD WAY	KEYSTONE WAY	07
Concrete Curb/Sidewalk Repair - 650 UPLAND DR	UPLAND DR	APTOS AVE	07
Concrete Curb/Sidewalk Repair - 660 MIRAMAR AVE	MIRAMAR AVE	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 670 MIRAMAR AVE	MIRAMAR AVE	WILDWOOD WAY	07
Concrete Curb/Sidewalk Repair - 10 SAN ANDREAS WAY	SAN ANDREAS WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 1615 MONTEREY BLVD	MONTEREY BLVD	SAN ANSELMO AVE \ SANTA CLARA AVE	07
Concrete Curb/Sidewalk Repair - 127 WESTGATE DR	WESTGATE DR	KENWOOD WAY	07
Concrete Curb/Sidewalk Repair - 255 WESTGATE DR	WESTGATE DR	UPLAND DR	07
Concrete Curb/Sidewalk Repair - 30 EASTWOOD DR	EASTWOOD DR	MIRAMAR AVE \ WESTWOOD DR	07
Concrete Curb/Sidewalk Repair - 56 MERCED AVE	MERCED AVE	LAGUNA HONDA BLVD	07
Concrete Curb/Sidewalk Repair - 1845 MONTEREY BLVD	MONTEREY BLVD	SANTA ANA AVE	07
Concrete Curb/Sidewalk Repair - 1950 MONTEREY BLVD	MONTEREY BLVD	SAN LEANDRO WAY	07
Concrete Curb/Sidewalk Repair - 600 PORTOLA DR	PORTOLA DR	OSHAUGHNESSY BLVD \ WOODSIDE AVE	07
Concrete Curb/Sidewalk Repair -	SAN BUENAVENTURA WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 100 SAN BUENAVENTURA WAY	SAN BUENAVENTURA WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 130 SAN BUENAVENTURA WAY	SAN BUENAVENTURA WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 135 SAINT FRANCIS BLVD	SAINT FRANCIS BLVD	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 225 SANTA ANA AVE	SANTA ANA AVE	MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 115 SAN ALESO AVE	SAN ALESO AVE	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 169 SAN ALESO AVE	SAN ALESO AVE	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 1690 PORTOLA DR	PORTOLA DR	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 177 SAN ALESO AVE	SAN ALESO AVE	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 0251 SAN ANSELMO AVE	SAN ANSELMO AVE	SAN ANDREAS WAY	07
Concrete Curb/Sidewalk Repair - 110 SAN ALESO AVE	SAN ALESO AVE	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 130 SAN BENITO WAY	SAN BENITO WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 135 SAN BUENAVENTURA WAY	SAN BUENAVENTURA WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 165 SAN BUENAVENTURA WAY	SAN BUENAVENTURA WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 20 SAN BUENAVENTURA WAY	SAN BUENAVENTURA WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 25 SAN ANDREAS WAY	SAN ANDREAS WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 340 SAINT FRANCIS BLVD	SAINT FRANCIS BLVD	SANTA ANA AVE	07
Concrete Curb/Sidewalk Repair - 651 UPLAND DR	UPLAND DR	APTOS AVE	07
Concrete Curb/Sidewalk Repair - 1922 19TH AVE	19TH AVE	ORTEGA ST	07
Concrete Curb/Sidewalk Repair - 242 FLOOD AVE	FLOOD AVE	DETROIT ST	07
Concrete Curb/Sidewalk Repair - 141 JUNIPERO SERRA BLVD	JUNIPERO SERRA BLVD	MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 1470 MONTEREY BLVD	MONTEREY BLVD	SAN ALESO AVE	07
Concrete Curb/Sidewalk Repair - 201 SAN ANSELMO AVE	SAN ANSELMO AVE	SAN ANDREAS WAY	07
Concrete Curb/Sidewalk Repair - 2045 MONTEREY BLVD	MONTEREY BLVD	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 50 DARIEN WAY	DARIEN WAY	JUNIPERO SERRA BLVD	07
Concrete Curb/Sidewalk Repair - 557 CONGO ST	CONGO ST	MELROSE AVE	07
Concrete Curb/Sidewalk Repair - 95 JUNIPERO SERRA BLVD	JUNIPERO SERRA BLVD	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 17 SAN ANDREAS WAY	SAN ANDREAS WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 270 SAN ANSELMO AVE	SAN ANSELMO AVE	SAN BUENAVENTURA WAY	07
Concrete Curb/Sidewalk Repair - 45 SAN ANDREAS WAY	SAN ANDREAS WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 51 SAN ANDREAS WAY	SAN ANDREAS WAY	SAN ANSELMO AVE	07
Concrete Curb/Sidewalk Repair - 1567 18TH AVE	18TH AVE	KIRKHAM ST	07
Concrete Curb/Sidewalk Repair - 325 WARREN DR	WARREN DR	DEVONSHIRE WAY	07
Concrete Curb/Sidewalk Repair - 1535 IRVING ST	IRVING ST	16TH AVE	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 201 SAN BENITO WAY	SAN BENITO WAY	MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 1250 09TH AVE	09TH AVE	LINCOLN WAY	07
Concrete Curb/Sidewalk Repair - 2290 CECILIA AVE	CECILIA AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair - 198 MIRALOMA DR	MIRALOMA DR	BENGAL ALY	07
Concrete Curb/Sidewalk Repair - 55 SAN PABLO AVE	SAN PABLO AVE	SANTA MONICA WAY	07
Concrete Curb/Sidewalk Repair - 242 FLOOD AVE	FLOOD AVE	DETROIT ST	07
Concrete Curb/Sidewalk Repair - 100 DENSLOWE DR	DENSLOWE DR	WYTON LN	07
Concrete Curb/Sidewalk Repair - 109 ALTON AVE	ALTON AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 601 SAINT FRANCIS BLVD	SAINT FRANCIS BLVD	SAN BUENAVENTURA WAY	07
Concrete Curb/Sidewalk Repair -	FARVIEW CT	MARVIEW WAY	07
Concrete Curb/Sidewalk Repair - 1183 OCEAN AVE	OCEAN AVE	LEE AVE	07
Concrete Curb/Sidewalk Repair - 319 CASTENADA AVE	CASTENADA AVE	SAN MARCOS AVE	07
Concrete Curb/Sidewalk Repair - 1000 MONTEREY BLVD	MONTEREY BLVD	YERBA BUENA AVE	07
Concrete Curb/Sidewalk Repair - 101 CRESTA VISTA DR	CRESTA VISTA DR	GLOBE ALY	07
Concrete Curb/Sidewalk Repair - 35 AGUA WAY	AGUA WAY	TERESITA BLVD	07
Concrete Curb/Sidewalk Repair - 110 SYLVAN DR	SYLVAN DR	OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 121 SAN BENITO WAY	SAN BENITO WAY	SAINT FRANCIS BLVD	07
Concrete Curb/Sidewalk Repair - 262 SANTA PAULA AVE	SANTA PAULA AVE	TERRACE WALK \ YERBA BUENA AVE	07
Concrete Curb/Sidewalk Repair - 600 SAINT FRANCIS BLVD	SAINT FRANCIS BLVD	SAN BUENAVENTURA WAY	07
Concrete Curb/Sidewalk Repair - 140 ALTON AVE	ALTON AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 1650 PLYMOUTH AVE	PLYMOUTH AVE	MANGELS AVE	07
Concrete Curb/Sidewalk Repair - 245 FOWLER AVE	FOWLER AVE	JUANITA WAY	07
Concrete Curb/Sidewalk Repair - 501 ROCKDALE DR	ROCKDALE DR	OMAR WAY	07
Concrete Curb/Sidewalk Repair - 55 SAN PABLO AVE	SAN PABLO AVE	SANTA MONICA WAY	07
Concrete Curb/Sidewalk Repair - 944 MONTEREY BLVD	MONTEREY BLVD	COLON AVE	07
Concrete Curb/Sidewalk Repair - 1222 MORAGA ST	MORAGA ST	18TH AVE	07
Concrete Curb/Sidewalk Repair - 41 FOERSTER ST	FOERSTER ST	SUNNYSIDE TER	07
Concrete Curb/Sidewalk Repair - 626 TERESITA BLVD	TERESITA BLVD	MARIETTA DR \ MOLIMO DR	07
Concrete Curb/Sidewalk Repair -	SLOAT BLVD	SUNSET BLVD ON RAMP	07
Concrete Curb/Sidewalk Repair - 1745 SLOAT BLVD	SLOAT BLVD	34TH AVE \ CLEARFIELD DR	07
Concrete Curb/Sidewalk Repair - 41 LAGUNITAS DR	LAGUNITAS DR	CRANLEIGH DR	07
Concrete Curb/Sidewalk Repair - 41 SANTA RITA AVE	SANTA RITA AVE	SOTELO AVE	07
Concrete Curb/Sidewalk Repair - 2119 12TH AVE	12TH AVE	QUINTARA ST	07
Concrete Curb/Sidewalk Repair - 50 YERBA BUENA AVE	YERBA BUENA AVE	SANTA CLARA AVE \ SANTA MONICA WAY	07
Concrete Curb/Sidewalk Repair - 355 SERRANO DR	SERRANO DR	FONT BLVD	07
Concrete Curb/Sidewalk Repair - 39 BELLE AVE	BELLE AVE	NIANTIC AVE \ SAINT CHARLES AVE	07
Concrete Curb/Sidewalk Repair - 435 MAGELLAN AVE	MAGELLAN AVE	MONTALVO AVE	07
Concrete Curb/Sidewalk Repair - 2701 SLOAT BLVD	SLOAT BLVD	45TH AVE	07
Concrete Curb/Sidewalk Repair - 1600 FUNSTON AVE	FUNSTON AVE	LAWTON ST	07
Concrete Curb/Sidewalk Repair - 375 STAPLES AVE	STAPLES AVE	FOERSTER ST	07
Concrete Curb/Sidewalk Repair - 65 MERCED AVE	MERCED AVE	LAGUNA HONDA BLVD	07
Concrete Curb/Sidewalk Repair - 100 DORCAS WAY	DORCAS WAY	MOLIMO DR	07
Concrete Curb/Sidewalk Repair - 175 SAN FELIPE AVE	SAN FELIPE AVE	EL VERANO WAY \ MONTEREY BLVD \ NORTHGA	07
Concrete Curb/Sidewalk Repair - 260 LANSDALE AVE	LANSDALE AVE	ROBINHOOD DR	07
Concrete Curb/Sidewalk Repair - 801 PORTOLA DR	PORTOLA DR	EVELYN WAY	07
Concrete Curb/Sidewalk Repair - 270 LANSDALE AVE	LANSDALE AVE	ROBINHOOD DR	07
Concrete Curb/Sidewalk Repair - 299 SANTA PAULA AVE	SANTA PAULA AVE	TERRACE WALK \ YERBA BUENA AVE	07
Concrete Curb/Sidewalk Repair - 2200 09TH AVE	09TH AVE	MESA AVE	07
Concrete Curb/Sidewalk Repair - 2249 17TH AVE	17TH AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair -	JUNIPERO SERRA BLVD	ROSSMOOR DR	07
Concrete Curb/Sidewalk Repair - 10 VENTURA AVE	VENTURA AVE	LINARES AVE	07
Concrete Curb/Sidewalk Repair - 2233 CECILIA AVE	CECILIA AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair - 2701 SLOAT BLVD	SLOAT BLVD	45TH AVE	07
Concrete Curb/Sidewalk Repair - 30 CIRCULAR AVE	CIRCULAR AVE	I-280 N ON RAMP \ I-280 S OFF RAMP \ MONTE	07
Concrete Curb/Sidewalk Repair - 555 TARAVAL ST	TARAVAL ST	15TH AVE	07
Concrete Curb/Sidewalk Repair - 75 ROCKWOOD CT	ROCKWOOD CT	ROCKAWAY AVE	07
Concrete Curb/Sidewalk Repair - 0200 SAINT CHARLES AVE	SAINT CHARLES AVE	ALEMANY BLVD \ PALMETTO AVE	07
Concrete Curb/Sidewalk Repair - 2251 16TH AVE	16TH AVE	RIVERA ST	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 355 SERRANO DR	SERRANO DR	FONT BLVD	07
Concrete Curb/Sidewalk Repair - 2400 OCEAN AVE	OCEAN AVE	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 56 DENSLOWE DR	DENSLOWE DR	LYNDHURST DR	07
Concrete Curb/Sidewalk Repair - 369 MAGELLAN AVE	MAGELLAN AVE	DORANTES AVE \ PACHECO ST	07
Concrete Curb/Sidewalk Repair - 235 SAINT CHARLES AVE	SAINTE CHARLES AVE	ALEMANY BLVD \ PALMETTO AVE	07
Concrete Curb/Sidewalk Repair - 634 HEARST AVE	HEARST AVE	GENNESSEE ST	07
Concrete Curb/Sidewalk Repair - 1235 LAWTON ST	LAWTON ST	18TH AVE	07
Concrete Curb/Sidewalk Repair - 140 ALTON AVE	ALTON AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 120 ALTON AVE	ALTON AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 109 ALTON AVE	ALTON AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 66 SOTELO AVE	SOTELO AVE	UNNAMED 034	07
Concrete Curb/Sidewalk Repair - 451 YERBA BUENA AVE	YERBA BUENA AVE	PLYMOUTH AVE \ SAINT ELMO WAY	07
Concrete Curb/Sidewalk Repair - 300 BRENTWOOD AVE	BRENTWOOD AVE	FERNWOOD DR \ ROSEWOOD DR \ UNNAMED 0	07
Concrete Curb/Sidewalk Repair - 493 JOOST AVE	JOOST AVE	DETROIT ST	07
Concrete Curb/Sidewalk Repair - 643 TERESITA BLVD	TERESITA BLVD	MARIETTA DR \ MOLIMO DR	07
Concrete Curb/Sidewalk Repair - 2191 FUNSTON AVE	FUNSTON AVE	QUINTARA ST	07
Concrete Curb/Sidewalk Repair - 1441 11TH AVE	11TH AVE	JUDAH ST	07
Concrete Curb/Sidewalk Repair - 55 SANTA PAULA AVE	SANTA PAULA AVE	PORTOLA DR	07
Concrete Curb/Sidewalk Repair - 285 SAINT CHARLES AVE	SAINTE CHARLES AVE	ALEMANY BLVD \ PALMETTO AVE	07
Concrete Curb/Sidewalk Repair - 32 SOTELO AVE	SOTELO AVE	SANTA RITA AVE	07
Concrete Curb/Sidewalk Repair - 111 JOOST AVE	JOOST AVE	ACADIA ST	07
Concrete Curb/Sidewalk Repair - 11 YERBA BUENA AVE	YERBA BUENA AVE	SANTA CLARA AVE \ SANTA MONICA WAY	07
Concrete Curb/Sidewalk Repair - 55 SANTA CLARA AVE	SANTA CLARA AVE	SANTA MONICA WAY \ YERBA BUENA AVE	07
Concrete Curb/Sidewalk Repair - 2499 OCEAN AVE	OCEAN AVE	SAN FERNANDO WAY	07
Concrete Curb/Sidewalk Repair - 50 FOREST KNOLLS DR	FOREST KNOLLS DR	CHRISTOPHER DR	07
Concrete Curb/Sidewalk Repair -	FRIDA KAHLO WAY	GENEVA AVE \ OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 140 PACHECO ST	PACHECO ST	MAGELLAN AVE	07
Concrete Curb/Sidewalk Repair - 401 DETROIT ST	DETROIT ST	HEARST AVE	07
Concrete Curb/Sidewalk Repair - 354 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	PLAZA ST	07
Concrete Curb/Sidewalk Repair - 99 MERCED AVE	MERCED AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 15 MAGELLAN AVE	MAGELLAN AVE	CASTENADA AVE \ FOREST HILL PATH	07
Concrete Curb/Sidewalk Repair - 50 EVELYN WAY	EVELYN WAY	PORTOLA DR	07
Concrete Curb/Sidewalk Repair - 275 SANTA ANA AVE	SANTA ANA AVE	MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 191 SAN ANSELMO AVE	SAN ANSELMO AVE	SANTA PAULA AVE \ TERRACE WALK	07
Concrete Curb/Sidewalk Repair - 747 LAWTON ST	LAWTON ST	FUNSTON AVE	07
Concrete Curb/Sidewalk Repair - 56 DENSLOWE DR	DENSLOWE DR	LYNDHURST DR	07
Concrete Curb/Sidewalk Repair - 101 MERCED AVE	MERCED AVE	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 1209 CAPITOL AVE	CAPITOL AVE	DE MONTFORT AVE	07
Concrete Curb/Sidewalk Repair - 2130 09TH AVE	09TH AVE	SOTELO AVE	07
Concrete Curb/Sidewalk Repair - 745 RIVERA ST	RIVERA ST	17TH AVE	07
Concrete Curb/Sidewalk Repair - 431 VICENTE ST	VICENTE ST	15TH AVE	07
Concrete Curb/Sidewalk Repair - 2396 OCEAN AVE	OCEAN AVE	SAN LEANDRO WAY	07
Concrete Curb/Sidewalk Repair - 90 SANTA PAULA AVE	SANTA PAULA AVE	PORTOLA DR	07
Concrete Curb/Sidewalk Repair - 66 AERIAL WAY	AERIAL WAY	PACHECO ST	07
Concrete Curb/Sidewalk Repair - 38 SANTA RITA AVE	SANTA RITA AVE	SOTELO AVE	07
Concrete Curb/Sidewalk Repair -	OCEAN AVE	VICTORIA ST	07
Concrete Curb/Sidewalk Repair - 210 LANSDALE AVE	LANSDALE AVE	CASITAS AVE	07
Concrete Curb/Sidewalk Repair -	EUCALYPTUS DR	JUNIPERO SERRA BLVD \ OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 798 ULLOA ST	ULLOA ST	DORCHESTER WAY	07
Concrete Curb/Sidewalk Repair -	FRIDA KAHLO WAY	GENEVA AVE \ OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 111 DEVONSHIRE WAY	DEVONSHIRE WAY	OAK PARK DR	07
Concrete Curb/Sidewalk Repair - 2214 14TH AVE	14TH AVE	RIVERA ST	07
Concrete Curb/Sidewalk Repair - 375 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	PLAZA ST	07
Concrete Curb/Sidewalk Repair - 95 MONTEREY BLVD	MONTEREY BLVD	ACADIA ST	07
Concrete Curb/Sidewalk Repair - 445 MIRAMAR AVE	MIRAMAR AVE	SOUTHWOOD DR	07
Concrete Curb/Sidewalk Repair - 201 VICENTE ST	VICENTE ST	MADRONE AVE	07
Concrete Curb/Sidewalk Repair - 39 WESTWOOD DR	WESTWOOD DR	EASTWOOD DR \ MIRAMAR AVE	07
Concrete Curb/Sidewalk Repair - 75 SAN RAFAEL WAY	SAN RAFAEL WAY	SAINTE FRANCIS BLVD	07

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 124 SAINT CHARLES AVE	SAINT CHARLES AVE	PAYSON ST	07
Concrete Curb/Sidewalk Repair - 95 MONTEREY BLVD	MONTEREY BLVD	ACADIA ST	07
Concrete Curb/Sidewalk Repair - 39 WESTGATE DR	WESTGATE DR	CERRITOS AVE \ OCEAN AVE	07
Concrete Curb/Sidewalk Repair - 2193 09TH AVE	09TH AVE	MENDOSA AVE	07
Concrete Curb/Sidewalk Repair - 285 OLYMPIA WAY	OLYMPIA WAY	DELLBROOK AVE	07
Concrete Curb/Sidewalk Repair - 375 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	PLAZA ST	07
Concrete Curb/Sidewalk Repair - 401 PARNASSUS AVE	PARNASSUS AVE	HILLWAY AVE	07
Concrete Curb/Sidewalk Repair - 398 SAN LEANDRO WAY	SAN LEANDRO WAY	DARIEN WAY	07
Concrete Curb/Sidewalk Repair - 40 EVELYN WAY	EVELYN WAY	PORTOLA DR	07
Concrete Curb/Sidewalk Repair - 49 MARCELA AVE	MARCELA AVE	SOLA AVE	07
Concrete Curb/Sidewalk Repair - 24 YERBA BUENA AVE	YERBA BUENA AVE	SANTA CLARA AVE \ SANTA MONICA WAY	07
Concrete Curb/Sidewalk Repair - 375 LAGUNA HONDA BLVD	LAGUNA HONDA BLVD	PLAZA ST	07
Concrete Curb/Sidewalk Repair -	19TH AVE	LAWTON ST	07
Concrete Curb/Sidewalk Repair - 101 EDNA ST	EDNA ST	MARSTON AVE	07
Concrete Curb/Sidewalk Repair - 1441 OCEAN AVE	OCEAN AVE	GRANADA AVE	07
Concrete Curb/Sidewalk Repair - 30 CIRCULAR AVE	CIRCULAR AVE	I-280 N ON RAMP \ I-280 S OFF RAMP \ MONTEREY BLVD	07
Concrete Curb/Sidewalk Repair - 1 IDORA AVE	IDORA AVE	WOODSIDE AVE	07
Concrete Curb/Sidewalk Repair - 198 CHATTANOOGA ST	CHATTANOOGA ST	22ND ST	08
Concrete Curb/Sidewalk Repair - 2020 MARKET ST	MARKET ST	BUCHANAN ST \ DUBOCE AVE	08
Concrete Curb/Sidewalk Repair -	MARKET ST	DIAMOND ST	08
Concrete Curb/Sidewalk Repair - 512 14TH ST	14TH ST	GUERRERO ST	08
Concrete Curb/Sidewalk Repair - 422 28TH ST	28TH ST	NOE ST	08
Concrete Curb/Sidewalk Repair - 730 SAN JOSE AVE	SAN JOSE AVE	29TH ST	08
Concrete Curb/Sidewalk Repair - 3928 17TH ST	17TH ST	NOE ST	08
Concrete Curb/Sidewalk Repair - 860 DOLORES ST	DOLORES ST	21ST ST	08
Concrete Curb/Sidewalk Repair - 278 COLLINGWOOD ST	COLLINGWOOD ST	19TH ST	08
Concrete Curb/Sidewalk Repair - 91 MIGUEL ST	MIGUEL ST	BEACON ST	08
Concrete Curb/Sidewalk Repair - 118 DIAMOND ST	DIAMOND ST	18TH ST	08
Concrete Curb/Sidewalk Repair - 920 SANCHEZ ST	SANCHEZ ST	22ND ST	08
Concrete Curb/Sidewalk Repair - 94 MILTON ST	MILTON ST	GLEN CT	08
Concrete Curb/Sidewalk Repair - 847 DIAMOND ST	DIAMOND ST	24TH ST	08
Concrete Curb/Sidewalk Repair - 183 CHATTANOOGA ST	CHATTANOOGA ST	22ND ST	08
Concrete Curb/Sidewalk Repair - 41 SATURN ST	SATURN ST	LOWER TER	08
Concrete Curb/Sidewalk Repair - 3864 18TH ST	18TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 200 FAIR OAKS ST	FAIR OAKS ST	23RD ST	08
Concrete Curb/Sidewalk Repair - 459 BELVEDERE ST	BELVEDERE ST	GRATTAN ST	08
Concrete Curb/Sidewalk Repair - 588 JERSEY ST	JERSEY ST	DIAMOND ST	08
Concrete Curb/Sidewalk Repair - 4244 19TH ST	19TH ST	COLLINGWOOD ST	08
Concrete Curb/Sidewalk Repair - 599 CHENERY ST	CHENERY ST	ROANOKE ST	08
Concrete Curb/Sidewalk Repair - 204 CLINTON PARK	CLINTON PARK	GUERRERO ST	08
Concrete Curb/Sidewalk Repair - 242 SAN JOSE AVE	SAN JOSE AVE	24TH ST	08
Concrete Curb/Sidewalk Repair - 317 SAN JOSE AVE	SAN JOSE AVE	25TH ST	08
Concrete Curb/Sidewalk Repair - 318 SAN JOSE AVE	SAN JOSE AVE	25TH ST	08
Concrete Curb/Sidewalk Repair - 4301 CESAR CHAVEZ ST	CESAR CHAVEZ ST	DIAMOND ST	08
Concrete Curb/Sidewalk Repair - 3448 22ND ST	22ND ST	AMES ST	08
Concrete Curb/Sidewalk Repair - 808 STANYAN ST	STANYAN ST	BEULAH ST	08
Concrete Curb/Sidewalk Repair - 850 STANYAN ST	STANYAN ST	BEULAH ST	08
Concrete Curb/Sidewalk Repair - 3750 18TH ST	18TH ST	DOLORES ST	08
Concrete Curb/Sidewalk Repair - 0198 MANGELS AVE	MANGELS AVE	NORDHOFF ST	08
Concrete Curb/Sidewalk Repair - 1123 STANYAN ST	STANYAN ST	PARNASSUS AVE	08
Concrete Curb/Sidewalk Repair - 356 DAY ST	DAY ST	SANCHEZ ST	08
Concrete Curb/Sidewalk Repair - 1542 GUERRERO ST	GUERRERO ST	27TH ST	08
Concrete Curb/Sidewalk Repair - 180 FAIR OAKS ST	FAIR OAKS ST	22ND ST	08
Concrete Curb/Sidewalk Repair - 10 DIAMOND ST	DIAMOND ST	17TH ST	08
Concrete Curb/Sidewalk Repair - 3600 21ST ST	21ST ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 45 CASTRO ST	CASTRO ST	DUBOCE AVE	08
Concrete Curb/Sidewalk Repair - 1 SCOTT ST	SCOTT ST	DUBOCE AVE	08

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 345 DAY ST	DAY ST	SANCHEZ ST	08
Concrete Curb/Sidewalk Repair - 550 30TH ST	30TH ST	LAIDLEY ST	08
Concrete Curb/Sidewalk Repair - 136 JERSEY ST	JERSEY ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 666 NOE ST	NOE ST	19TH ST	08
Concrete Curb/Sidewalk Repair - 246 CHENERY ST	CHENERY ST	CHARLES ST	08
Concrete Curb/Sidewalk Repair - 2301 MARKET ST	MARKET ST	16TH ST \ NOE ST	08
Concrete Curb/Sidewalk Repair - 798 STANYAN ST	STANYAN ST	WALLER ST	08
Concrete Curb/Sidewalk Repair - 443 BURNETT AVE	BURNETT AVE	GARDENSIDE DR	08
Concrete Curb/Sidewalk Repair - 4660 19TH ST	19TH ST	CLOVER LN	08
Concrete Curb/Sidewalk Repair - 91 ALPINE TER	ALPINE TER	WALLER ST	08
Concrete Curb/Sidewalk Repair - 462 COLLINGWOOD ST	COLLINGWOOD ST	21ST ST	08
Concrete Curb/Sidewalk Repair - 445 BURNETT AVE	BURNETT AVE	GARDENSIDE DR	08
Concrete Curb/Sidewalk Repair - 243 CASELLI AVE	CASELLI AVE	DANVERS ST	08
Concrete Curb/Sidewalk Repair - 264 CASTRO ST	CASTRO ST	BEAVER ST	08
Concrete Curb/Sidewalk Repair - 3810 24TH ST	24TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 151 LIPPARD AVE	LIPPARD AVE	BOSWORTH ST	08
Concrete Curb/Sidewalk Repair - 3924 20TH ST	20TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 1069 14TH ST	14TH ST	ALPINE TER \ ROOSEVELT WAY	08
Concrete Curb/Sidewalk Repair - 3968 24TH ST	24TH ST	SANCHEZ ST	08
Concrete Curb/Sidewalk Repair - 500 DOLORES ST	DOLORES ST	18TH ST	08
Concrete Curb/Sidewalk Repair - 500 DOLORES ST	DOLORES ST	18TH ST	08
Concrete Curb/Sidewalk Repair - 400 SANCHEZ ST	SANCHEZ ST	17TH ST	08
Concrete Curb/Sidewalk Repair - 570 30TH ST	30TH ST	LAIDLEY ST	08
Concrete Curb/Sidewalk Repair - 226 GRAND VIEW AVE	GRAND VIEW AVE	ROMAIN ST	08
Concrete Curb/Sidewalk Repair -	GUERRERO ST	LAGUNA ST \ MARKET ST	08
Concrete Curb/Sidewalk Repair - 323 29TH ST	29TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 747 DUNCAN ST	DUNCAN ST	DIAMOND ST	08
Concrete Curb/Sidewalk Repair - 346 CASTRO ST	CASTRO ST	STATES ST	08
Concrete Curb/Sidewalk Repair - 3898 MARKET ST	MARKET ST	ARGENT ALY	08
Concrete Curb/Sidewalk Repair - 365 HILL ST	HILL ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 3601 21ST ST	21ST ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 4301 21ST ST	21ST ST	DOUGLASS ST \ ROMAIN ST	08
Concrete Curb/Sidewalk Repair - 830 ALVARADO ST	ALVARADO ST	DOUGLASS ST	08
Concrete Curb/Sidewalk Repair - 142 AMBER DR	AMBER DR	QUARTZ WAY	08
Concrete Curb/Sidewalk Repair - 3398 22ND ST	22ND ST	SAN JOSE AVE	08
Concrete Curb/Sidewalk Repair - 4339 CESAR CHAVEZ ST	CESAR CHAVEZ ST	DIAMOND ST	08
Concrete Curb/Sidewalk Repair - 220 DANVERS ST	DANVERS ST	CASELLI AVE	08
Concrete Curb/Sidewalk Repair - 3560 24TH ST	24TH ST	SAN JOSE AVE	08
Concrete Curb/Sidewalk Repair - 506 SANCHEZ ST	SANCHEZ ST	18TH ST	08
Concrete Curb/Sidewalk Repair - 88 CASTRO ST	CASTRO ST	DUBOCE AVE	08
Concrete Curb/Sidewalk Repair - 88 CASTRO ST	CASTRO ST	DUBOCE AVE	08
Concrete Curb/Sidewalk Repair - 3444 22ND ST	22ND ST	AMES ST	08
Concrete Curb/Sidewalk Repair - 49 LAPIDGE ST	LAPIDGE ST	18TH ST	08
Concrete Curb/Sidewalk Repair - 2700 DIAMOND ST	DIAMOND ST	SURREY ST	08
Concrete Curb/Sidewalk Repair - 673 SAN JOSE AVE	SAN JOSE AVE	28TH ST \ GUERRERO ST	08
Concrete Curb/Sidewalk Repair - 40 GRAND VIEW AVE	GRAND VIEW AVE	GRAND VIEW TER	08
Concrete Curb/Sidewalk Repair - 3962 20TH ST	20TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 299 DOLORES ST	DOLORES ST	ALERT ALY	08
Concrete Curb/Sidewalk Repair - 1010 14TH ST	14TH ST	CASTRO ST	08
Concrete Curb/Sidewalk Repair - 3898 MARKET ST	MARKET ST	ARGENT ALY	08
Concrete Curb/Sidewalk Repair - 1482 MASONIC AVE	MASONIC AVE	FREDERICK ST	08
Concrete Curb/Sidewalk Repair - 2086 MARKET ST	MARKET ST	RESERVOIR ST	08
Concrete Curb/Sidewalk Repair - 110 LIPPARD AVE	LIPPARD AVE	BOSWORTH ST	08
Concrete Curb/Sidewalk Repair - 254 CLINTON PARK	CLINTON PARK	GUERRERO ST	08
Concrete Curb/Sidewalk Repair - 104 MORELAND ST	MORELAND ST	FARNUM ST	08
Concrete Curb/Sidewalk Repair - 22 HOFFMAN AVE	HOFFMAN AVE	22ND ST	08
Concrete Curb/Sidewalk Repair - 307 30TH ST	30TH ST	CHURCH ST	08
Concrete Curb/Sidewalk Repair - 35 MILTON ST	MILTON ST	SAN JOSE AVE	08

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 3531 22ND ST	22ND ST	DOLORES ST	08
Concrete Curb/Sidewalk Repair - 3838 CESAR CHAVEZ ST	CESAR CHAVEZ ST	DOLORES ST	08
Concrete Curb/Sidewalk Repair - 94 MILTON ST	MILTON ST	GLEN CT	08
Concrete Curb/Sidewalk Repair - 3822 CESAR CHAVEZ ST	CESAR CHAVEZ ST	DOLORES ST	08
Concrete Curb/Sidewalk Repair - 4651 19TH ST	19TH ST	CLOVER LN	08
Concrete Curb/Sidewalk Repair - 88 CASTRO ST	CASTRO ST	DUBOCE AVE	08
Concrete Curb/Sidewalk Repair - 3141 16TH ST	16TH ST	ALBION ST	08
Concrete Curb/Sidewalk Repair - 39 DIAMOND ST	DIAMOND ST	MARKET ST	08
Concrete Curb/Sidewalk Repair - 396 CUMBERLAND ST		NOE ST	08
Concrete Curb/Sidewalk Repair -	14TH ST	MARKET ST	08
Concrete Curb/Sidewalk Repair - 3636 CESAR CHAVEZ ST	CESAR CHAVEZ ST	VALENCIA ST	08
Concrete Curb/Sidewalk Repair - 690 CHURCH ST	CHURCH ST	HANCOCK ST	08
Concrete Curb/Sidewalk Repair - 3550 CESAR CHAVEZ ST	CESAR CHAVEZ ST	VALENCIA ST	08
Concrete Curb/Sidewalk Repair - 4201 18TH ST	18TH ST	COLLINGWOOD ST	08
Concrete Curb/Sidewalk Repair - 251 CHURCH ST	CHURCH ST	MARKET ST	08
Concrete Curb/Sidewalk Repair - 61 NOE ST	NOE ST	DUBOCE AVE	08
Concrete Curb/Sidewalk Repair - 3450 16TH ST	16TH ST	SHARON ST	08
Concrete Curb/Sidewalk Repair - 502 ROOSEVELT WAY	ROOSEVELT WAY	LOWER TER	08
Concrete Curb/Sidewalk Repair - 300 PORTOLA DR	PORTOLA DR	BURNETT AVE \ DIAMOND HEIGHTS BLVD	08
Concrete Curb/Sidewalk Repair -	22ND ST	AMES ST	08
Concrete Curb/Sidewalk Repair - 630 CHENERY ST	CHENERY ST	CARRIE ST \ UNNAMED 026	08
Concrete Curb/Sidewalk Repair - 1652 DOLORES ST	DOLORES ST	DAY ST	08
Concrete Curb/Sidewalk Repair - 4144 18TH ST	18TH ST	CASTRO ST	08
Concrete Curb/Sidewalk Repair - 70 ELK ST	ELK ST	CHENERY ST	08
Concrete Curb/Sidewalk Repair - 3001 MARKET ST	MARKET ST	HATTIE ST	08
Concrete Curb/Sidewalk Repair - 351 BUENA VISTA AVE	BUENA VISTA AVE EAST	PARK HILL AVE	08
Concrete Curb/Sidewalk Repair - 70 ORD ST	ORD ST	SATURN ST	08
Concrete Curb/Sidewalk Repair - 70 ORD ST	ORD ST	SATURN ST	08
Concrete Curb/Sidewalk Repair - 1514 SANCHEZ ST	SANCHEZ ST	28TH ST	08
Concrete Curb/Sidewalk Repair - 61 WHITNEY ST	WHITNEY ST	30TH ST	08
Concrete Curb/Sidewalk Repair - 291 SURREY ST	SURREY ST	VAN BUREN ST	08
Concrete Curb/Sidewalk Repair - 695 GRAND VIEW AVE	GRAND VIEW AVE	24TH ST	08
Concrete Curb/Sidewalk Repair - 87 DOLORES ST	DOLORES ST	CLINTON PARK	08
Concrete Curb/Sidewalk Repair - 336 SANCHEZ ST	SANCHEZ ST	16TH ST	08
Concrete Curb/Sidewalk Repair - 465 COLLINGWOOD ST	COLLINGWOOD ST	21ST ST	08
Concrete Curb/Sidewalk Repair - 555 PORTOLA DR	PORTOLA DR	TWIN PEAKS BLVD	08
Concrete Curb/Sidewalk Repair - 274 DOLORES ST	DOLORES ST	ALERT ALY	08
Concrete Curb/Sidewalk Repair - 430 PORTOLA DR	PORTOLA DR	GLENVIEW DR	08
Concrete Curb/Sidewalk Repair - 230 DOLORES ST	DOLORES ST	ALERT ALY	08
Concrete Curb/Sidewalk Repair - 66 STATES ST	STATES ST	CASTRO ST	08
Concrete Curb/Sidewalk Repair - 139 LAIDLEY ST	LAIDLEY ST	HARPER ST	08
Concrete Curb/Sidewalk Repair - 1 CUVIER ST	CUVIER ST	END	08
Concrete Curb/Sidewalk Repair - 691 CHENERY ST	CHENERY ST	CARRIE ST \ UNNAMED 026	08
Concrete Curb/Sidewalk Repair - 430 PORTOLA DR	PORTOLA DR	GLENVIEW DR	08
Concrete Curb/Sidewalk Repair - 1198 VALENCIA ST	VALENCIA ST	22ND ST	08
Concrete Curb/Sidewalk Repair - 407 MIGUEL ST	MIGUEL ST	ARLINGTON ST	08
Concrete Curb/Sidewalk Repair - 359 CLIPPER ST	CLIPPER ST	NOE ST	08
Concrete Curb/Sidewalk Repair - 4193 26TH ST	26TH ST	NOE ST	08
Concrete Curb/Sidewalk Repair -	CESAR CHAVEZ ST	DOUGLASS ST	08
Concrete Curb/Sidewalk Repair -	BOSWORTH ST	CONGO ST \ ELK ST	08
Concrete Curb/Sidewalk Repair - 701 SANCHEZ ST	SANCHEZ ST	20TH ST	08
Concrete Curb/Sidewalk Repair - 99 ORD ST	ORD ST	SATURN ST	08
Concrete Curb/Sidewalk Repair - 380 VALLEY ST	VALLEY ST	SANCHEZ ST	08
Concrete Curb/Sidewalk Repair - 3496 22ND ST	22ND ST	QUANE ST	08
Concrete Curb/Sidewalk Repair - 442 SANCHEZ ST	SANCHEZ ST	17TH ST	08
Concrete Curb/Sidewalk Repair - 683 14TH ST	14TH ST	LANDERS ST	08
Concrete Curb/Sidewalk Repair - 300 VALENCIA ST		14TH ST	08
Concrete Curb/Sidewalk Repair -	NATICK ST	CHENERY ST	08

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 71

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 72 SATURN ST	SATURN ST	LOWER TER	08
Concrete Curb/Sidewalk Repair - 64 DEARBORN ST	DEARBORN ST	17TH ST	09
Concrete Curb/Sidewalk Repair - 3145 CESAR CHAVEZ ST	CESAR CHAVEZ ST	HARRISON ST	09
Concrete Curb/Sidewalk Repair - 87 29TH ST	29TH ST	TIFFANY AVE	09
Concrete Curb/Sidewalk Repair - 675 VALENCIA ST	VALENCIA ST	SYCAMORE ST	09
Concrete Curb/Sidewalk Repair - 430 SHOTWELL ST	SHOTWELL ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 438 SHOTWELL ST	SHOTWELL ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 120 ELSIE ST	ELSIE ST	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 255 SAN CARLOS ST	SAN CARLOS ST	19TH ST	09
Concrete Curb/Sidewalk Repair - 211 NEVADA ST	NEVADA ST	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 1941 MISSION ST	MISSION ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 154 TIFFANY AVE	TIFFANY AVE	DUNCAN ST	09
Concrete Curb/Sidewalk Repair - 585 ANDOVER ST	ANDOVER ST	PARK ST	09
Concrete Curb/Sidewalk Repair - 180 SAN CARLOS ST	SAN CARLOS ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 790 GIRARD ST	GIRARD ST	DWIGHT ST	09
Concrete Curb/Sidewalk Repair - 270 NEVADA ST	NEVADA ST	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 36 GLADYS ST	GLADYS ST	SANTA MARINA ST	09
Concrete Curb/Sidewalk Repair - 1985 MISSION ST	MISSION ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 325 HIGHLAND AVE	HIGHLAND AVE	HOLLY PARK CIR	09
Concrete Curb/Sidewalk Repair - 745 CORTLAND AVE	CORTLAND AVE	ANDERSON ST	09
Concrete Curb/Sidewalk Repair - 2988 MISSION ST	MISSION ST	25TH ST	09
Concrete Curb/Sidewalk Repair - 314 WOOLSEY ST	WOOLSEY ST	BRUSSELS ST	09
Concrete Curb/Sidewalk Repair - 1220 VALENCIA ST	VALENCIA ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 995 GUERRERO ST	GUERRERO ST	HILL ST	09
Concrete Curb/Sidewalk Repair - 301 PRECITA AVE	PRECITA AVE	FOLSOM ST	09
Concrete Curb/Sidewalk Repair - 1766 ALABAMA ST	ALABAMA ST	RUTLEDGE ST	09
Concrete Curb/Sidewalk Repair -	OGDEN AVE	PUTNAM ST	09
Concrete Curb/Sidewalk Repair - 2748 MISSION ST	MISSION ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 1495 POTRERO AVE	POTRERO AVE	25TH ST \ CESAR CHAVEZ ON RAMP	09
Concrete Curb/Sidewalk Repair - 2894 MISSION ST	MISSION ST	24TH ST	09
Concrete Curb/Sidewalk Repair - 571 NEVADA ST	NEVADA ST	OGDEN AVE	09
Concrete Curb/Sidewalk Repair -	25TH ST	UTAH ST	09
Concrete Curb/Sidewalk Repair - 103 LUNDYS LN	LUNDYS LN	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair -	COSTA ST	HOLLADAY AVE	09
Concrete Curb/Sidewalk Repair - 2889 CESAR CHAVEZ ST	CESAR CHAVEZ ST	CESAR CHAVEZ ON RAMP \ HAMPSHIRE ST	09
Concrete Curb/Sidewalk Repair - 2601 FOLSOM ST	FOLSOM ST	22ND ST	09
Concrete Curb/Sidewalk Repair - 346 ALEMANY BLVD	ALEMANY BLVD	HWY 101 S OFF RAMP \ PUTNAM ST	09
Concrete Curb/Sidewalk Repair - 896 CAPP ST	CAPP ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 2 ELSIE ST	ELSIE ST	COSO AVE	09
Concrete Curb/Sidewalk Repair - 1499 POTRERO AVE	POTRERO AVE	25TH ST \ CESAR CHAVEZ ON RAMP	09
Concrete Curb/Sidewalk Repair - 177 BOCANA ST	BOCANA ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 155 WOOL ST	WOOL ST	EUGENIA AVE	09
Concrete Curb/Sidewalk Repair - 162 BRONTE ST	BRONTE ST	TOMPKINS AVE	09
Concrete Curb/Sidewalk Repair - 75 PUTNAM ST	PUTNAM ST	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 11 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 144 PROSPECT AVE	PROSPECT AVE	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 15 BENNINGTON ST	BENNINGTON ST	BOCANA ST \ EUGENIA AVE	09
Concrete Curb/Sidewalk Repair - 186 BRONTE ST	BRONTE ST	TOMPKINS AVE	09
Concrete Curb/Sidewalk Repair - 32 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 5 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 51 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 57 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 79 WOOL ST	WOOL ST	POWHATTAN AVE	09
Concrete Curb/Sidewalk Repair - 119 SAN CARLOS ST	SAN CARLOS ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 161 SAN CARLOS ST	SAN CARLOS ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 241 SAN CARLOS ST	SAN CARLOS ST	19TH ST	09
Concrete Curb/Sidewalk Repair - 3426 19TH ST	19TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 3525 20TH ST	20TH ST	MISSION ST	09

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 38 SAN CARLOS ST	SAN CARLOS ST	SYCAMORE ST	09
Concrete Curb/Sidewalk Repair - 137 LUNDYS LN	LUNDYS LN	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 185 LUNDYS LN	LUNDYS LN	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 113 LUNDYS LN	LUNDYS LN	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 124 LUNDYS LN	LUNDYS LN	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 187 WINFIELD ST	WINFIELD ST	ESMERALDA AVE	09
Concrete Curb/Sidewalk Repair - 54 SAN JOSE AVE	SAN JOSE AVE	ALVARADO ST	09
Concrete Curb/Sidewalk Repair - 601 ALABAMA ST	ALABAMA ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 1730 FOLSOM ST	FOLSOM ST	ERIE ST	09
Concrete Curb/Sidewalk Repair - 2230 BRYANT ST	BRYANT ST	20TH ST	09
Concrete Curb/Sidewalk Repair - 1060 POTRERO AVE	POTRERO AVE	22ND ST	09
Concrete Curb/Sidewalk Repair - 486 ANDOVER ST	ANDOVER ST	TOMPKINS AVE	09
Concrete Curb/Sidewalk Repair - 727 VALENCIA ST	VALENCIA ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 346 ALEMANY BLVD	ALEMANY BLVD	HWY 101 S OFF RAMP \ PUTNAM ST	09
Concrete Curb/Sidewalk Repair - 581 VALENCIA ST	VALENCIA ST	16TH ST	09
Concrete Curb/Sidewalk Repair - 248 BRUSSELS ST	BRUSSELS ST	FELTON ST	09
Concrete Curb/Sidewalk Repair - 2 MIRABEL AVE	MIRABEL AVE	COSO AVE	09
Concrete Curb/Sidewalk Repair - 2800 MISSION ST	MISSION ST	24TH ST	09
Concrete Curb/Sidewalk Repair - 400 HOLYOKE ST	HOLYOKE ST	BACON ST	09
Concrete Curb/Sidewalk Repair - 268 ALABAMA ST	ALABAMA ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 2396 BRYANT ST	BRYANT ST	21ST ST	09
Concrete Curb/Sidewalk Repair - 1298 POTRERO AVE	POTRERO AVE	25TH ST	09
Concrete Curb/Sidewalk Repair - 206 BENNINGTON ST	BENNINGTON ST	ELLERT ST	09
Concrete Curb/Sidewalk Repair - 510 JUSTIN DR	JUSTIN DR	GENEBERN WAY	09
Concrete Curb/Sidewalk Repair - 3050 19TH ST	19TH ST	ALABAMA ST	09
Concrete Curb/Sidewalk Repair - 6 30TH ST	30TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 3277 19TH ST	19TH ST	SHOTWELL ST	09
Concrete Curb/Sidewalk Repair - 2 BRONTE ST	BRONTE ST	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 301 VALENCIA ST	VALENCIA ST	14TH ST	09
Concrete Curb/Sidewalk Repair - 1536 BAY SHORE BLVD	BAY SHORE BLVD	WOOLSEY ST	09
Concrete Curb/Sidewalk Repair - 2970 24TH ST	24TH ST	ALABAMA ST	09
Concrete Curb/Sidewalk Repair - 1200 POTRERO AVE	POTRERO AVE	24TH ST	09
Concrete Curb/Sidewalk Repair - 240 BAY SHORE BLVD	BAY SHORE BLVD	COSTA ST	09
Concrete Curb/Sidewalk Repair - 2712 MISSION ST	MISSION ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 2027 MISSION ST	MISSION ST	16TH ST	09
Concrete Curb/Sidewalk Repair - 2982 MISSION ST	MISSION ST	25TH ST	09
Concrete Curb/Sidewalk Repair - 1493 POTRERO AVE	POTRERO AVE	25TH ST \ CESAR CHAVEZ ON RAMP	09
Concrete Curb/Sidewalk Repair - 2640 MISSION ST	MISSION ST	22ND ST	09
Concrete Curb/Sidewalk Repair - 3090 16TH ST	16TH ST	CALEDONIA ST	09
Concrete Curb/Sidewalk Repair - 1890 BRYANT ST	BRYANT ST	17TH ST	09
Concrete Curb/Sidewalk Repair - 1106 VALENCIA ST	VALENCIA ST	22ND ST	09
Concrete Curb/Sidewalk Repair - 876 POTRERO AVE	POTRERO AVE	20TH ST	09
Concrete Curb/Sidewalk Repair - 66 POTRERO AVE	POTRERO AVE	10TH ST \ BRANNAN ST \ DIVISION ST	09
Concrete Curb/Sidewalk Repair - 810 POTRERO AVE	POTRERO AVE	20TH ST	09
Concrete Curb/Sidewalk Repair - 124 HOLLADAY AVE	HOLLADAY AVE	PERALTA AVE	09
Concrete Curb/Sidewalk Repair - 304 MONTCALM ST	MONTCALM ST	PERALTA AVE	09
Concrete Curb/Sidewalk Repair - 3030 16TH ST	16TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 2997 CESAR CHAVEZ ST	CESAR CHAVEZ ST	BRYANT ST	09
Concrete Curb/Sidewalk Repair - 740 MOULTRIE ST	MOULTRIE ST	OGDEN AVE	09
Concrete Curb/Sidewalk Repair - 830 GIRARD ST	GIRARD ST	OLMSTEAD ST	09
Concrete Curb/Sidewalk Repair - 3266 24TH ST	24TH ST	CAPP ST	09
Concrete Curb/Sidewalk Repair - 121 SAN CARLOS ST	SAN CARLOS ST	18TH ST	09
Concrete Curb/Sidewalk Repair - 615 SOUTH VAN NESS AVE	SOUTH VAN NESS AVE	17TH ST	09
Concrete Curb/Sidewalk Repair - 3294 26TH ST	26TH ST	VIRGIL ST	09
Concrete Curb/Sidewalk Repair - 1661 15TH ST	15TH ST	JULIAN AVE	09
Concrete Curb/Sidewalk Repair - 18 30TH ST	30TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 3458 MISSION ST	MISSION ST	KINGSTON ST	09
Concrete Curb/Sidewalk Repair - 1924 MISSION ST	MISSION ST	15TH ST	09

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 73

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 3230 CESAR CHAVEZ ST	CESAR CHAVEZ ST	SHOTWELL ST	09
Concrete Curb/Sidewalk Repair - 3090 16TH ST	16TH ST	CALEDONIA ST	09
Concrete Curb/Sidewalk Repair - 737 CORTLAND AVE	CORTLAND AVE	ANDERSON ST	09
Concrete Curb/Sidewalk Repair - 1940 HARRISON ST	HARRISON ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 343 GIRARD ST	GIRARD ST	BURROWS ST	09
Concrete Curb/Sidewalk Repair - 355 GIRARD ST	GIRARD ST	BURROWS ST	09
Concrete Curb/Sidewalk Repair - 2920 MISSION ST	MISSION ST	25TH ST	09
Concrete Curb/Sidewalk Repair - 210 BURROWS ST	BURROWS ST	GIRARD ST	09
Concrete Curb/Sidewalk Repair - 1501 VALENCIA ST	VALENCIA ST	26TH ST	09
Concrete Curb/Sidewalk Repair - 1479 ALABAMA ST	ALABAMA ST	26TH ST	09
Concrete Curb/Sidewalk Repair - 3425 CESAR CHAVEZ ST	CESAR CHAVEZ ST	CAPP ST \ MISSION ST	09
Concrete Curb/Sidewalk Repair - 839 WOOLSEY ST	WOOLSEY ST	BOWDOIN ST	09
Concrete Curb/Sidewalk Repair - 318 HOLLADAY AVE	HOLLADAY AVE	RUTLEDGE ST	09
Concrete Curb/Sidewalk Repair - 3474 MISSION ST	MISSION ST	KINGSTON ST	09
Concrete Curb/Sidewalk Repair - 500 BURROWS ST	BURROWS ST	SOMERSET ST	09
Concrete Curb/Sidewalk Repair - 37 COSO AVE	COSO AVE	PRECITA AVE	09
Concrete Curb/Sidewalk Repair - 3045 MISSION ST	MISSION ST	26TH ST	09
Concrete Curb/Sidewalk Repair - 2565 MISSION ST	MISSION ST	21ST ST	09
Concrete Curb/Sidewalk Repair - 135 CORTLAND AVE	CORTLAND AVE	PROSPECT AVE	09
Concrete Curb/Sidewalk Repair - 2712 BRYANT ST	BRYANT ST	25TH ST	09
Concrete Curb/Sidewalk Repair - 1855 FELTON ST	FELTON ST	MADISON ST	09
Concrete Curb/Sidewalk Repair - 939 SHOTWELL ST	SHOTWELL ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 1766 ALABAMA ST	ALABAMA ST	RUTLEDGE ST	09
Concrete Curb/Sidewalk Repair - 633 GATES ST	GATES ST	OGDEN AVE	09
Concrete Curb/Sidewalk Repair - 654 GATES ST	GATES ST	OGDEN AVE	09
Concrete Curb/Sidewalk Repair - 1000 CORTLAND AVE	CORTLAND AVE	FOLSOM ST	09
Concrete Curb/Sidewalk Repair - 3046 24TH ST	24TH ST	BALMY ST	09
Concrete Curb/Sidewalk Repair -	HOLLADAY AVE	YORK ST	09
Concrete Curb/Sidewalk Repair - 1227 HAMPSHIRE ST	HAMPSHIRE ST	24TH ST	09
Concrete Curb/Sidewalk Repair - 68 AZTEC ST	AZTEC ST	COSO AVE \ WINFIELD ST	09
Concrete Curb/Sidewalk Repair -	BRONTE ST	TOMPKINS AVE	09
Concrete Curb/Sidewalk Repair - 3070 23RD ST	23RD ST	TREAT AVE	09
Concrete Curb/Sidewalk Repair -	SOUTH VAN NESS AVE	13TH ST	09
Concrete Curb/Sidewalk Repair - 0000	SOUTH VAN NESS AVE	13TH ST	09
Concrete Curb/Sidewalk Repair - 2620 MISSION ST	MISSION ST	22ND ST	09
Concrete Curb/Sidewalk Repair - 2789 HARRISON ST	HARRISON ST	23RD ST	09
Concrete Curb/Sidewalk Repair - 3000 17TH ST	17TH ST	HARRISON ST	09
Concrete Curb/Sidewalk Repair - 340 BAY SHORE BLVD	BAY SHORE BLVD	COSGROVE ST	09
Concrete Curb/Sidewalk Repair - 145 GENEVERN WAY	GENEVERN WAY	MURRAY ST	09
Concrete Curb/Sidewalk Repair - 1390 YORK ST	YORK ST	25TH ST	09
Concrete Curb/Sidewalk Repair - 3166 26TH ST	26TH ST	LUCKY ST	09
Concrete Curb/Sidewalk Repair - 3458 MISSION ST	MISSION ST	KINGSTON ST	09
Concrete Curb/Sidewalk Repair - 93 PRENTISS ST	PRENTISS ST	CHAPMAN ST	09
Concrete Curb/Sidewalk Repair - 2781 24TH ST	24TH ST	HAMPSHIRE ST	09
Concrete Curb/Sidewalk Repair - 1447 SILVER AVE	SILVER AVE	GOETTINGEN ST	09
Concrete Curb/Sidewalk Repair - 2021 FOLSOM ST	FOLSOM ST	16TH ST	09
Concrete Curb/Sidewalk Repair - 3089 16TH ST	16TH ST	CALEDONIA ST	09
Concrete Curb/Sidewalk Repair - 1968 MISSION ST	MISSION ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 3000 16TH ST	16TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 3032 16TH ST	16TH ST	MISSION ST	09
Concrete Curb/Sidewalk Repair - 93 JUSTIN DR	JUSTIN DR	AGNON AVE	09
Concrete Curb/Sidewalk Repair - 1587 15TH ST	15TH ST	MINNA ST	09
Concrete Curb/Sidewalk Repair - 100 ALEMANY BLVD	ALEMANY BLVD	INDUSTRIAL ST \ INDUSTRIAL ST OFF RAMP	09
Concrete Curb/Sidewalk Repair - 30 HARVARD ST	HARVARD ST	SILVER AVE	09
Concrete Curb/Sidewalk Repair - 341 HOLYOKE ST	HOLYOKE ST	BURROWS ST	09
Concrete Curb/Sidewalk Repair - 3465 CESAR CHAVEZ ST	CESAR CHAVEZ ST	CAPP ST \ MISSION ST	09
Concrete Curb/Sidewalk Repair -	BAY SHORE BLVD	INDUSTRIAL ST \ INDUSTRIAL ST ON RAMP	09
Concrete Curb/Sidewalk Repair - 1980 MISSION ST	MISSION ST	15TH ST	09

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 98 PUTNAM ST	PUTNAM ST	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 3139 MISSION ST	MISSION ST	CAPP ST \ CESAR CHAVEZ ST	09
Concrete Curb/Sidewalk Repair -	CASE ST	END	09
Concrete Curb/Sidewalk Repair - 1985 MISSION ST	MISSION ST	15TH ST	09
Concrete Curb/Sidewalk Repair - 4053 MISSION ST	MISSION ST	BOSWORTH ST \ MURRAY ST	09
Concrete Curb/Sidewalk Repair - 500 BAY SHORE BLVD	BAY SHORE BLVD	CORTLAND AVE	09
Concrete Curb/Sidewalk Repair - 69 POMONA ST	POMONA ST	BAY VIEW ST	10
Concrete Curb/Sidewalk Repair - 200 PAUL AVE	PAUL AVE	GOULD ST	10
Concrete Curb/Sidewalk Repair - 594 VERMONT ST	VERMONT ST	MARIPOSA ST	10
Concrete Curb/Sidewalk Repair - 698 MISSOURI ST	MISSOURI ST	SIERRA ST	10
Concrete Curb/Sidewalk Repair - 2142 22ND ST	22ND ST	RHODE ISLAND ST	10
Concrete Curb/Sidewalk Repair -	24TH ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1086 INGERSON AVE	INGERSON AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1582 SHAFTER AVE	SHAFTER AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair -	23RD ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 1720 KEITH ST	KEITH ST	REVERE AVE	10
Concrete Curb/Sidewalk Repair - 774 RHODE ISLAND ST	RHODE ISLAND ST	19TH ST	10
Concrete Curb/Sidewalk Repair -	BALDWIN CT	OAKDALE AVE	10
Concrete Curb/Sidewalk Repair - 1572 KIRKWOOD AVE	KIRKWOOD AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 2244 23RD ST	23RD ST	RHODE ISLAND ST	10
Concrete Curb/Sidewalk Repair - 2645 24TH ST	24TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 45 REBECCA LN	REBECCA LN	KEITH ST	10
Concrete Curb/Sidewalk Repair - 1526 KIRKWOOD AVE	KIRKWOOD AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 1386 GOETTINGEN ST	GOETTINGEN ST	ALPHA ST \ WILDE AVE	10
Concrete Curb/Sidewalk Repair - 1125 20TH ST	20TH ST	TENNESSEE ST	10
Concrete Curb/Sidewalk Repair - 1041 25TH ST	25TH ST	TENNESSEE ST	10
Concrete Curb/Sidewalk Repair - 2601 24TH ST	24TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 4517 03RD ST	03RD ST	LA SALLE AVE	10
Concrete Curb/Sidewalk Repair - 35 EXETER ST	EXETER ST	PAUL AVE	10
Concrete Curb/Sidewalk Repair - 76 EXETER ST	EXETER ST	PAUL AVE	10
Concrete Curb/Sidewalk Repair - 200 SALINAS AVE	SALINAS AVE	GOULD ST	10
Concrete Curb/Sidewalk Repair - 1228 HOLLISTER AVE	HOLLISTER AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1100 GILMAN AVE	GILMAN AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 567 KANSAS ST	KANSAS ST	MARIPOSA ST	10
Concrete Curb/Sidewalk Repair - 700 MINNESOTA ST	MINNESOTA ST	19TH ST	10
Concrete Curb/Sidewalk Repair - 1208 JAMESTOWN AVE	JAMESTOWN AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 1215 JAMESTOWN AVE	JAMESTOWN AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 135 SALINAS AVE	SALINAS AVE	CARR ST	10
Concrete Curb/Sidewalk Repair - 210 SALINAS AVE	SALINAS AVE	GOULD ST	10
Concrete Curb/Sidewalk Repair - 65 TUCKER AVE	TUCKER AVE	ALPHA ST	10
Concrete Curb/Sidewalk Repair - 1440 BANCROFT AVE	BANCROFT AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1501 BANCROFT AVE	BANCROFT AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 759 WISCONSIN ST	WISCONSIN ST	20TH ST	10
Concrete Curb/Sidewalk Repair - 805 WISCONSIN ST	WISCONSIN ST	22ND ST	10
Concrete Curb/Sidewalk Repair - 837 WISCONSIN ST	WISCONSIN ST	22ND ST	10
Concrete Curb/Sidewalk Repair - 611 WISCONSIN ST	WISCONSIN ST	20TH ST	10
Concrete Curb/Sidewalk Repair - 3101 03RD ST	03RD ST	CESAR CHAVEZ ST	10
Concrete Curb/Sidewalk Repair - 1001 16TH ST	16TH ST	MISSOURI ST	10
Concrete Curb/Sidewalk Repair - 396 WILDE AVE	WILDE AVE	GOETTINGEN ST	10
Concrete Curb/Sidewalk Repair - 1418 THOMAS AVE	THOMAS AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 2351 23RD ST	23RD ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1212 UTAH ST	UTAH ST	23RD ST	10
Concrete Curb/Sidewalk Repair - 1936 QUESADA AVE	QUESADA AVE	QUINT ST	10
Concrete Curb/Sidewalk Repair - 2100 REVERE AVE	REVERE AVE	RANKIN ST	10
Concrete Curb/Sidewalk Repair - 1200 CESAR CHAVEZ ST	CESAR CHAVEZ ST	MINNESOTA ST	10
Concrete Curb/Sidewalk Repair - 1344 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 5075 03RD ST	03RD ST	QUESADA AVE	10
Concrete Curb/Sidewalk Repair - 1435 SAN BRUNO AVE	SAN BRUNO AVE	25TH ST	10

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 75

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1240 FITZGERALD AVE	FITZGERALD AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1290 EGBERT AVE	EGBERT AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 5251 03RD ST	03RD ST	UNDERWOOD AVE	10
Concrete Curb/Sidewalk Repair - 1373 EGBERT AVE	EGBERT AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 4850 03RD ST	03RD ST	OAKDALE AVE	10
Concrete Curb/Sidewalk Repair - 619 CAROLINA ST	CAROLINA ST	19TH ST	10
Concrete Curb/Sidewalk Repair - 609 TEXAS ST	TEXAS ST	20TH ST	10
Concrete Curb/Sidewalk Repair - 2200 22ND ST	22ND ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1480 BANCROFT AVE	BANCROFT AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 461 HARKNESS AVE	HARKNESS AVE	MILL ST	10
Concrete Curb/Sidewalk Repair - 1 RUTLAND ST	RUTLAND ST	HARKNESS AVE	10
Concrete Curb/Sidewalk Repair - 332 WILDE AVE	WILDE AVE	GOETTINGEN ST	10
Concrete Curb/Sidewalk Repair - 314 WILDE AVE	WILDE AVE	GOETTINGEN ST	10
Concrete Curb/Sidewalk Repair - 2895 03RD ST	03RD ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 442 HARKNESS AVE	HARKNESS AVE	ALDER ST	10
Concrete Curb/Sidewalk Repair - 2205 JENNINGS ST	JENNINGS ST	WALLACE AVE	10
Concrete Curb/Sidewalk Repair - 2600 INGALLS ST	INGALLS ST	CARROLL AVE	10
Concrete Curb/Sidewalk Repair - 1598 YOSEMITE AVE	YOSEMITE AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1345 UNDERWOOD AVE	UNDERWOOD AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 134 DELTA ST	DELTA ST	WILDE AVE	10
Concrete Curb/Sidewalk Repair - 2199 17TH ST	17TH ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 1440 BANCROFT AVE	BANCROFT AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1950 CESAR CHAVEZ ST	CESAR CHAVEZ ST	CONNECTICUT ST	10
Concrete Curb/Sidewalk Repair - 3450 03RD ST	03RD ST	ARTHUR AVE \ CARGO WAY	10
Concrete Curb/Sidewalk Repair - 1425 YOSEMITE AVE	YOSEMITE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1842 SILVER AVE	SILVER AVE	WATERVILLE ST	10
Concrete Curb/Sidewalk Repair - 3400 03RD ST	03RD ST	ARTHUR AVE \ CARGO WAY	10
Concrete Curb/Sidewalk Repair - 1069 PENNSYLVANIA AVE	PENNSYLVANIA AVE	I-280 S OFF RAMP	10
Concrete Curb/Sidewalk Repair - 648 PENNSYLVANIA AVE	PENNSYLVANIA AVE	20TH ST	10
Concrete Curb/Sidewalk Repair - 1105 REVERE AVE	REVERE AVE	GRIFFITH ST	10
Concrete Curb/Sidewalk Repair - 1425 ARMSTRONG AVE	ARMSTRONG AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2323 CESAR CHAVEZ ST	CESAR CHAVEZ ST	EVANS AVE	10
Concrete Curb/Sidewalk Repair - 2323 CESAR CHAVEZ ST	CESAR CHAVEZ ST	EVANS AVE	10
Concrete Curb/Sidewalk Repair - 435 POTRERO AVE	POTRERO AVE	17TH ST	10
Concrete Curb/Sidewalk Repair - 875 VERMONT ST	VERMONT ST	21ST ST	10
Concrete Curb/Sidewalk Repair - 1299 25TH ST	25TH ST	I-280 N ON RAMP \ INDIANA ST	10
Concrete Curb/Sidewalk Repair - 6201 03RD ST	03RD ST	GILMAN AVE \ PAUL AVE	10
Concrete Curb/Sidewalk Repair - 5250 03RD ST	03RD ST	UNDERWOOD AVE	10
Concrete Curb/Sidewalk Repair - 1555 BANCROFT AVE	BANCROFT AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1414 PALOU AVE	PALOU AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 1490 CARROLL AVE	CARROLL AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2501 25TH ST	25TH ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 6202 03RD ST	03RD ST	GILMAN AVE \ PAUL AVE	10
Concrete Curb/Sidewalk Repair - 6271 03RD ST	03RD ST	HOLLISTER AVE	10
Concrete Curb/Sidewalk Repair - 5411 03RD ST	03RD ST	LANE ST \ WALLACE AVE	10
Concrete Curb/Sidewalk Repair - 6025 03RD ST	03RD ST	EGBERT AVE	10
Concrete Curb/Sidewalk Repair - 1424 YOSEMITE AVE	YOSEMITE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1550 CARROLL AVE	CARROLL AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 3238 INGALLS ST	INGALLS ST	INGERSON AVE	10
Concrete Curb/Sidewalk Repair - 1619 REVERE AVE	REVERE AVE	LANE ST	10
Concrete Curb/Sidewalk Repair - 1201 HOLLISTER AVE	HOLLISTER AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1990 ALAMEDA ST	ALAMEDA ST	HENRY ADAMS ST	10
Concrete Curb/Sidewalk Repair - 1490 19TH ST	19TH ST	MISSOURI ST	10
Concrete Curb/Sidewalk Repair - 1197 HOLLISTER AVE	HOLLISTER AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 628 MISSOURI ST	MISSOURI ST	20TH ST	10
Concrete Curb/Sidewalk Repair - 1089 PALOU AVE	PALOU AVE	CRISP RD	10
Concrete Curb/Sidewalk Repair - 495 DE HARO ST	DE HARO ST	17TH ST	10
Concrete Curb/Sidewalk Repair - 1190 THOMAS AVE	THOMAS AVE	GRIFFITH ST	10

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1468 25TH ST		PENNSYLVANIA AVE	10
Concrete Curb/Sidewalk Repair - 1301 CESAR CHAVEZ ST	CESAR CHAVEZ ST	INDIANA ST	10
Concrete Curb/Sidewalk Repair - 6245 03RD ST	03RD ST	GILMAN AVE \ PAUL AVE	10
Concrete Curb/Sidewalk Repair - 5155 03RD ST	03RD ST	SHAFTER AVE	10
Concrete Curb/Sidewalk Repair - 100 POTRERO AVE	POTRERO AVE	ALAMEDA ST	10
Concrete Curb/Sidewalk Repair - 1100 CESAR CHAVEZ ST		TENNESSEE ST	10
Concrete Curb/Sidewalk Repair - 5245 03RD ST	03RD ST	THORNTON AVE	10
Concrete Curb/Sidewalk Repair - 5251 03RD ST	03RD ST	UNDERWOOD AVE	10
Concrete Curb/Sidewalk Repair - 1355 VAN DYKE AVE	VAN DYKE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1613 SHAFTER AVE	SHAFTER AVE	LANE ST	10
Concrete Curb/Sidewalk Repair - 201 PAUL AVE	PAUL AVE	GOULD ST	10
Concrete Curb/Sidewalk Repair - 1555 YOSEMITE AVE	YOSEMITE AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 2932 INGALLS ST	INGALLS ST	FITZGERALD AVE	10
Concrete Curb/Sidewalk Repair - 3000 JENNINGS ST	JENNINGS ST	GILMAN AVE	10
Concrete Curb/Sidewalk Repair - 715 IOWA ST	IOWA ST	22ND ST	10
Concrete Curb/Sidewalk Repair - 1195 GILMAN AVE	GILMAN AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1500 QUESADA AVE	QUESADA AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 1701 BAY SHORE BLVD	BAY SHORE BLVD	CRANE ST \ HWY 101 S ON RAMP \ SALINAS AVE	10
Concrete Curb/Sidewalk Repair - 2944 INGALLS ST	INGALLS ST	FITZGERALD AVE	10
Concrete Curb/Sidewalk Repair - 1198 GILMAN AVE	GILMAN AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 2110 INGALLS ST	INGALLS ST	VAN DYKE AVE	10
Concrete Curb/Sidewalk Repair - 1316 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 1600 DONNER AVE	DONNER AVE	03RD ST	10
Concrete Curb/Sidewalk Repair - 2285 JERROLD AVE	JERROLD AVE	UPTON ST	10
Concrete Curb/Sidewalk Repair - 1200 THOMAS AVE	THOMAS AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1230 FITZGERALD AVE	FITZGERALD AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2110 INGALLS ST	INGALLS ST	VAN DYKE AVE	10
Concrete Curb/Sidewalk Repair - 344 CONNECTICUT ST	CONNECTICUT ST	18TH ST	10
Concrete Curb/Sidewalk Repair - 1101 PALOU AVE	PALOU AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1155 PALOU AVE	PALOU AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1201 HAWES ST	HAWES ST	PALOU AVE	10
Concrete Curb/Sidewalk Repair - 6300 03RD ST	03RD ST	SALINAS AVE	10
Concrete Curb/Sidewalk Repair - 1210 GRIFFITH ST	GRIFFITH ST	PALOU AVE	10
Concrete Curb/Sidewalk Repair - 1405 INDIANA ST	INDIANA ST	25TH ST \ I-280 N ON RAMP	10
Concrete Curb/Sidewalk Repair - 5501 03RD ST	03RD ST	YOSEMITE AVE	10
Concrete Curb/Sidewalk Repair - 6245 03RD ST	03RD ST	GILMAN AVE \ PAUL AVE	10
Concrete Curb/Sidewalk Repair - 1345 20TH ST	20TH ST	MISSISSIPPI ST	10
Concrete Curb/Sidewalk Repair - 2325 HUMBOLDT ST	HUMBOLDT ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1426 DONNER AVE	DONNER AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1485 CARROLL AVE	CARROLL AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1043 MARIN ST	MARIN ST	ILLINOIS ST	10
Concrete Curb/Sidewalk Repair - 1207 THOMAS AVE	THOMAS AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1251 THOMAS AVE	THOMAS AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1423 THOMAS AVE	THOMAS AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1450 VAN DYKE AVE	VAN DYKE AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1555 BANCROFT AVE	BANCROFT AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1924 JENNINGS ST	JENNINGS ST	THOMAS AVE	10
Concrete Curb/Sidewalk Repair -	CESAR CHAVEZ ST	I-280 N OFF RAMP \ PENNSYLVANIA AVE	10
Concrete Curb/Sidewalk Repair - 595 RHODE ISLAND ST	RHODE ISLAND ST	MARIPOSA ST	10
Concrete Curb/Sidewalk Repair - 1367 KANSAS ST	KANSAS ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 2789 25TH ST	25TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 2500 MARIN ST	MARIN ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 0300 SELBY ST	SELBY ST	EVANS AVE	10
Concrete Curb/Sidewalk Repair - 1353 YOSEMITE AVE	YOSEMITE AVE	HAWES ST	10
Concrete Curb/Sidewalk Repair - 1560 WALLACE AVE	WALLACE AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1600 ARMSTRONG AVE	ARMSTRONG AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 890 VERMONT ST	VERMONT ST	21ST ST	10
Concrete Curb/Sidewalk Repair - 1450 DONNER AVE	DONNER AVE	INGALLS ST	10

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 77

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1455 DONNER AVE	DONNER AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2446 24TH ST	24TH ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 1203 GIRARD ST	GIRARD ST	HARKNESS AVE	10
Concrete Curb/Sidewalk Repair - 1048 LE CONTE AVE	LE CONTE AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1489 ARMSTRONG AVE	ARMSTRONG AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1509 ARMSTRONG AVE	ARMSTRONG AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 1401 YOSEMITE AVE	YOSEMITE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2275 JENNINGS ST	JENNINGS ST	WALLACE AVE	10
Concrete Curb/Sidewalk Repair - 2050 20TH ST	20TH ST	DE HARO ST	10
Concrete Curb/Sidewalk Repair - 2125 BRYANT ST	BRYANT ST	19TH ST	10
Concrete Curb/Sidewalk Repair - 2590 MARIN ST	MARIN ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 2225 23RD ST	23RD ST	RHODE ISLAND ST	10
Concrete Curb/Sidewalk Repair - 893 MEADE AVE	MEADE AVE	JENNINGS CT	10
Concrete Curb/Sidewalk Repair - 1500 CARROLL AVE	CARROLL AVE	JENNINGS ST	10
Concrete Curb/Sidewalk Repair - 5701 03RD ST	03RD ST	BANCROFT AVE	10
Concrete Curb/Sidewalk Repair - 1563 INNES AVE	INNES AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 2275 JENNINGS ST	JENNINGS ST	WALLACE AVE	10
Concrete Curb/Sidewalk Repair - 1435 SAN BRUNO AVE	SAN BRUNO AVE	25TH ST	10
Concrete Curb/Sidewalk Repair - 1050 MARIN ST	MARIN ST	ILLINOIS ST	10
Concrete Curb/Sidewalk Repair - 1460 YOSEMITE AVE	YOSEMITE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 2001 OAKDALE AVE	OAKDALE AVE	RANKIN ST	10
Concrete Curb/Sidewalk Repair - 1790 MCKINNON AVE	MCKINNON AVE	NEWHALL ST	10
Concrete Curb/Sidewalk Repair - 319 RAYMOND AVE	RAYMOND AVE	DELTA ST	10
Concrete Curb/Sidewalk Repair - 1394 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 220 RANKIN ST	RANKIN ST	DAVIDSON AVE	10
Concrete Curb/Sidewalk Repair - 1414 KANSAS ST	KANSAS ST	25TH ST	10
Concrete Curb/Sidewalk Repair - 161 DESMOND ST	DESMOND ST	VISITACION AVE	10
Concrete Curb/Sidewalk Repair - 295 SAN BRUNO AVE	SAN BRUNO AVE	15TH ST	10
Concrete Curb/Sidewalk Repair - 1273 POTRERO AVE	POTRERO AVE	24TH ST	10
Concrete Curb/Sidewalk Repair - 1346 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 1851 BRYANT ST	BRYANT ST	17TH ST	10
Concrete Curb/Sidewalk Repair - 1700 EVANS AVE	EVANS AVE	QUINT ST	10
Concrete Curb/Sidewalk Repair - 1842 SILVER AVE	SILVER AVE	WATERVILLE ST	10
Concrete Curb/Sidewalk Repair - 10 BRIDGEVIEW DR	BRIDGEVIEW DR	NEWHALL ST \ REVERE AVE	10
Concrete Curb/Sidewalk Repair - 715 IOWA ST	IOWA ST	22ND ST	10
Concrete Curb/Sidewalk Repair - 1400 EVANS AVE	EVANS AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 1242 UTAH ST	UTAH ST	23RD ST	10
Concrete Curb/Sidewalk Repair -	23RD ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1391 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 1614 MCKINNON AVE	MCKINNON AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 2500 23RD ST	23RD ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 1500 NEWCOMB AVE	NEWCOMB AVE	LANE ST	10
Concrete Curb/Sidewalk Repair - 1950 CESAR CHAVEZ ST	CESAR CHAVEZ ST	CONNECTICUT ST	10
Concrete Curb/Sidewalk Repair - 1621 PALOU AVE	PALOU AVE	03RD ST \ MENDELL ST	10
Concrete Curb/Sidewalk Repair - 1403 SAN BRUNO AVE	SAN BRUNO AVE	25TH ST	10
Concrete Curb/Sidewalk Repair - 2603 23RD ST	23RD ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 1346 VERMONT ST	VERMONT ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 2301 23RD ST	23RD ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 1380 VERMONT ST	VERMONT ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 1671 JERROLD AVE	JERROLD AVE	03RD ST \ NEWHALL ST	10
Concrete Curb/Sidewalk Repair - 220 SAN BRUNO AVE	SAN BRUNO AVE	15TH ST	10
Concrete Curb/Sidewalk Repair -	NEWCOMB AVE	WHITNEY YOUNG CIR	10
Concrete Curb/Sidewalk Repair - 1204 VERMONT ST	VERMONT ST	23RD ST	10
Concrete Curb/Sidewalk Repair - 101 BAY SHORE BLVD	BAY SHORE BLVD	BAY SHORE BLVD OFF RAMP \ HWY 101 N OFF RAMP \ HWY 101 N ON RAMP \ JERROLD AVE	10
Concrete Curb/Sidewalk Repair - 420 23RD ST	23RD ST	ILLINOIS ST	10
Concrete Curb/Sidewalk Repair - 5150 03RD ST	03RD ST	SHAFTER AVE	10

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1300 LA SALLE AVE	LA SALLE AVE	OSCEOLA LN	10
Concrete Curb/Sidewalk Repair - 1399 POTRERO AVE	POTRERO AVE	25TH ST \ CESAR CHAVEZ ON RAMP	10
Concrete Curb/Sidewalk Repair - 2500 24TH ST	24TH ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 33 FLORA ST	FLORA ST	BAY VIEW ST	10
Concrete Curb/Sidewalk Repair - 2401 22ND ST	22ND ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 5146 03RD ST	03RD ST	SHAFTER AVE	10
Concrete Curb/Sidewalk Repair - 1499 POTRERO AVE	POTRERO AVE	25TH ST \ CESAR CHAVEZ ON RAMP	10
Concrete Curb/Sidewalk Repair -	23RD ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 211 INDUSTRIAL ST	INDUSTRIAL ST	BARNEVELD AVE \ SHAFTER AVE	10
Concrete Curb/Sidewalk Repair -	25TH ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 501 RHODE ISLAND ST	RHODE ISLAND ST	MARIPOSA ST	10
Concrete Curb/Sidewalk Repair - 1 HENRY ADAMS ST	HENRY ADAMS ST	DIVISION ST	10
Concrete Curb/Sidewalk Repair - 2 HENRY ADAMS ST	HENRY ADAMS ST	DIVISION ST	10
Concrete Curb/Sidewalk Repair - 50 MADDUX AVE	MADDUX AVE	QUINT ST	10
Concrete Curb/Sidewalk Repair - 2210 QUESADA AVE	QUESADA AVE	SELBY ST	10
Concrete Curb/Sidewalk Repair - 801 TOLAND ST	TOLAND ST	MCKINNON AVE	10
Concrete Curb/Sidewalk Repair - 2150 CESAR CHAVEZ ST	CESAR CHAVEZ ST	EVANS AVE	10
Concrete Curb/Sidewalk Repair - 1501 VERMONT ST	VERMONT ST	26TH ST	10
Concrete Curb/Sidewalk Repair - 2174 BAY SHORE BLVD	BAY SHORE BLVD	TUNNEL AVE	10
Concrete Curb/Sidewalk Repair - 91 GILLETTE AVE	GILLETTE AVE	BLANKEN AVE	10
Concrete Curb/Sidewalk Repair - 2400 BAY SHORE BLVD	BAY SHORE BLVD	LELAND AVE	10
Concrete Curb/Sidewalk Repair - 100 CORA ST	CORA ST	VISITACION AVE	10
Concrete Curb/Sidewalk Repair - 3433 03RD ST	03RD ST	ARTHUR AVE \ CARGO WAY	10
Concrete Curb/Sidewalk Repair - 93 DELTA ST	DELTA ST	HAMILTON ST	10
Concrete Curb/Sidewalk Repair - 1425 ARMSTRONG AVE	ARMSTRONG AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1090 GIRARD ST	GIRARD ST	ORDWAY ST	10
Concrete Curb/Sidewalk Repair - 1800 EVANS AVE	EVANS AVE	RANKIN ST	10
Concrete Curb/Sidewalk Repair - 2100 REVERE AVE	REVERE AVE	RANKIN ST	10
Concrete Curb/Sidewalk Repair - 1075 GILMAN AVE	GILMAN AVE	GRIFFITH ST	10
Concrete Curb/Sidewalk Repair - 2789 25TH ST	25TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 2789 25TH ST	25TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 1280 WISCONSIN ST	WISCONSIN ST	BLAIR TER	10
Concrete Curb/Sidewalk Repair - 2639 24TH ST	24TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 1200 KANSAS ST	KANSAS ST	23RD ST	10
Concrete Curb/Sidewalk Repair - 1485 ARMSTRONG AVE	ARMSTRONG AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 1307 KANSAS ST	KANSAS ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 390 KANSAS ST	KANSAS ST	16TH ST	10
Concrete Curb/Sidewalk Repair - 1510 REVERE AVE	REVERE AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair - 301 RAYMOND AVE	RAYMOND AVE	DELTA ST	10
Concrete Curb/Sidewalk Repair - 1101 ILLINOIS ST	ILLINOIS ST	22ND ST	10
Concrete Curb/Sidewalk Repair - 3100 03RD ST	03RD ST	CESAR CHAVEZ ST	10
Concrete Curb/Sidewalk Repair - 1100 CESAR CHAVEZ ST		TENNESSEE ST	10
Concrete Curb/Sidewalk Repair - 5 LELAND AVE	LELAND AVE	BAY SHORE BLVD	10
Concrete Curb/Sidewalk Repair - 2401 22ND ST	22ND ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 4250 3RD ST	3RD ST	INNES AVE	10
Concrete Curb/Sidewalk Repair - 6202 03RD ST	03RD ST	GILMAN AVE \ PAUL AVE	10
Concrete Curb/Sidewalk Repair - 1495 YOSEMITE AVE	YOSEMITE AVE	INGALLS ST	10
Concrete Curb/Sidewalk Repair - 4702 03RD ST	03RD ST	NEWCOMB AVE	10
Concrete Curb/Sidewalk Repair -	HARKNESS AVE	SPARTA ST	10
Concrete Curb/Sidewalk Repair - 200 LOOMIS ST	LOOMIS ST	WATERLOO ST	10
Concrete Curb/Sidewalk Repair - 2500 23RD ST	23RD ST	SAN BRUNO AVE	10
Concrete Curb/Sidewalk Repair - 801 MINNESOTA ST	MINNESOTA ST	20TH ST	10
Concrete Curb/Sidewalk Repair - 1444 RANKIN ST	RANKIN ST	PALOU AVE	10
Concrete Curb/Sidewalk Repair - 2096 QUESADA AVE	QUESADA AVE	SILVER AVE	10
Concrete Curb/Sidewalk Repair - 480 TOLAND ST	TOLAND ST	HUDSON AVE	10
Concrete Curb/Sidewalk Repair - 435 WILDE AVE	WILDE AVE	RUTLAND ST	10
Concrete Curb/Sidewalk Repair - 714 DELTA ST	DELTA ST	VISITACION AVE	10
Concrete Curb/Sidewalk Repair - 1645 17TH ST	17TH ST	WISCONSIN ST	10

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024 79

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair -	DIVISION ST	HENRY ADAMS ST	10
Concrete Curb/Sidewalk Repair - 25 SPARTA ST	SPARTA ST	ANKENY ST \ WARD ST	10
Concrete Curb/Sidewalk Repair -	BAY SHORE BLVD	LOIS LN	10
Concrete Curb/Sidewalk Repair -	LOOMIS ST	WATERLOO ST	10
Concrete Curb/Sidewalk Repair -	DIVISION ST	HENRY ADAMS ST	10
Concrete Curb/Sidewalk Repair -	CASHMERE ST	LA SALLE AVE	10
Concrete Curb/Sidewalk Repair -	03RD ST	HWY 101 S ON RAMP \ JAMESTOWN AVE	10
Concrete Curb/Sidewalk Repair - 1639 PALOU AVE	PALOU AVE	03RD ST \ MENDELL ST	10
Concrete Curb/Sidewalk Repair - 4301 03RD ST	03RD ST	JERROLD AVE \ NEWHALL ST	10
Concrete Curb/Sidewalk Repair - 1552 INNES AVE	INNES AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 2789 25TH ST	25TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 625 BAY SHORE BLVD	BAY SHORE BLVD	INDUSTRIAL ST \ INDUSTRIAL ST ON RAMP	10
Concrete Curb/Sidewalk Repair - 1200 18TH ST	18TH ST	MISSISSIPPI ST	10
Concrete Curb/Sidewalk Repair - 1316 UTAH ST	UTAH ST	24TH ST	10
Concrete Curb/Sidewalk Repair - 2157 BAY SHORE BLVD	BAY SHORE BLVD	TUNNEL AVE	10
Concrete Curb/Sidewalk Repair - 3550 03RD ST	03RD ST	BURKE AVE	10
Concrete Curb/Sidewalk Repair - 1740 REVERE AVE	REVERE AVE	03RD ST \ BAY VIEW ST	10
Concrete Curb/Sidewalk Repair - 220 RANKIN ST	RANKIN ST	DAVIDSON AVE	10
Concrete Curb/Sidewalk Repair -	BLANKEN AVE	EXECUTIVE PARK BLVD	10
Concrete Curb/Sidewalk Repair - 960 7TH ST	7TH ST	BERRY ST	10
Concrete Curb/Sidewalk Repair - 1501 KIRKWOOD AVE	KIRKWOOD AVE	MENDELL ST	10
Concrete Curb/Sidewalk Repair - 643 MENDELL ST	MENDELL ST	GALVEZ AVE	10
Concrete Curb/Sidewalk Repair - 2641 24TH ST	24TH ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 2325 HUMBOLDT ST	HUMBOLDT ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 555 DE HARO ST	DE HARO ST	MARIPOSA ST	10
Concrete Curb/Sidewalk Repair - 2001 BAY SHORE BLVD	BAY SHORE BLVD	BAYVIEW PARK RD \ HESTER AVE \ HWY 101 S O	10
Concrete Curb/Sidewalk Repair - 2200 22ND ST	22ND ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 2446 24TH ST	24TH ST	VERMONT ST	10
Concrete Curb/Sidewalk Repair - 2603 23RD ST	23RD ST	UTAH ST	10
Concrete Curb/Sidewalk Repair - 1492 HUDSON AVE	HUDSON AVE	KEITH ST	10
Concrete Curb/Sidewalk Repair -	23RD ST	KANSAS ST	10
Concrete Curb/Sidewalk Repair - 2030 THOMAS AVE	THOMAS AVE	MADDUX AVE	10
Concrete Curb/Sidewalk Repair - 2101 23RD ST	23RD ST	DE HARO ST	10
Concrete Curb/Sidewalk Repair - 2129 24TH ST	24TH ST	DE HARO ST	10
Concrete Curb/Sidewalk Repair - 230 AVALON AVE	AVALON AVE	PARIS ST	11
Concrete Curb/Sidewalk Repair - 300 NIAGARA AVE	NIAGARA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 2275 SAN JOSE AVE	SAN JOSE AVE	SENECA AVE	11
Concrete Curb/Sidewalk Repair - 4690 MISSION ST	MISSION ST	OCEAN AVE	11
Concrete Curb/Sidewalk Repair - 139 LOBOS ST	LOBOS ST	PLYMOUTH AVE	11
Concrete Curb/Sidewalk Repair -	MISSION ST	SILVER AVE	11
Concrete Curb/Sidewalk Repair - 645 BRUNSWICK ST	BRUNSWICK ST	LOWELL ST	11
Concrete Curb/Sidewalk Repair - 4089 19TH AVE	19TH AVE	CHESTER AVE	11
Concrete Curb/Sidewalk Repair - 51 BRIGHTON AVE	BRIGHTON AVE	LAKEVIEW AVE	11
Concrete Curb/Sidewalk Repair - 612 LA GRANDE AVE	LA GRANDE AVE	RUSSIA AVE	11
Concrete Curb/Sidewalk Repair - 12 LEE AVE	LEE AVE	LAKEVIEW AVE \ SUMMIT ST	11
Concrete Curb/Sidewalk Repair - 66 SAN JUAN AVE	SAN JUAN AVE	MISSION ST	11
Concrete Curb/Sidewalk Repair - 600 PRAGUE ST	PRAGUE ST	GENEVA AVE	11
Concrete Curb/Sidewalk Repair - 19 MAJESTIC AVE	MAJESTIC AVE	RIDGE LN \ TARA ST	11
Concrete Curb/Sidewalk Repair - 5 CANYON DR	CANYON DR	ROBINSON DR	11
Concrete Curb/Sidewalk Repair -	CAINE AVE	RIDGE LN	11
Concrete Curb/Sidewalk Repair - 967 DELANO AVE	DELANO AVE	NAHUA AVE	11
Concrete Curb/Sidewalk Repair - 5507 MISSION ST	MISSION ST	GUTTENBERG ST	11
Concrete Curb/Sidewalk Repair - 250 WILSON ST	WILSON ST	RHINE ST	11
Concrete Curb/Sidewalk Repair -	GENEVA AVE	OCEAN AVE	11
Concrete Curb/Sidewalk Repair -	ALEMANY BLVD	CONGDON ST	11
Concrete Curb/Sidewalk Repair - 489 FAXON AVE	FAXON AVE	HOLLOWAY AVE	11
Concrete Curb/Sidewalk Repair - 319 VERNON ST	VERNON ST	SHIELDS ST	11
Concrete Curb/Sidewalk Repair - 842 EDINBURGH ST	EDINBURGH ST	ITALY AVE	11

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair -	GENEVA AVE	MUNICH ST	11
Concrete Curb/Sidewalk Repair - 348 NIAGARA AVE	NIAGARA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 200 CURTIS ST	CURTIS ST	BRUNSWICK ST	11
Concrete Curb/Sidewalk Repair - 4304 MISSION ST	MISSION ST	SILVER AVE	11
Concrete Curb/Sidewalk Repair - 615 LAKEVIEW AVE	LAKEVIEW AVE	PLYMOUTH AVE	11
Concrete Curb/Sidewalk Repair - 719 GENEVA AVE	GENEVA AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 159 SEVILLE ST	SEVILLE ST	CORDOVA ST	11
Concrete Curb/Sidewalk Repair - 163 SEVILLE ST	SEVILLE ST	CORDOVA ST	11
Concrete Curb/Sidewalk Repair - 169 SEVILLE ST	SEVILLE ST	CORDOVA ST	11
Concrete Curb/Sidewalk Repair - 1839 OCEAN AVE	OCEAN AVE	DORADO TER \ JULES AVE	11
Concrete Curb/Sidewalk Repair - 130 SEVILLE ST	SEVILLE ST	CORDOVA ST	11
Concrete Curb/Sidewalk Repair - 176 SEVILLE ST	SEVILLE ST	CORDOVA ST	11
Concrete Curb/Sidewalk Repair - 31 SEVILLE ST	SEVILLE ST	ROLPH ST	11
Concrete Curb/Sidewalk Repair - 242 TRUMBULL ST	TRUMBULL ST	CONGDON ST	11
Concrete Curb/Sidewalk Repair - 2401 SAN JOSE AVE	SAN JOSE AVE	NIAGARA AVE	11
Concrete Curb/Sidewalk Repair - 56 NAVAJO AVE	NAVAJO AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 579 MADRID ST	MADRID ST	PERSIA AVE	11
Concrete Curb/Sidewalk Repair - 375 CAPITOL AVE	CAPITOL AVE	BROAD ST	11
Concrete Curb/Sidewalk Repair - 47 NAVAJO AVE	NAVAJO AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 2099 SAN JOSE AVE	SAN JOSE AVE	SERGEANT JOHN V YOUNG ST	11
Concrete Curb/Sidewalk Repair - 414 MOUNT VERNON AVE	MOUNT VERNON AVE	SAN JOSE AVE	11
Concrete Curb/Sidewalk Repair - 73 BROAD ST	BROAD ST	FARRAGUT AVE \ SAN JOSE AVE	11
Concrete Curb/Sidewalk Repair - 315 LONDON ST	LONDON ST	BRAZIL AVE	11
Concrete Curb/Sidewalk Repair - 32 MADRID ST	MADRID ST	SILVER AVE	11
Concrete Curb/Sidewalk Repair - 122 RAMSELL ST	RAMSELL ST	RANDOLPH ST	11
Concrete Curb/Sidewalk Repair - 167 RAMSELL ST	RAMSELL ST	RANDOLPH ST	11
Concrete Curb/Sidewalk Repair - 17 SANTA YNEZ AVE	SANTA YNEZ AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 4638 MISSION ST	MISSION ST	NORTON ST	11
Concrete Curb/Sidewalk Repair - 530 BRUNSWICK ST	BRUNSWICK ST	GUTTENBERG ST	11
Concrete Curb/Sidewalk Repair - 900 VIENNA ST	VIENNA ST	AMAZON AVE	11
Concrete Curb/Sidewalk Repair - 209 THERESA ST	THERESA ST	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 436 RUSSIA AVE	RUSSIA AVE	MADRID ST	11
Concrete Curb/Sidewalk Repair - 501 LISBON ST	LISBON ST	RUSSIA AVE	11
Concrete Curb/Sidewalk Repair - 151 MONTANA ST	MONTANA ST	PLYMOUTH AVE	11
Concrete Curb/Sidewalk Repair - 415 GARFIELD ST	GARFIELD ST	RAMSELL ST	11
Concrete Curb/Sidewalk Repair - 607 PRAGUE ST	PRAGUE ST	GENEVA AVE	11
Concrete Curb/Sidewalk Repair - 70 HAVELOCK ST	HAVELOCK ST	SAN JOSE AVE	11
Concrete Curb/Sidewalk Repair - 40 WANDA ST	WANDA ST	OCEAN AVE	11
Concrete Curb/Sidewalk Repair - 205 SAGAMORE ST	SAGAMORE ST	CAPITOL AVE	11
Concrete Curb/Sidewalk Repair - 350 OCEAN AVE	OCEAN AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 358 NAPLES ST	NAPLES ST	EXCELSIOR AVE	11
Concrete Curb/Sidewalk Repair - 231 SILVER AVE	SILVER AVE	ALEMANY BLVD	11
Concrete Curb/Sidewalk Repair - 118 GUTTENBERG ST	GUTTENBERG ST	MORSE ST	11
Concrete Curb/Sidewalk Repair - 720 MOSCOW ST	MOSCOW ST	FRANCE AVE	11
Concrete Curb/Sidewalk Repair - 4747 MISSION ST	MISSION ST	LEO ST	11
Concrete Curb/Sidewalk Repair - 4994 MISSION ST	MISSION ST	KENNY ALY	11
Concrete Curb/Sidewalk Repair - 173 SANTA ROSA AVE	SANTA ROSA AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 275 MINERVA ST	MINERVA ST	CAPITOL AVE	11
Concrete Curb/Sidewalk Repair - 47 NAVAJO AVE	NAVAJO AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 5006 MISSION ST	MISSION ST	ITALY AVE	11
Concrete Curb/Sidewalk Repair - 30 SANTA YSABEL AVE	SANTA YSABEL AVE	OTSEGO AVE	11
Concrete Curb/Sidewalk Repair - 90 ONEIDA AVE	ONEIDA AVE	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 449 RANDOLPH ST	RANDOLPH ST	RAMSELL ST	11
Concrete Curb/Sidewalk Repair - 1770 SAN JOSE AVE	SAN JOSE AVE	BADEN ST	11
Concrete Curb/Sidewalk Repair - 4689 MISSION ST	MISSION ST	OCEAN AVE	11
Concrete Curb/Sidewalk Repair - 162 EDINBURGH ST	EDINBURGH ST	PERU AVE	11
Concrete Curb/Sidewalk Repair - 25 ACTON ST	ACTON ST	MISSION ST \ SICKLES AVE	11
Concrete Curb/Sidewalk Repair - 28 SENECA AVE	SENECA AVE	MISSION ST	11

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 177 HAROLD AVE	HAROLD AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 842 BRUNSWICK ST	BRUNSWICK ST	OLIVER ST	11
Concrete Curb/Sidewalk Repair - 1 LAWRENCE AVE	LAWRENCE AVE	MISSION ST	11
Concrete Curb/Sidewalk Repair - 151 MONTICELLO ST	MONTICELLO ST	SARGENT ST	11
Concrete Curb/Sidewalk Repair - 4308 MISSION ST	MISSION ST	SILVER AVE	11
Concrete Curb/Sidewalk Repair - 700 CAYUGA AVE	CAYUGA AVE	SANTA ROSA AVE	11
Concrete Curb/Sidewalk Repair - 282 MAYNARD ST	MAYNARD ST	CONGDON ST	11
Concrete Curb/Sidewalk Repair - 342 NIAGARA AVE	NIAGARA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 66 JOSIAH AVE	JOSIAH AVE	RIDGE LN	11
Concrete Curb/Sidewalk Repair - 5080 MISSION ST	MISSION ST	AMAZON AVE	11
Concrete Curb/Sidewalk Repair - 4950 MISSION ST	MISSION ST	FRANCE AVE	11
Concrete Curb/Sidewalk Repair - 200 HAROLD AVE	HAROLD AVE	BRUCE AVE	11
Concrete Curb/Sidewalk Repair - 154 OCEAN AVE	OCEAN AVE	WANDA ST	11
Concrete Curb/Sidewalk Repair - 10 ROEMER WAY	ROEMER WAY	BRUNSWICK ST	11
Concrete Curb/Sidewalk Repair - 1500 CAYUGA AVE	CAYUGA AVE	MOUNT VERNON AVE	11
Concrete Curb/Sidewalk Repair - 530 EDINBURGH ST	EDINBURGH ST	PERSIA AVE	11
Concrete Curb/Sidewalk Repair - 668 LISBON ST	LISBON ST	FRANCE AVE	11
Concrete Curb/Sidewalk Repair - 16 CAMELLIA AVE	CAMELLIA AVE	ADMIRAL AVE	11
Concrete Curb/Sidewalk Repair - 1915 SAN JOSE AVE	SAN JOSE AVE	HAVELOCK ST	11
Concrete Curb/Sidewalk Repair - 900 MOSCOW ST	MOSCOW ST	AMAZON AVE	11
Concrete Curb/Sidewalk Repair - 70 LEE AVE	LEE AVE	LAKEVIEW AVE \ SUMMIT ST	11
Concrete Curb/Sidewalk Repair - 415 HURON AVE	HURON AVE	OTTAWA AVE	11
Concrete Curb/Sidewalk Repair - 71 LIEBIG ST	LIEBIG ST	LESSING ST	11
Concrete Curb/Sidewalk Repair - 101 POPE ST	POPE ST	CROSS ST	11
Concrete Curb/Sidewalk Repair - 101 ASHTON AVE	ASHTON AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 272 ONEIDA AVE	ONEIDA AVE	OTSEGO AVE	11
Concrete Curb/Sidewalk Repair - 519 EDINBURGH ST	EDINBURGH ST	PERSIA AVE	11
Concrete Curb/Sidewalk Repair - 255 POPE ST	POPE ST	MORSE ST	11
Concrete Curb/Sidewalk Repair - 118 SANTA YSABEL AVE	SANTA YSABEL AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 129 GRANADA AVE	GRANADA AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 1584 ALEMANY BLVD	ALEMANY BLVD	COTTER ST	11
Concrete Curb/Sidewalk Repair - 235 FARALLONES ST	FARALLONES ST	CAPITOL AVE	11
Concrete Curb/Sidewalk Repair - 101 GRAFTON AVE	GRAFTON AVE	LEE AVE	11
Concrete Curb/Sidewalk Repair - 159 HAROLD AVE	HAROLD AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 218 NEY ST	NEY ST	CONGDON ST	11
Concrete Curb/Sidewalk Repair - 155 GRANADA AVE	GRANADA AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 4610 MISSION ST	MISSION ST	NORTON ST	11
Concrete Curb/Sidewalk Repair - 647 GENEVA AVE	GENEVA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 700 DELANO AVE	DELANO AVE	GENEVA AVE	11
Concrete Curb/Sidewalk Repair - 701 ATHENS ST	ATHENS ST	FRANCE AVE	11
Concrete Curb/Sidewalk Repair - 201 OCEAN AVE	OCEAN AVE	MEDA AVE \ OTSEGO AVE	11
Concrete Curb/Sidewalk Repair - 217 THERESA ST	THERESA ST	CAYUGA AVE	11
Concrete Curb/Sidewalk Repair - 235 CAPITOL AVE	CAPITOL AVE	SADOWA ST	11
Concrete Curb/Sidewalk Repair - 1801 SAN JOSE AVE	SAN JOSE AVE	SANTA ROSA AVE	11
Concrete Curb/Sidewalk Repair - 1707 SAN JOSE AVE	SAN JOSE AVE	COTTER ST	11
Concrete Curb/Sidewalk Repair - 25 ACTON ST	ACTON ST	MISSION ST \ SICKLES AVE	11
Concrete Curb/Sidewalk Repair - 2377 SAN JOSE AVE	SAN JOSE AVE	GENEVA AVE	11
Concrete Curb/Sidewalk Repair -	CROSS ST	POPE ST	11
Concrete Curb/Sidewalk Repair - 242 ALLISON ST	ALLISON ST	MORSE ST	11
Concrete Curb/Sidewalk Repair - 125 ALLISON ST	ALLISON ST	CROSS ST	11
Concrete Curb/Sidewalk Repair - 26 CROSS ST	CROSS ST	POPE ST	11
Concrete Curb/Sidewalk Repair - 270 FARALLONES ST	FARALLONES ST	CAPITOL AVE	11
Concrete Curb/Sidewalk Repair - 33 POPE ST	POPE ST	HOLLYWOOD CT	11
Concrete Curb/Sidewalk Repair - 314 VICTORIA ST	VICTORIA ST	SARGENT ST	11
Concrete Curb/Sidewalk Repair - 1050 CAPITOL AVE	CAPITOL AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 143 HAROLD AVE	HAROLD AVE	GRAFTON AVE	11
Concrete Curb/Sidewalk Repair - 69 OLIVER ST	OLIVER ST	MISSION ST	11
Concrete Curb/Sidewalk Repair - 155 MORSE ST	MORSE ST	UNNAMED 071	11

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 1780 SAN JOSE AVE	SAN JOSE AVE	PILGRIM AVE	11
Concrete Curb/Sidewalk Repair - 54 HAVELOCK ST	HAVELOCK ST	SAN JOSE AVE	11
Concrete Curb/Sidewalk Repair - 85 RESTANI WAY	RESTANI WAY	RESTANI STWY	11
Concrete Curb/Sidewalk Repair - 99 CURTIS ST	CURTIS ST	ROLPH ST	11
Concrete Curb/Sidewalk Repair - 504 MUNICH ST	MUNICH ST	RUSSIA AVE	11
Concrete Curb/Sidewalk Repair -	ALEMANY BLVD	SICKLES AVE	11
Concrete Curb/Sidewalk Repair - 6 POPE ST	POPE ST	MISSION ST	11
Concrete Curb/Sidewalk Repair - 2710 ALEMANY BLVD	ALEMANY BLVD	NAGLEE AVE	11
Concrete Curb/Sidewalk Repair - 2 MADRID ST	MADRID ST	SILVER AVE	11
Concrete Curb/Sidewalk Repair - 5145 MISSION ST	MISSION ST	AMAZON AVE	11
Concrete Curb/Sidewalk Repair - 4600 MISSION ST	MISSION ST	NORTON ST	11
Concrete Curb/Sidewalk Repair - 144 SANTA YNEZ AVE	SANTA YNEZ AVE	OTSEGO AVE	11
Concrete Curb/Sidewalk Repair -	RALSTON ST	VERNON ST	11
Concrete Curb/Sidewalk Repair - 1112 PRAGUE ST	PRAGUE ST	CURTIS ST	11
Concrete Curb/Sidewalk Repair - 1118 PRAGUE ST	PRAGUE ST	CURTIS ST	11
Concrete Curb/Sidewalk Repair - 279 FAXON AVE	FAXON AVE	LAKEVIEW AVE	11
Concrete Curb/Sidewalk Repair - 1970 ALEMANY BLVD	ALEMANY BLVD	ONONDAGA AVE	11
Concrete Curb/Sidewalk Repair - 116 BROAD ST	BROAD ST	PLYMOUTH AVE	11
Concrete Curb/Sidewalk Repair - 358 OCEAN AVE	OCEAN AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 690 CAYUGA AVE	CAYUGA AVE	COTTER ST	11
Concrete Curb/Sidewalk Repair - 4100 MISSION ST	MISSION ST	TRUMBULL ST	11
Concrete Curb/Sidewalk Repair - 120 SENECA AVE	SENECA AVE	ALEMANY BLVD	11
Concrete Curb/Sidewalk Repair - 185 ALLISON ST	ALLISON ST	CROSS ST	11
Concrete Curb/Sidewalk Repair - 195 ALLISON ST	ALLISON ST	CROSS ST	11
Concrete Curb/Sidewalk Repair - 647 GENEVA AVE	GENEVA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 379 CAPITOL AVE	CAPITOL AVE	BROAD ST	11
Concrete Curb/Sidewalk Repair - 80 LAURA ST	LAURA ST	MISSION ST	11
Concrete Curb/Sidewalk Repair - 451 HURON AVE	HURON AVE	SALA TER	11
Concrete Curb/Sidewalk Repair - 322 VICTORIA ST	VICTORIA ST	SARGENT ST	11
Concrete Curb/Sidewalk Repair - 398 ELLINGTON AVE	ELLINGTON AVE	DICHIERA CT	11
Concrete Curb/Sidewalk Repair - 339 MOSCOW ST	MOSCOW ST	EXCELSIOR AVE	11
Concrete Curb/Sidewalk Repair - 62 SANTA ROSA AVE	SANTA ROSA AVE	MISSION ST	11
Concrete Curb/Sidewalk Repair - 4085 MISSION ST	MISSION ST	BOSWORTH ST \ MURRAY ST	11
Concrete Curb/Sidewalk Repair - 285 FAXON AVE	FAXON AVE	LAKEVIEW AVE	11
Concrete Curb/Sidewalk Repair - 500 VICTORIA ST	VICTORIA ST	GARFIELD ST	11
Concrete Curb/Sidewalk Repair - 2275 SAN JOSE AVE	SAN JOSE AVE	SENECA AVE	11
Concrete Curb/Sidewalk Repair - 371 SILVER AVE	SILVER AVE	MISSION ST	11
Concrete Curb/Sidewalk Repair - 1 NAHUA AVE	NAHUA AVE	DELANO AVE	11
Concrete Curb/Sidewalk Repair - 949 DELANO AVE	DELANO AVE	NAHUA AVE	11
Concrete Curb/Sidewalk Repair - 207 RALSTON ST	RALSTON ST	SARGENT ST	11
Concrete Curb/Sidewalk Repair - 101 OTSEGO AVE	OTSEGO AVE	SAN JUAN AVE	11
Concrete Curb/Sidewalk Repair - 166 FOOTE AVE	FOOTE AVE	ELLINGTON AVE	11
Concrete Curb/Sidewalk Repair - 217 MINERVA ST	MINERVA ST	CAPITOL AVE	11
Concrete Curb/Sidewalk Repair - 2377 SAN JOSE AVE	SAN JOSE AVE	GENEVA AVE	11
Concrete Curb/Sidewalk Repair - 254 FAXON AVE	FAXON AVE	LAKEVIEW AVE	11
Concrete Curb/Sidewalk Repair - 900 HURON AVE	HURON AVE	LAWRENCE AVE	11
Concrete Curb/Sidewalk Repair - 39 LESSING ST	LESSING ST	LIEBIG ST	11
Concrete Curb/Sidewalk Repair - 563 EDINBURGH ST	EDINBURGH ST	PERSIA AVE	11
Concrete Curb/Sidewalk Repair - 771 MADRID ST	MADRID ST	FRANCE AVE	11
Concrete Curb/Sidewalk Repair - 167 NAPLES ST	NAPLES ST	PERU AVE	11
Concrete Curb/Sidewalk Repair - 0101 BROAD ST	BROAD ST	PLYMOUTH AVE	11
Concrete Curb/Sidewalk Repair - 78 EDGAR AVE	EDGAR AVE	NIAGARA AVE	11
Concrete Curb/Sidewalk Repair - 218 ARCH ST	ARCH ST	RANDOLPH ST	11
Concrete Curb/Sidewalk Repair - 230 GARFIELD ST	GARFIELD ST	HEAD ST	11
Concrete Curb/Sidewalk Repair - 293 MONTANA ST	MONTANA ST	FAXON AVE	11
Concrete Curb/Sidewalk Repair - 1707 SAN JOSE AVE	SAN JOSE AVE	COTTER ST	11
Concrete Curb/Sidewalk Repair - 1770 SAN JOSE AVE	SAN JOSE AVE	BADEN ST	11
Concrete Curb/Sidewalk Repair - 1826 SAN JOSE AVE	SAN JOSE AVE	COLONIAL WAY	11

List of Outstanding Sidewalk and Curb Repairs by District as of 3/22/2024

83

Description	On Street	From Street	District
Concrete Curb/Sidewalk Repair - 265 MONTANA ST	MONTANA ST	FAXON AVE	11
Concrete Curb/Sidewalk Repair - 43 WANDA ST	WANDA ST	OCEAN AVE	11

[this page intentionally left blank]

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Traffic Signs and Signals Maintenance
Current PROP L Request:	\$1,758,637
Supervisory Districts	District 07, District 08, District 09

REQUEST

Brief Project Description

Requested Prop L funds along with \$301,363 in Prop K cost savings, would be used to construct traffic-signal related upgrades at five locations on Folsom Street and 19th, 21st, 22nd and 23rd streets, and at Gough/Haight/Market streets. Upgrades include new pedestrian signals, new accessible pedestrian signals, new higher-visibility 12-inch traffic signals on mast arms, curb ramps, and replacement of old/damaged signal infrastructure.

Detailed Scope, Project Benefits and Community Outreach

In December 2022, the Transportation Authority allocated \$2,376,909 in Prop K funds to the SFMTA for the Traffic Signal Upgrade Contract 36 project. The original scope of work includes the construction phase of traffic-signal related upgrades at 14 locations across the City. These upgrades include new pedestrian signals (PCS), new accessible pedestrian signals (APS), new higher-visibility 12-inch traffic signals on mast arms, new left turn signals, curb ramps, and replacement of old/damaged signal infrastructure. Twelve of the intersections are located on the Vision Zero High Injury Network, which encompasses the pedestrian, bicycle, and vehicle high injury corridors. These signal upgrades will improve accessibility and safety for all. Construction for Contract 36 started in early April 2024.

SFMTA requests \$1,758,637 in Prop L funds for five additional signal upgrade locations to be constructed through Contract 36. SFMTA will add these five locations through a change order to the Contract 36 construction contract in order to expedite delivery and avoid the potential loss of Affordable Housing Sustainable Communities (AHSC) grant funds for signal upgrades at four locations on Folsom Street at 19th, 21st, 22nd and 23rd streets, and to address continuing right-angle collisions occurring at Gough/Haight Street/Market streets.

Signal upgrades at all five locations were designed with Prop K funds allocated to the Contract 35 project. The Prop L Traffic Sign and Signal Maintenance 5YPP includes \$7,104,000 in funds programmed for the construction phase of Contract 35, including the five locations that are the subject of this request. The SFMTA expects to advertise the construction contract for Contract 35 in early 2025. Based on the latest project schedule for Contract 35, the Folsom locations would not be

86

completed to meet the timely use of funds required by the AHSC grant. The SFMTA is requesting a 5YPP amendment to reprogram funds from Contract 35 to Contract 36 construction to fully fund this request. SFMTA has also requested amendment of the prior Contract 34 allocation to allow \$301,363 in cost savings to be used to help fund the five additional locations.

Project Location

See attached scope list and map for change order locations.

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Greater than Programmed Amount

Justification for Necessary Amendment

This request includes an amendment to the Prop L Traffic Sign and Signal Maintenance 5YPP to reprogram \$1,758,637 from Traffic Signal Upgrade Contract 35 to the subject project. The SFMTA is requesting Prop L funds to expedite delivery of traffic signal upgrades at five locations that have funds programmed in Contract 35, by delivering the scope through Contract 36, which is proceeding prior to Contract 35 construction.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)	Jul-Aug-Sep	2020	Jul-Aug-Sep	2021
Right of Way				
Design Engineering (PS&E)	Apr-May-Jun	2020	Jan-Feb-Mar	2023
Advertise Construction	Apr-May-Jun	2023		
Start Construction (e.g. Award Contract)	Oct-Nov-Dec	2023		
Operations (OP)				
Open for Use			Jul-Aug-Sep	2025
Project Completion (means last eligible expenditure)			Jul-Aug-Sep	2025

SCHEDULE DETAILS

Based on the Affordable Housing Sustainable Communities (AHSC) grant deadlines of construction completion by June 30, 2025 and funds must be spent by December 31, 2025, the open for use goal is summer 2025 for the signal upgrades at Folsom Street and 19th Street, Folsom Street and 21st Street, Folsom Street and 22nd Street, Folsom Street and 23rd Street. The change order work to Contract 36 is expected to be presented at the San Francisco Public Works Commission on July 22, 2024.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-217: Traffic Signs and Signals Maintenance	\$1,758,637	\$0	\$0	\$1,758,637
Affordable Housing Community Grant (AHSC)	\$0	\$0	\$1,200,000	\$1,200,000
Prop K	\$0	\$0	\$301,363	\$301,363
Phases In Current Request Total:	\$1,758,637	\$0	\$1,501,363	\$3,260,000

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$0		
Construction	\$3,260,000	\$1,758,637	Engineer's Estimate at 100% design
Operations	\$0		
Total:	\$3,260,000	\$1,758,637	

% Complete of Design:	100.0%
As of Date:	04/15/2024
Expected Useful Life:	30 Years

San Francisco County Transportation Authority
Prop L Allocation Request Form for Additional Locations in Contract 36

Budget Line Item	Totals	% of contract	SFPW	SFMTA	Contractor
1. Contract					
Task 1: Curb Ramps	\$734,628				\$734,628
Task 2: Signals /Mountings	\$237,100				\$237,100
Task 3: Poles	\$176,500				\$176,500
Task 4: Pullboxes/Conduits	\$285,910				\$285,910
Task 5: Wiring	\$97,000				\$97,000
Task 6: Traffic Routing	\$132,000				\$132,000
Task 7: Misc **	\$243,680				\$243,680
Contract Subtotal	\$1,906,818				\$1,906,818
2. SFMTA-Provided Materials					
Controller Cabinet	\$150,000			\$150,000	
Accessible Ped Signals	\$75,000			\$75,000	
Ped Countdown Modules	\$7,500			\$7,500	
Materials Subtotal	\$232,500	12.19%		\$232,500	
3. Construction Management/ Support					
Construction Engineering	\$700,000	36.71%	\$450,000	\$250,000	
Signal Shop	\$150,000			\$150,000	
Paint Shop	\$62,000			\$62,000	
Sign Shop	\$15,000			\$15,000	
Meter Shop	\$2,500			\$2,500	
Labor Subtotal	\$929,500	48.75%	\$450,000	\$479,500	
4. Other Direct Costs *	\$500	0.03%			
5. Contract Contingency	\$190,682	10.00%			
TOTAL CONSTRUCTION PHASE	\$3,260,000		\$450,000	\$712,000	\$1,906,818

* City Attorney Review,

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$1,758,637	Total PROP L Recommended	\$1,758,637

SGA Project Number:		Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	09/30/2026
Phase:	Construction	Fundshare:	52.79%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2025/26	FY2026/27	Total
PROP L EP-217	\$879,319	\$879,318	\$1,758,637

Deliverables

1. Quarterly progress reports shall provide the percent complete for each location and the percent complete for the overall project, in addition to all other requirements described in the Standard Grant Agreement (SGA). Over the course of the project quarterly progress reports should include 2-3 photos of work in progress for recent activities and of completed work. See SGA for details.

Special Conditions

1. The recommended allocation is contingent upon an amendment of the Traffic Signs and Signals Maintenance 5YPP to reprogram \$1,758,637 in funds from Traffic Signal Upgrade Contract 35 to Traffic Signal Upgrade Contract 36 - Additional Funds. See attached 5YPP amendment for details.
2. The recommended allocation is also contingent upon an amendment to the Prop K Traffic Signal Upgrade Contract 34 - Additional Funds project (133-907074) to allow SFMTA to use \$301,363 in remaining Prop K funds for the Traffic Signal Upgrade Contract 36 - Additional Funds project. Contract 34 construction was completed under budget; thus, we are recommending applying cost savings toward construction of additional signal upgrades.
3. Reimbursement of funds is conditioned upon SFMTA providing evidence of completion of design (e.g. copy of certifications page).

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	46.05%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	46.05%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Traffic Signal Upgrade Contract 36 - Additional Funds
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$1,758,637
--------------------------------	-------------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

ML

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Geraldine De Leon	Joel C Goldberg
Title:	Lead Engineer	Grants Procurement Manager
Phone:	(415) 701-4675	555-5555
Email:	geraldine.deleon@sfmta.com	joel.goldberg@sfmta.com

Table 1 - Contract 36 Change Order Locations

#	Intersection	Vision Zero High Injury Network	Equity Priority Location	PCS upgrades planned	New APS	Signal Visibility Upgrades	Muni Lines	Supervisor District
1	19th Street and Folsom Street	Yes	-	Add PCS for crossing 19th St	Yes	Yes	12	9
2	21st Street and Folsom Street	Yes	-	Add PCS for crossing 21st St	Yes	Yes	12	9
3	22nd Street and Folsom Street	Yes	-	Add PCS for all crosswalks	Yes	Yes	12	9
4	23rd Street and Folsom Street	-	Yes	Add PCS for crossing 23rd St	Yes	Yes	12	9
5	Gough Street, Haight Street, and Market Street	Yes	Yes	Existing	Existing	Yes	F, 6, 7	7,8


Table 2 - Project Locations for Traffic Signal Upgrade Contract 36 - Original Scope

#	Street 1	Street 2	Vision Zero High Injury Network	Pedestrian Countdown Signal Upgrades Planned	Accessible Pedestrian Signal Upgrades Planned	Signal Visibility Upgrades	Other improvement	Muni Lines	Supervisor District
1	4th Street	Howard	YES	-	-	-	Upgrade damaged signal infrastructure.	8,30,45	6
2	17th Street	Folsom	YES	YES	YES	YES	-	12	9
3	3rd Street	Carroll	YES	-	-	-	Replace and relocate pole damaged by collision	T	10
4	9th Street	Bryant	YES	-	YES	YES	Corner sidewalk extensions for pedestrian safety	27	6
5	10th Street	Bryant	YES	-	YES	YES	Corner sidewalk extensions for pedestrian safety, open closed crosswalk	27	6
6	7th Avenue	Kirkham	YES	YES	YES	YES	-	-	7
7	Essex	Harrison	YES	-	-	YES	-	12	6
8	Jones	Pine	YES	-	YES	YES	New left turn signals to improve safety	-	3
9	Pine	Taylor	YES	-	YES	YES	New left turn signals to improve safety	-	3
10	Bush	Taylor	YES	-	YES	YES	-	-	3
11	20th Street	Dolores	-	YES	YES	YES	-	-	8
12	Stanyan	Turk	YES	YES	YES	YES	-	31	1
13	California	Presidio	-	YES	YES	YES	-	1,2,3,43	2
14	9th Street	Brannan	YES	-	YES	YES	Relocate left turn signals to improve visibility	-	6

94 Map 1 - Traffic Signal Upgrade Contract 36 - Change Order Locations

Project Locations


1. 19th Street & Folsom Street
2. 21st Street & Folsom Street
3. 22nd Street & Folsom Street
4. 23rd Street & Folsom Street
5. Gough Street, Haight Street, & Market

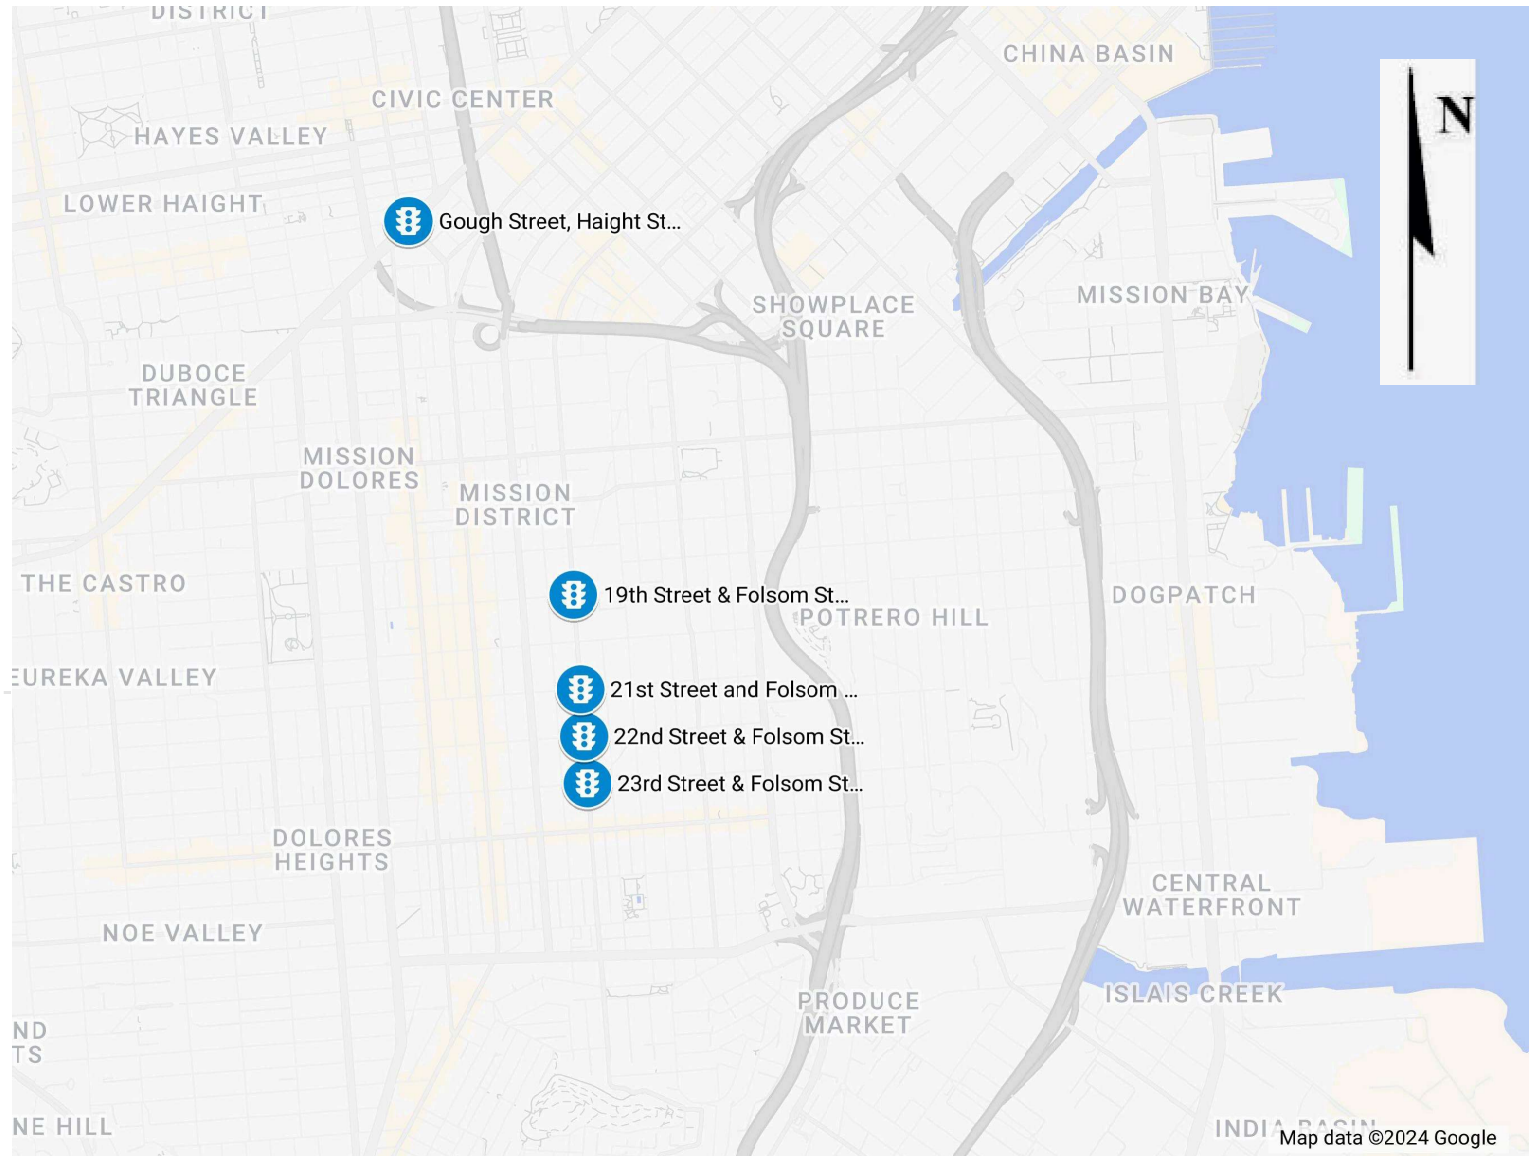

Map 2 - Traffic Signal Upgrade Contract 36 Locations - Original Scope

Project Locations

1. 4th St & Howard
2. 17th St & Folsom
3. 3rd St & Carroll
4. 9th St & Bryant
5. 10th St & Bryant
6. 7th Av & Kirkham
7. Essex & Harrison
8. Jones & Pine
9. Pine & Taylor
10. Bush & Taylor
11. 20th St & Dolores
12. Stanyan & Turk
13. California & Presidio
14. 9th St & Brannan

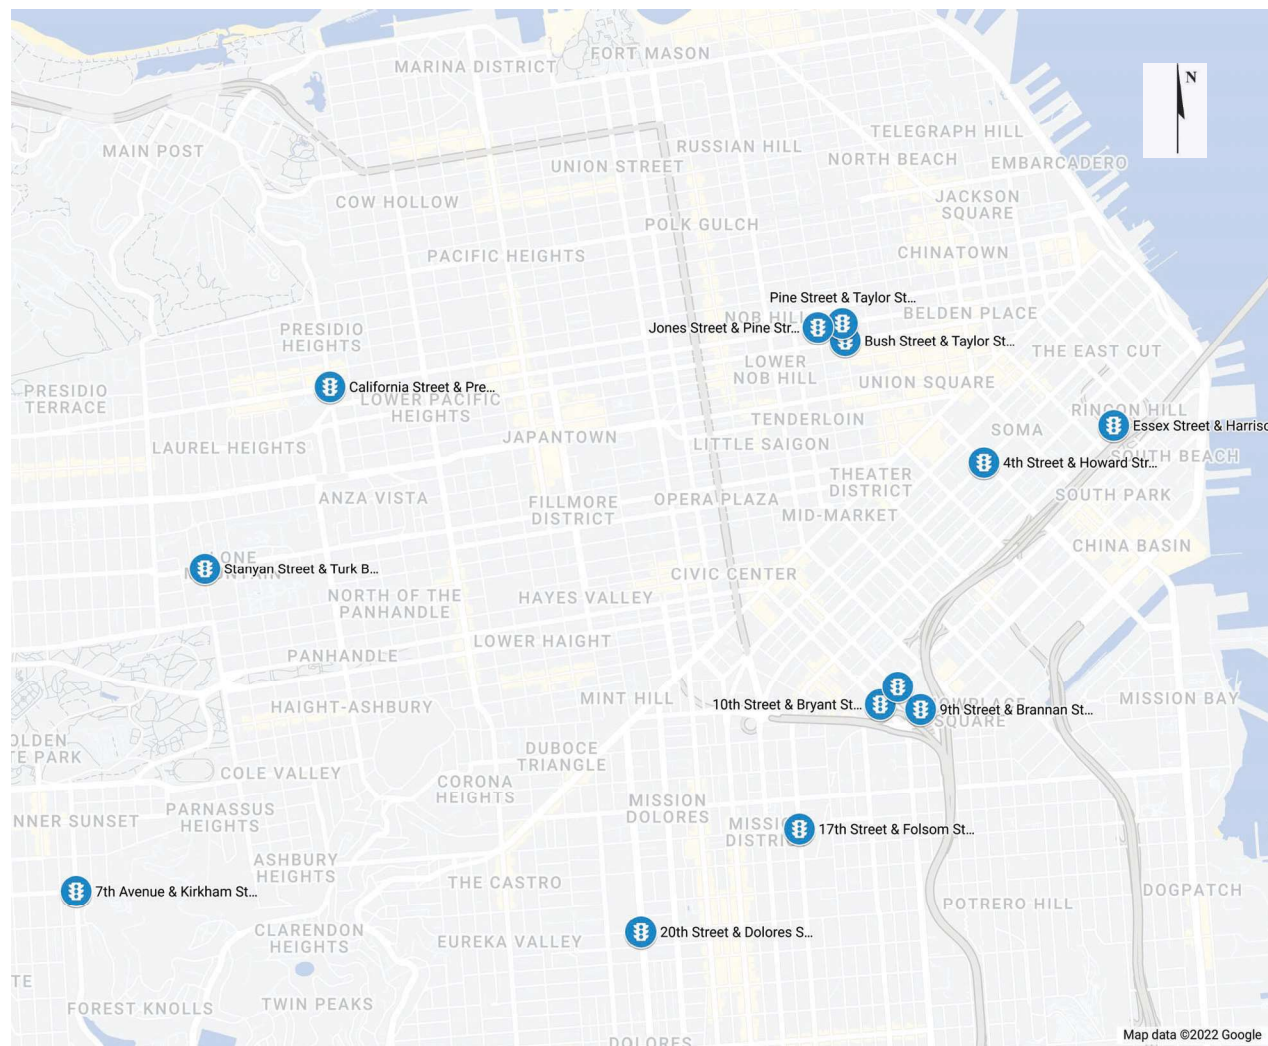

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Traffic Signs and Signals Maintenance (EP 17)
 Programming and Allocations to Date
 Pending June 2024 Board

Agency	Project Name	Phase	Status	Fiscal Year					Total
				2023/24	2024/25	2025/26	2026/27	2027/28	
SFMTA	Bus Transit Signal Priority	CON	Programmed		\$1,149,000				\$1,149,000
SFMTA	Bus Transit Signal Priority	CON	Programmed			\$1,099,000			\$1,099,000
SFMTA	Bus Transit Signal Priority	CON	Programmed				\$1,099,000		\$1,099,000
SFMTA	Bus Transit Signal Priority	CON	Programmed					\$1,099,000	\$1,099,000
SFMTA	City Coordination Opportunities: Traffic Signals Conduit Program	CON	Programmed			\$400,000			\$400,000
SFMTA	City Coordination Opportunities: Traffic Signals Conduit Program	CON	Programmed				\$400,000		\$400,000
SFMTA	City Coordination Opportunities: Traffic Signals Conduit Program	CON	Programmed					\$400,000	\$400,000
SFMTA	Great Highway Signals Upgrade	CON	Programmed	\$3,000,000					\$3,000,000
SFMTA	Tenderloin Signal Upgrade	CON	Programmed		\$2,032,000				\$2,032,000
SFMTA	Traffic Sign Replacement Program	CON	Programmed		\$405,000				\$405,000
SFMTA	Traffic Sign Replacement Program	CON	Programmed			\$405,000			\$405,000
SFMTA	Traffic Sign Replacement Program	CON	Programmed				\$405,000		\$405,000
SFMTA	Traffic Sign Replacement Program	CON	Programmed					\$405,000	\$405,000
SFMTA	Traffic Signal Hardware Replacement Program FY24	CON	Allocated	\$500,000					\$500,000
SFMTA	Traffic Signal Hardware Replacement Program FY25-28	CON	Programmed		\$500,000				\$500,000
SFMTA	Traffic Signal Hardware Replacement Program FY25-28	CON	Programmed			\$500,000			\$500,000
SFMTA	Traffic Signal Hardware Replacement Program FY25-28	CON	Programmed				\$500,000		\$500,000
SFMTA	Traffic Signal Hardware Replacement Program FY25-28	CON	Programmed					\$500,000	\$500,000
SFMTA	Traffic Signal Upgrade Contract 35	1	CON	Programmed	\$5,383,180				\$5,383,180
SFMTA	Traffic Signal Upgrade Contract 36 - Additional Funds	1	CON	Pending		\$1,720,820			\$1,720,820
SFMTA	Traffic Signal Visibility Upgrades Program FY24	CON	Allocated	\$400,000					\$400,000
SFMTA	Traffic Signal Visibility Upgrades Program FY25-28	CON	Programmed		\$400,000				\$400,000
SFMTA	Traffic Signal Visibility Upgrades Program FY25-28	CON	Programmed			\$400,000			\$400,000
SFMTA	Traffic Signal Visibility Upgrades Program FY25-28	CON	Programmed				\$400,000		\$400,000
SFMTA	Traffic Signal Visibility Upgrades Program FY25-28	CON	Programmed					\$400,000	\$400,000
SFMTA	Western Addition Area Traffic Signal Upgrades Phase 2	PS&E	Allocated	\$200,000					\$200,000
SFMTA	Western Addition Area Traffic Signal Upgrades Phase 2	CON	Programmed		\$3,389,000				\$3,389,000

Total Programmed in 2023 5YPP	\$9,483,180	\$9,595,820	\$2,804,000	\$2,804,000	\$2,804,000	\$27,491,000
Total Allocated and Pending	\$1,100,000	\$1,720,820	\$0	\$0	\$0	\$2,820,820
Total Unallocated	\$8,383,180	\$7,875,000	\$2,804,000	\$2,804,000	\$2,804,000	\$24,670,180
Total Programmed in 2023 Strategic Plan	\$11,204,000	\$7,875,000	\$2,804,000	\$2,804,000	\$2,804,000	\$27,491,000
Deobligated Funds	\$0	\$0	\$0	\$0	\$0	\$0
Cumulative Remaining Programming Capacity	\$1,720,820	\$0	\$0	\$0	\$0	\$0
Pending Allocation/Appropriation						
Board Approved Allocation/Appropriation						

FOOTNOTES:

- ¹ 5YPP amendment to accomodate allocation of \$1,720,820 for Traffic Signal Upgrade Contract 36 - Additional Funds (2024-XX, 6/25/24):
 Traffic Signal Upgrade Contract 35: Reduced from \$7,104,000 to \$5,383,180 in FY24.
 Traffic Signal Upgrade Contract 36 - Additional Funds: Added project with \$1,720,820 for construction in FY25.

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Traffic Signs and Signals Maintenance (EP 17)
 Cash Flow (Maximum Annual Reimbursement)
 Pending June 2024 Board

Project Name	Phase	Fiscal Year					Total
		2023/24	2024/25	2025/26	2026/27	2027/28	
Bus Transit Signal Priority	CON		\$1,149,000				\$1,149,000
Bus Transit Signal Priority	CON			\$1,099,000			\$1,099,000
Bus Transit Signal Priority	CON				\$1,099,000		\$1,099,000
Bus Transit Signal Priority	CON					\$1,099,000	\$1,099,000
City Coordination Opportunities: Traffic Signals Conduit Program	CON			\$50,000	\$350,000		\$400,000
City Coordination Opportunities: Traffic Signals Conduit Program	CON				\$50,000	\$350,000	\$400,000
City Coordination Opportunities: Traffic Signals Conduit Program	CON					\$50,000	\$400,000
Great Highway Signals Upgrade	CON			\$1,500,000	\$1,500,000		\$3,000,000
Tenderloin Signal Upgrade	CON			\$103,000	\$643,000	\$643,000	\$2,032,000
Traffic Sign Replacement Program	CON		\$101,000	\$304,000			\$405,000
Traffic Sign Replacement Program	CON			\$101,000	\$304,000		\$405,000
Traffic Sign Replacement Program	CON				\$101,000	\$304,000	\$405,000
Traffic Sign Replacement Program	CON					\$101,000	\$405,000
Traffic Signal Hardware Replacement Program FY24	CON	\$250,000	\$200,000	\$50,000			\$500,000
Traffic Signal Hardware Replacement Program FY25-28	CON		\$250,000	\$200,000	\$50,000		\$500,000
Traffic Signal Hardware Replacement Program FY25-28	CON			\$250,000	\$200,000	\$50,000	\$500,000
Traffic Signal Hardware Replacement Program FY25-28	CON				\$250,000	\$200,000	\$500,000
Traffic Signal Hardware Replacement Program FY25-28	CON					\$250,000	\$500,000
Traffic Signal Upgrade Contract 35	1 CON			\$1,383,180	\$4,000,000		\$5,383,180
Traffic Signal Upgrade Contract 36 - Additional Funds	1 CON			\$1,720,820			\$1,720,820
Traffic Signal Visibility Upgrades Program FY24	CON	\$200,000	\$150,000	\$50,000			\$400,000
Traffic Signal Visibility Upgrades Program FY25-28	CON		\$200,000	\$150,000	\$50,000		\$400,000
Traffic Signal Visibility Upgrades Program FY25-28	CON			\$200,000	\$150,000	\$50,000	\$400,000
Traffic Signal Visibility Upgrades Program FY25-28	CON				\$200,000	\$150,000	\$400,000
Traffic Signal Visibility Upgrades Program FY25-28	CON					\$200,000	\$400,000
Western Addition Area Traffic Signal Upgrades Phase 2	PS&E	\$100,000	\$100,000				\$200,000
Western Addition Area Traffic Signal Upgrades Phase 2	CON				\$1,800,000	\$1,589,000	\$3,389,000

Cash Flow Programmed in 2023 5YPP	\$550,000	\$2,150,000	\$7,161,000	\$10,747,000	\$5,036,000	\$27,491,000
Total Cash Flow Allocated and Pending	\$550,000	\$450,000	\$1,820,820	\$0	\$0	\$2,820,820
Total Cash Flow Unallocated	\$0	\$1,700,000	\$5,340,180	\$10,747,000	\$5,036,000	\$24,670,180
Total Cash Flow in 2023 Strategic Plan	\$550,000	\$2,150,000	\$7,161,000	\$10,747,000	\$5,036,000	\$27,491,000
Deobligated Funds	\$0	\$0	\$0	\$0	\$0	\$0
Cumulative Remaining Cash Flow Capacity	\$0	\$0	\$0	\$0	\$0	\$0
Pending Allocation/Appropriation						
Board Approved Allocation/Appropriation						

[this page intentionally left blank]

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Central Embarcadero Safety
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Safer and Complete Streets
Current PROP L Request:	\$200,000
Supervisory District	District 06

REQUEST

Brief Project Description

The Embarcadero is a busy multi-modal boulevard on the San Francisco Vision Zero High-Injury Network. Prop L would fund the design phase to extend a two-way, protected (Class IV) waterside bikeway 3 additional blocks from Folsom to Brannan, upgrade existing quick-build bikeway buffer areas between Broadway and Mission, modify traffic signals and shorten pedestrian roadway crossings at four intersections, and add a variable message sign for northbound drivers.

Detailed Scope, Project Benefits and Community Outreach

The Central Embarcadero Safety Project is the top priority for the Embarcadero Enhancement Program, a multi-agency and nearly decade-long effort to identify and implement transportation safety improvements for all users along The Embarcadero - a busy multi-modal, multi-way arterial boulevard included on the San Francisco Vision Zero High-Injury Network. SFMTA requests Prop L funds for the design phase of the project, which will also help provide a local match for a One Bay Area Grant (OBAG) award for the construction phase. The project expands upon recent quick-build implementation of a two-way, protected (Class IV) waterside bikeway from Folsom Street to Broadway by extending the bikeway south three blocks to Brannan Street where no quick-build opportunities exist. To make room for the bikeway, the project will narrow the existing northbound center medians and remove up to 24 parking spaces. The project will also enhance the physical protection of the existing bikeway (between Mission to Broadway) and add sidewalk extensions, curb ramp upgrades, and other measures for improved pedestrian safety and accessibility at the Clay, Ferry Building driveway, Harrison, and Bryant street intersections.

The project would also restrict northbound left-turns at Folsom Street to facilitate the bikeway and improve Muni operational safety and reliability for light rail vehicles exiting and entering the Market Street subway portal. As part of a commitment to Complete Streets for all users and in response to recent lane reductions, the project will also design and construct a Variable Message Sign at approximately Washington Street to support real-time wayfinding, better parking information, and special event messaging. Although the project corridor is not within an Equity Priority Community, it provides direct access to numerous regional transit providers and job centers and adjacent EPC communities such as Chinatown and Fisherman's Wharf.

Prior Community Outreach - From 2014 to 2018, the Embarcadero Enhancement project team held dozens of in-person meetings with key stakeholders including the Northeast Waterfront Advisory Group, Central Waterfront Advisory Group, Maritime Commerce Advisory Committee, Ballpark Mission Bay Transportation Committee, San Francisco Hotel Council, SF Travel, SF Tour Guide Guild, South Beach/Rincon/Mission Bay Neighborhood Association, District 3 SFMTA Working Group, Fisherman’s Wharf Community Benefit District, Fisherman’s Wharf Restaurant Association, as well as individual stakeholders such as the operators of the Ferry Building, Exploratorium, and many others. During this time, the project team also hosted five public open meetings, including three design workshops where residents, merchants, travelers, and the general public were invited to share their vision of the waterfront, desires for reconfiguring the roadway, and values relating to transportation, open space, and land use. In 2016, over 500 people attended an open house and responded to a survey to help assess bikeway alignment alternatives and other trade-offs, resulting in a conceptual design for a two-way, waterside protected bikeway adjacent to the promenade. In October of 2018, approximately 200 people attended an open house showcasing the conceptual design for the project, with 140 people completing a survey to gauge stakeholder support and priorities for the project moving forward. Additional stakeholder meetings took place throughout 2019 as the project moved into the preliminary engineering and environmental review phase and further public engagement are ongoing as projects within the three segments of the Embarcadero corridor manifest.

The Prop L design phase funding request is part of the local matching funds for OBAG 3, Prop AA, and Safe Routes to BART construction phase funding grant awards.

Project Location

The Embarcadero between Broadway and Brannan Street

Is this project in an Equity Priority Community?	No
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Design Engineering (PS&E)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$200,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Central Embarcadero Safety
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)	Jul-Aug-Sep	2013	Oct-Nov-Dec	2018
Environmental Studies (PA&ED)	Jan-Feb-Mar	2019	Jan-Feb-Mar	2022
Right of Way				
Design Engineering (PS&E)	Jul-Aug-Sep	2022	Jan-Feb-Mar	2025
Advertise Construction	Apr-May-Jun	2025		
Start Construction (e.g. Award Contract)	Oct-Nov-Dec	2025		
Operations (OP)				
Open for Use			Oct-Nov-Dec	2026
Project Completion (means last eligible expenditure)			Oct-Nov-Dec	2027

SCHEDULE DETAILS

The project will continue inter-agency and public engagement through summer 2024 in order to solidify a 65% design milestone and confirm/receive legislative approval. Concurrent with this phase, the project team has initiated conversations and review with Caltrans for NEPA environmental clearance (due to the OBAG federal funding). OBAG construction funds, currently programmed in FY26, must be obligated by 1/31/26.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Central Embarcadero Safety
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-218: Safer and Complete Streets	\$0	\$200,000	\$0	\$200,000
SFMTA Prop B	\$0	\$1,448,000	\$0	\$1,448,000
SFMTA Prop B / COVID relief	\$0	\$0	\$805,000	\$805,000
TDA Article III	\$0	\$0	\$92,000	\$92,000
Phases In Current Request Total:	\$0	\$1,648,000	\$897,000	\$2,545,000

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP AA	\$0	\$1,000,000	\$0	\$1,000,000
PROP L	\$0	\$200,000	\$0	\$200,000
FTA	\$0	\$0	\$250,000	\$250,000
OBAG	\$0	\$0	\$750,000	\$750,000
OBAG	\$0	\$6,320,000	\$0	\$6,320,000
Prop K	\$0	\$0	\$725,000	\$725,000
Safe Routes to BART	\$0	\$1,000,000	\$0	\$1,000,000
SFMTA Prop B	\$1,680,000	\$1,448,000	\$0	\$3,128,000
SFMTA Prop B / COVID relief	\$0	\$0	\$805,000	\$805,000
TDA Article III	\$0	\$0	\$92,000	\$92,000
Funding Plan for Entire Project Total:	\$1,680,000	\$9,968,000	\$2,622,000	\$14,270,000

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$1,000,000		Estimated Actuals
Environmental Studies	\$725,000		Actuals

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Right of Way	\$0		
Design Engineering	\$2,545,000	\$200,000	SFMTA/PW estimate
Construction	\$10,000,000		SFMTA/PW 35% estimate
Operations	\$0		
Total:	\$14,270,000	\$200,000	

% Complete of Design:	35.0%
As of Date:	03/20/2024
Expected Useful Life:	25 Years

**San Francisco County Transportation Authority
Prop L/Prop AA/Prop D TNC Allocation Request Form**

MAJOR LINE ITEM BUDGET - CENTRAL EMBARCADERO SAFETY PROJECT

SUMMARY BY MAJOR LINE ITEM - DESIGN		
Budget Line Item	Totals	% of phase
1. PW - Streets & Highways	\$ 360,000	14%
2. PW - Landscape	\$ 200,000	8%
3. PW - Hydraulics	\$ 225,000	9%
4. PW - Electrical	\$ 60,000	2%
5. PW - Project Management	\$ 75,000	3%
6. PW - Structural/CM support	\$ 30,000	1%
7. PW - Survey	\$ 200,000	8%
8. MTA - Streets	\$ 650,000	26%
9. MTA - CP&C	\$ 315,000	12%
10. Direct Costs/Contracts	\$ 200,000	8%
11. Contingency	\$ 230,000	9%
TOTAL PHASE	\$ 2,545,000	

TOTAL LABOR COST BY AGENCY	
SFMTA	\$ 965,000
SFPW	\$ 1,150,000
Direct Costs/Contracts	\$ 200,000
TBD	\$ 230,000
TOTAL	\$ 2,545,000

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Central Embarcadero Safety
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$200,000	Total PROP L Recommended	\$200,000

SGA Project Number:		Name:	Central Embarcadero Safety
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	09/30/2025
Phase:	Design Engineering	Fundshare:	7.86%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	Total
PROP L EP-218	\$200,000	\$200,000

Deliverables

1. Quarterly progress reports shall include % complete of the funded phase, work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, and any issues that may impact schedule, in addition to all other requirements described in the Standard Grant Agreement.
2. With the first quarterly progress report, SFMTA shall provide 2-3 photos of existing conditions.
3. Upon completion, SFMTA shall provide evidence of completion of 100% design (e.g., copy of certifications page, copy of workorder, internal design completion documentation, or similar).
4. Upon completion, SFMTA shall provide an updated scope, schedule, budget, and funding plan for construction. This deliverable may be met with an allocation request for construction.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	92.14%
Actual Leveraging - This Project	92.99%	No TNC TAX	98.6%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Central Embarcadero Safety
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$200,000
--------------------------------	-----------

1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.


Initials of sponsor staff member verifying the above statement:
ML

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Casey Hildreth	Joel C Goldberg
Title:	Transportation Planner	Grants Procurement Manager
Phone:	(415) 646-2217	555-5555
Email:	casey.hildreth@sfmta.com	joel.goldberg@sfmta.com

Central Embarcadero Safety Project

Summary Map

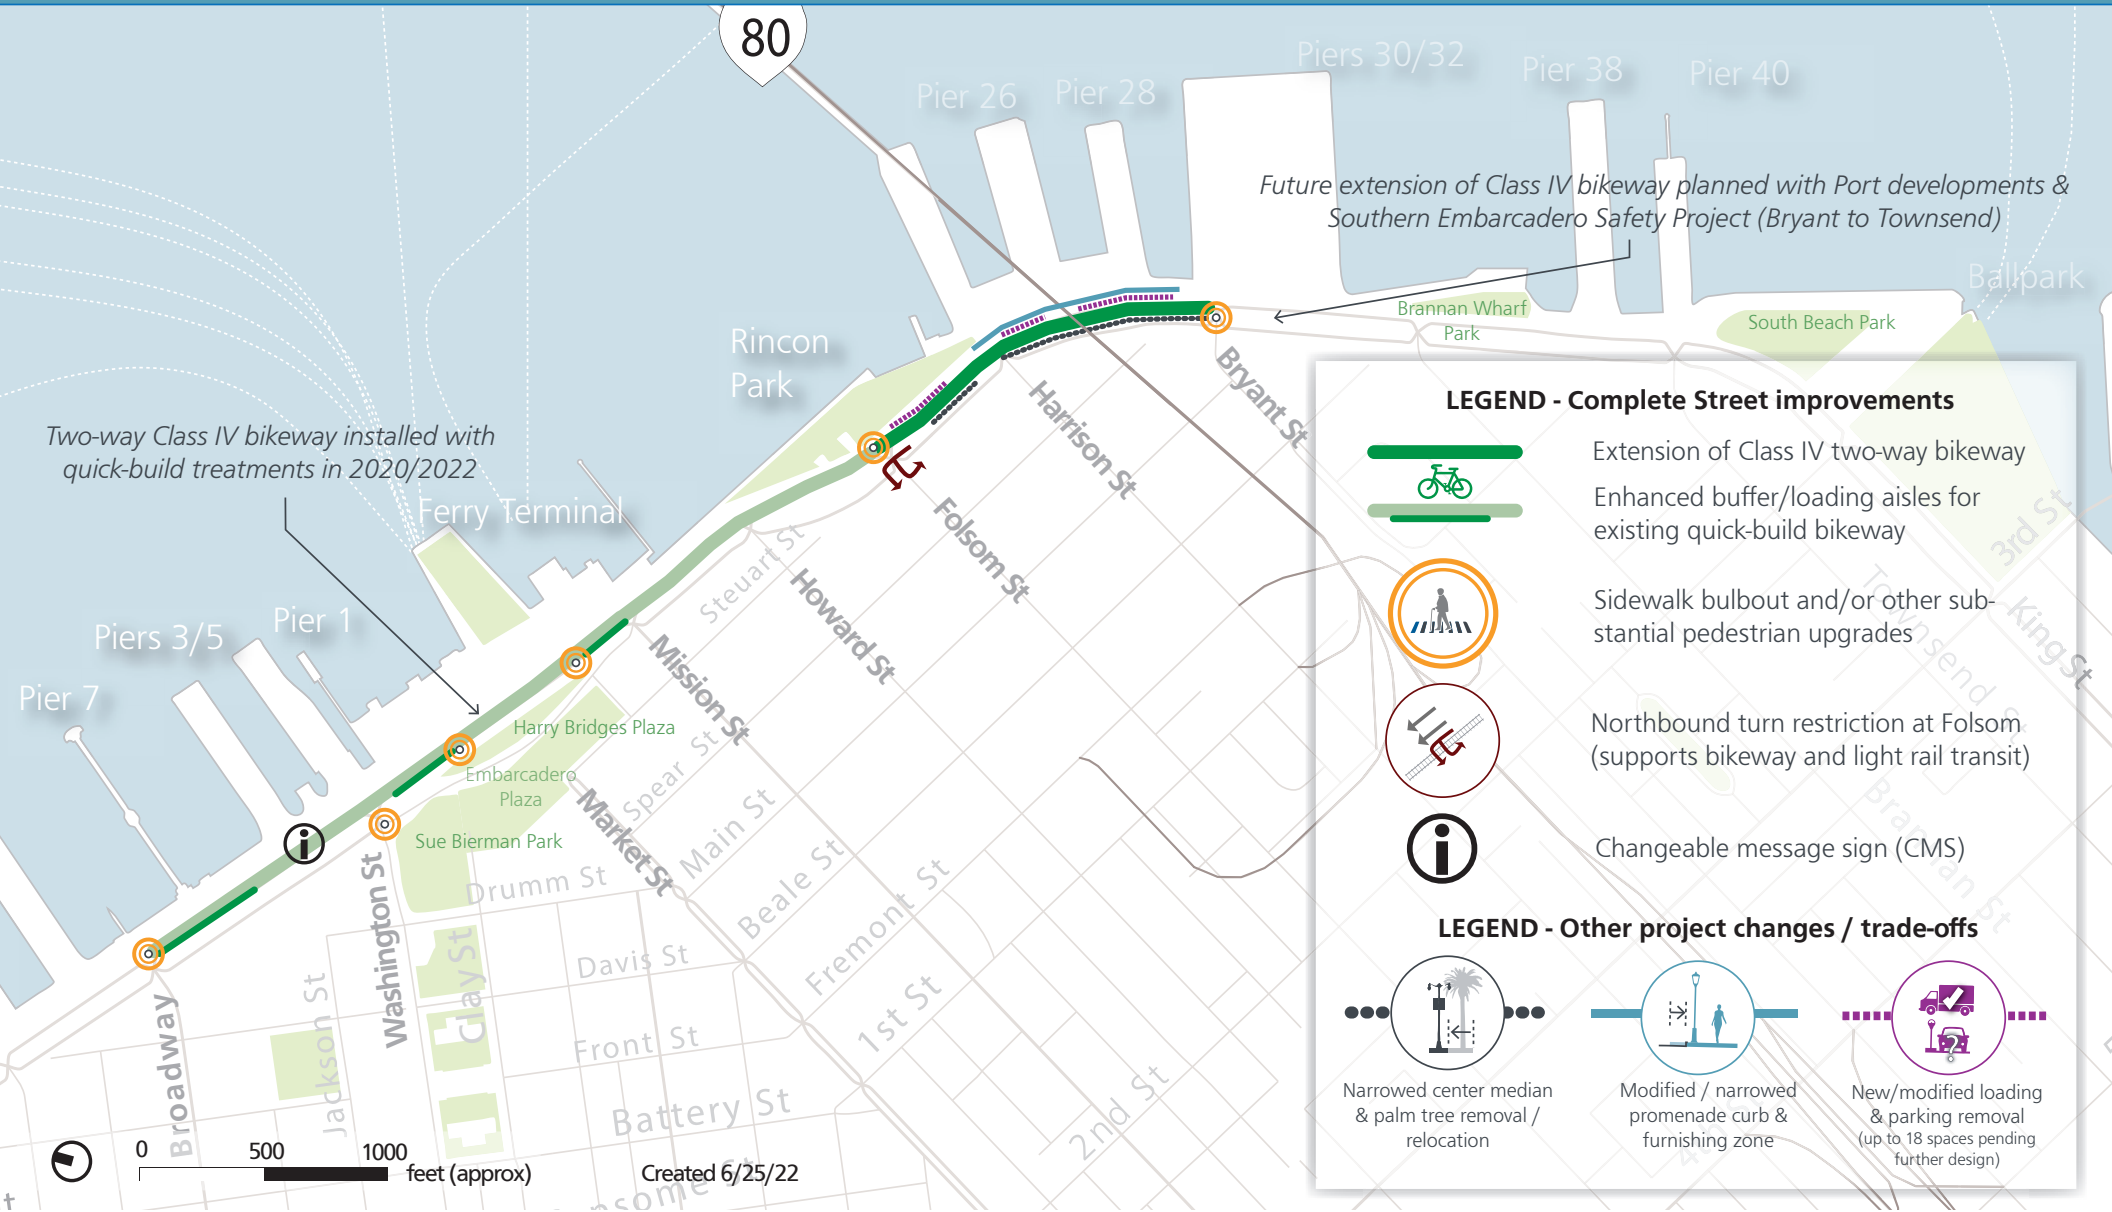


Waterfront Transportation

Attachment 2

Legend


- Major Transportation Centers
- Rapid Muni Route (10 minutes or less)
- Historic Streetcar Route
- Caltrain Route
- Dedicated Bikeways
- SF Bay Ferry & Golden Gate Ferry Landings
- Public Ferry Route
- Port Boundary
- Port Jurisdiction

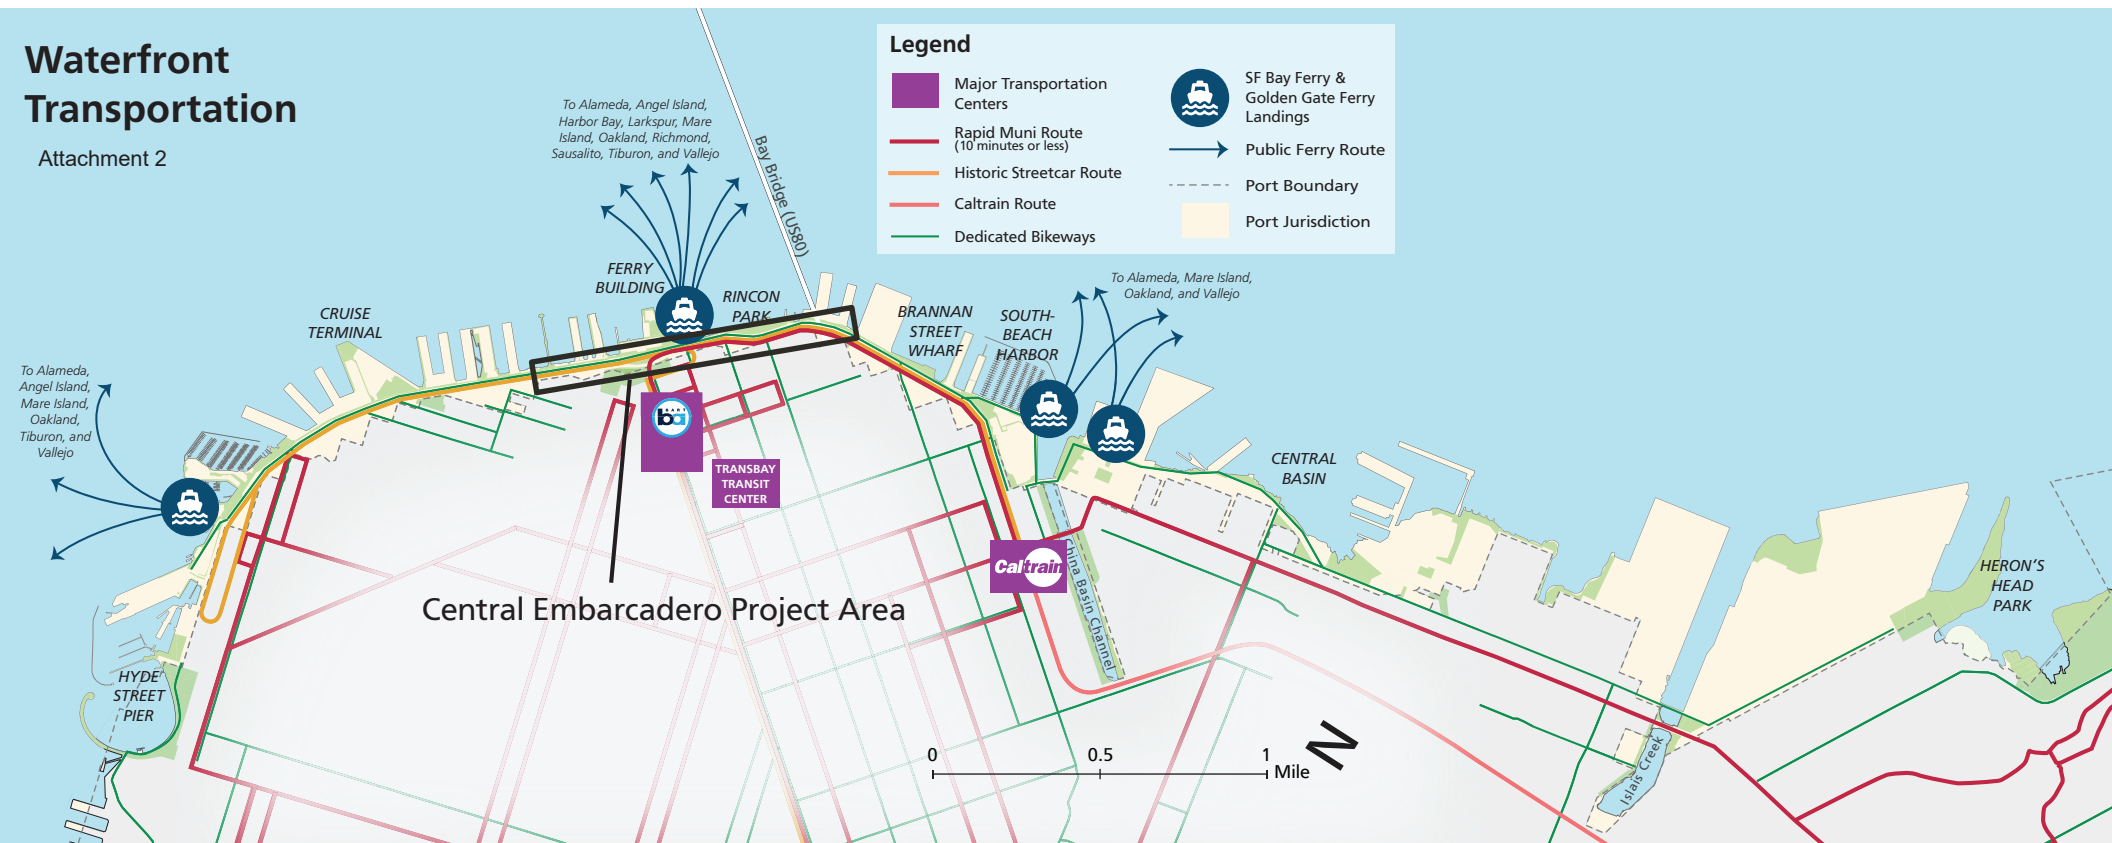


Waterfront Transportation

Legend

- Major Transportation Centers
- Rapid Muni Route (10 minutes or less)
- Historic Streetcar Route
- Caltrain Route
- Dedicated Bikeways
- SF Bay Ferry & Golden Gate Ferry Landings
- Public Ferry Route
- Port Boundary
- Port Jurisdiction

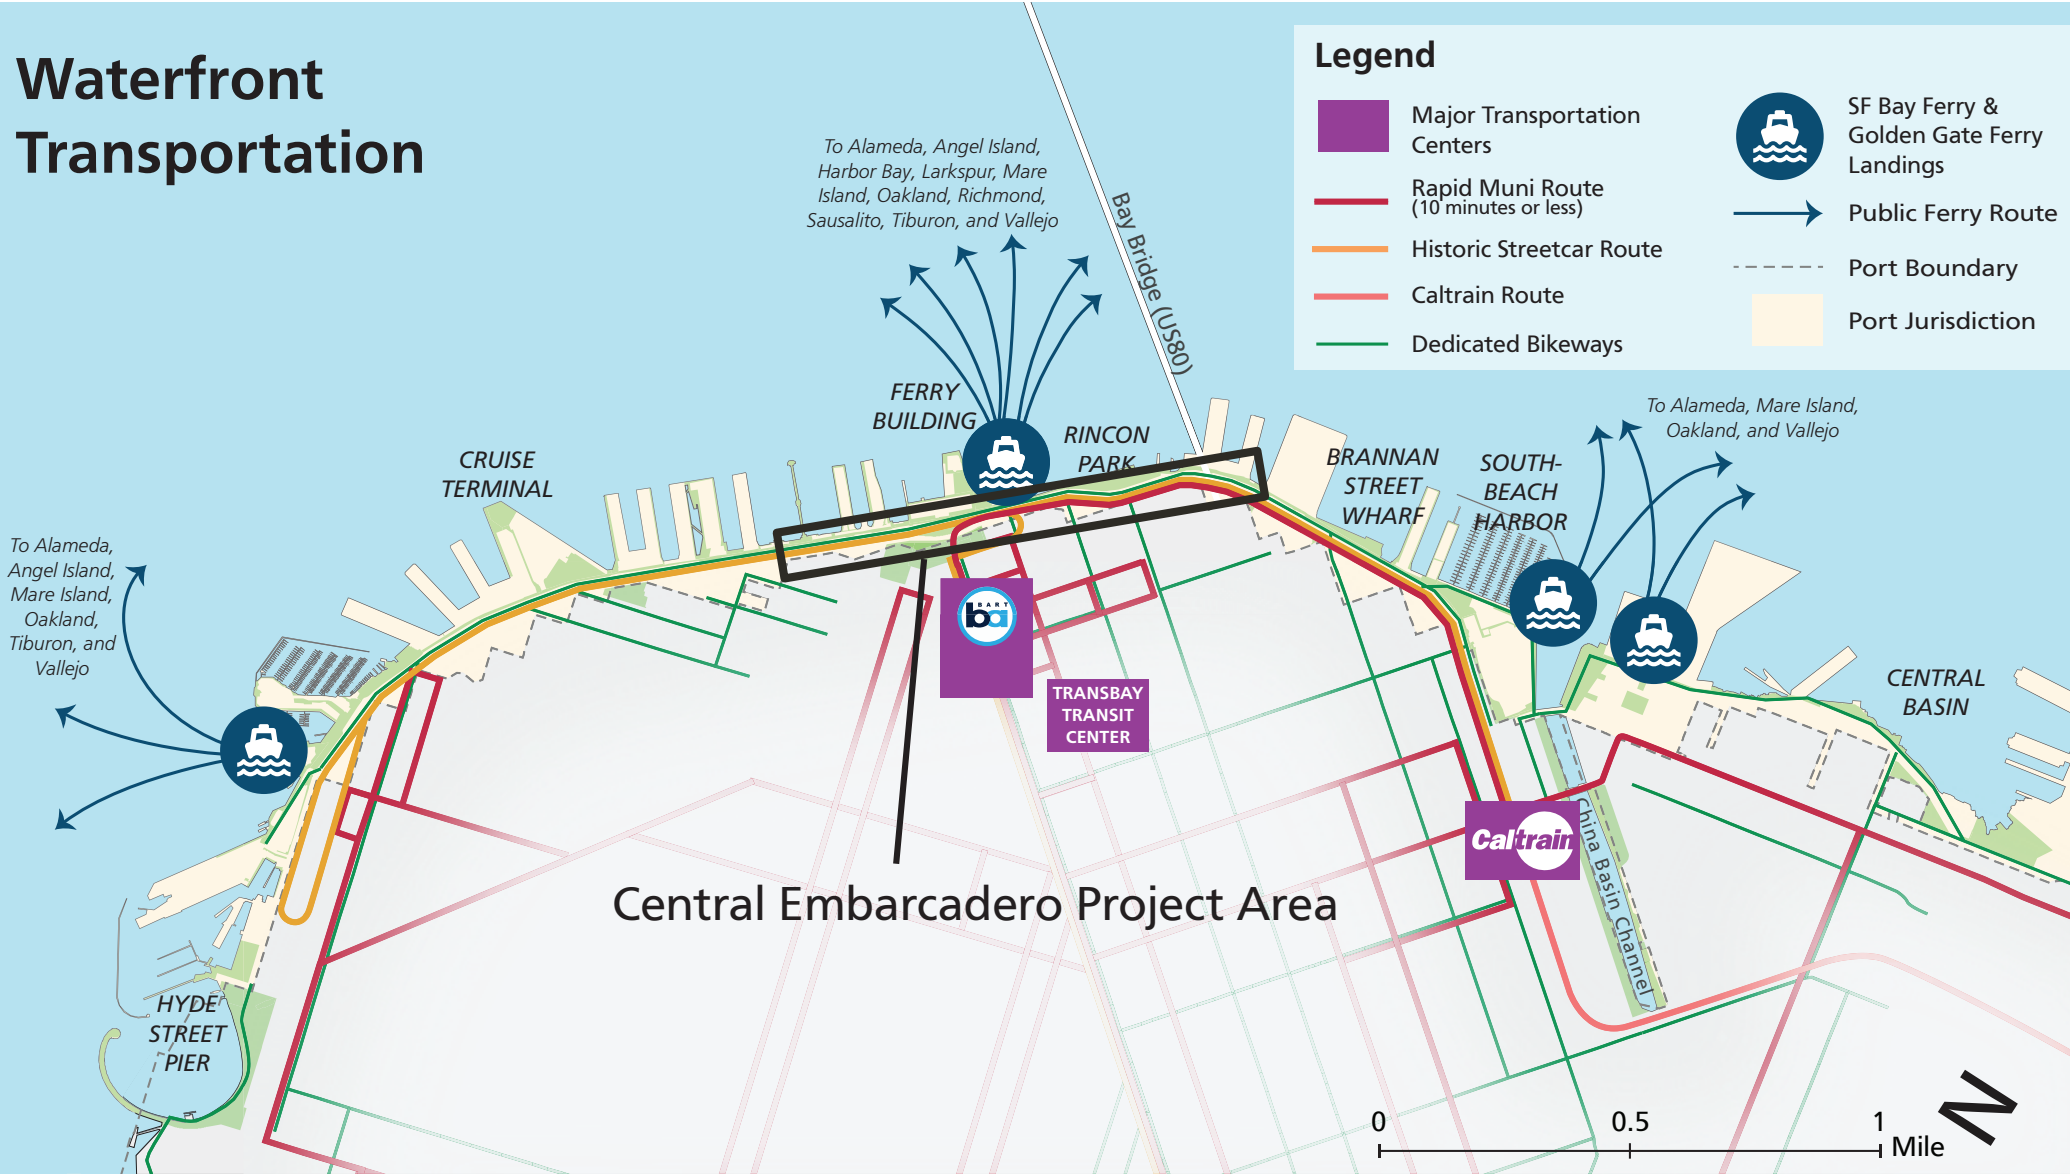

Central Embarcadero Safety Project - Protected bikeway extension concept (illustrative section)

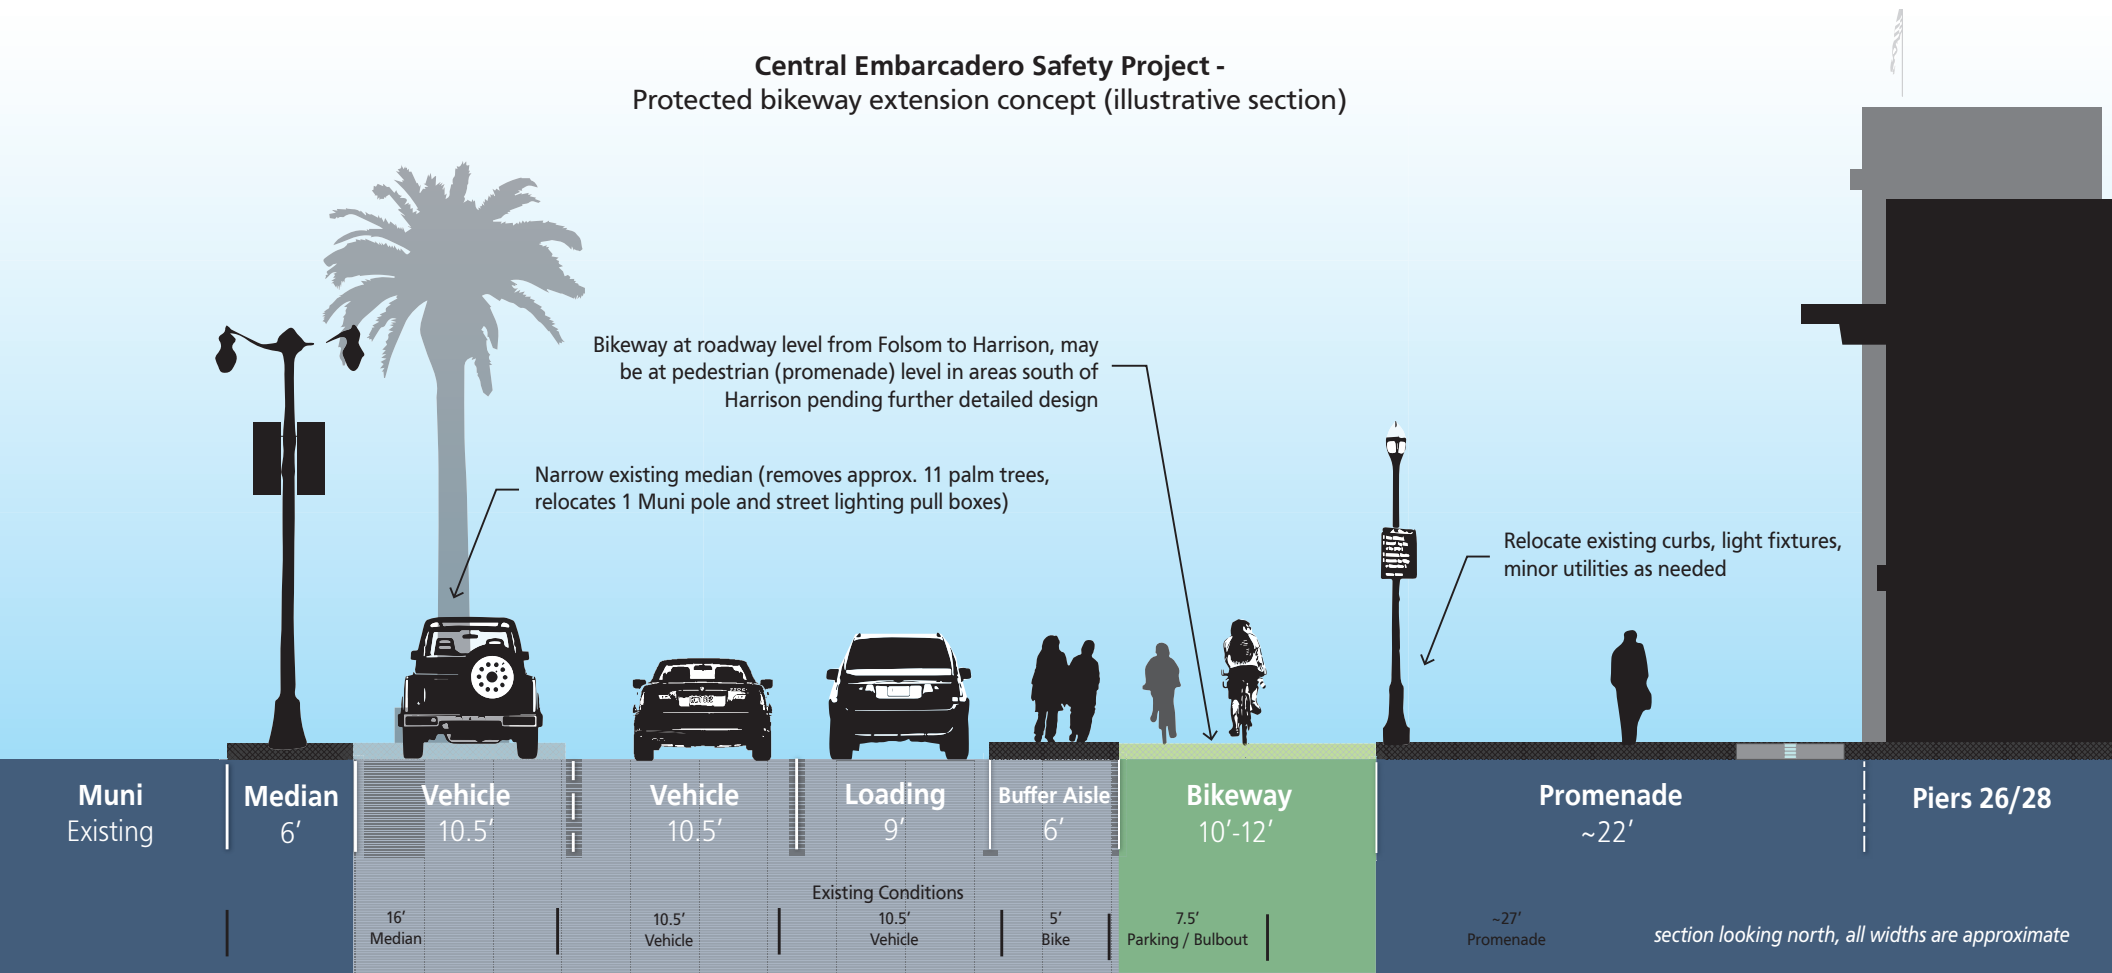

San Francisco County Transportation Authority

Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Safe Routes to School Non-Infrastructure
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Safer and Complete Streets
Current PROP L Request:	\$466,000
Supervisory District	Citywide

REQUEST

Brief Project Description

The San Francisco Safe Routes to School (SRTS) Non-Infrastructure program delivers educational, encouragement, and experiential activities aimed at decreasing commuting in single-family vehicles to San Francisco's 113 public schools, improving safety of walking and bicycling, reducing city congestion and air pollution, and inspiring the next generations of walkers, bicyclists, and transit users. Prop L funds would provide the local matching funds to the federal One Bay Area Grant 3 grant for San Francisco's SRTS Non-Infrastructure program for Fiscal Years 2023/24 and 2024/25.

Detailed Scope, Project Benefits and Community Outreach

The San Francisco Safe Routes to School Program reduces single-family vehicle trips and dependence on personal vehicles for trips made by students and their caretakers to and from schools by providing resources, organizational support, and skill-building events and activities that support walking, rolling, carpooling, and taking transit to school, as well as directly leading groups of students on regular walks and rides to school. Reducing student car-trips reduces congestion in and around school drop-off areas, reducing risk of student-vehicle collisions and car-generated pollution in school zones which is linked to negative health impacts including higher rates of asthma. Students who walk and roll to school as part of program events and activities benefit both physically and mentally from the physical activity involved, with families who participate in regular group walks and rides or adopt walking and rolling as a regular part of their school routine beyond program supported events benefitting the most. Increased physical activity in youth is linked to lower rates of childhood obesity and improved academic performance, with studies showing even single sessions of physical activity produce measurable improvements in memory and focus. Group walks to school have also been reported to reduce absenteeism and improve consistency in arriving to school on-time for walk participants.

In 2022 the SFCTA Board programmed \$7,082,400 in federal One Bay Area Grant Cycle 3 funds to the SF SRTS program for the period of FY22/23 through FY25/26. Requested Prop L funds would provide the required local match to the the federal grant for FY 23/24 and FY 24/25. SFMTA will request Prop L funds in the future for the local matching funds for FY 25/26 which is the remaining fiscal year of federal grant period.

Specific tasks to be accomplished through the Prop L grant include:

Prop L funds will provide the required local match to the federal One Bay Area Grant 3 funds for San Francisco's Safe Routes to School program. Specific tasks to be accomplished through the grant include:

- Identify and implement opportunities for in-school education related to transportation safety and choices
- Hold neighborhood skill building, encouragement, and outreach events to help reach and support parent/guardian champions, including weekend bike classes at shared schoolyards; parent-led walking school buses and bike trains; annual Walk and Roll to School, Bike and Roll to School, and Transit Day events
- Identify clusters of schools with common routes to school and connect parents and community members to joint resources for walking, bicycling, carpooling, and transit use
- Provide technical assistance and education on personal safety in school communities where real and perceived environmental hazards are barriers to families walking, biking, or taking transit to school
- Coordinate between SFUSD and SFMTA's school-serving programs to streamline communication and agency response to traffic and safety needs on and around school sites, including receiving and responding to parent and community concerns, safety assessments related to existing infrastructure, identifying needs for improvements, and engaging in ongoing planning processes
- Evaluation of program impacts on safety and mode-shift of children travelling to and from school.

Participating Schools:

The SRTS Non-Infrastructure Project will encompass SRTS efforts at all of the SFUSD elementary, middle and high schools in various capacities. Schools will be equitably prioritized based on baseline and changes in school performance related to mode shift, safety concerns and equity considerations.

Only public non-charter schools are included in the program. Private schools who reach out to the Safe Routes to School Program will be supported with resources such as how-to guides. The program also runs and participates in citywide events that private school students can attend.

Roles and Responsibilities:

- SFMTA – Program administration and oversight, strategic planning and goal setting, establishing workplans and deliverables, targeting of activities in collaboration with SFUSD and Consultant, new activity design in collaboration with Consultant, directing communication and promotion activities, overseeing program evaluation and reporting
- SFUSD – Communication and coordination with school staff, communication to students and families through school communication pathways, collaboration and support for activities held on school sites, collaboration with SFMTA and Consultant on determining activities best suited to individual schools, supporting the development and delivery of educational material on multi-modal transportation
- SFE – development and delivery of educational material on multi-modal transportation, in collaboration with SFMTA and SFUSD
- Contractor/subcontractors – Subject matter experts in bicycling, pedestrian safety, personal safety, and/or transit use. Communication and activity promotion, implementation of program activities (including annual events, bicycle classes, supervised group walks and bicycle rides, guided student field trips on Muni, and workshops on safely navigating to and from school), collecting and reporting event and activity metrics, procurement of services and materials needed for program activities and promotion, supporting annual program evaluation and reporting

Evaluating Program Metrics:

The SFMTA employs a variety of metrics to track program impact and progress towards goals. The Safe Routes to School Program performs a transportation tally at every SFUSD public non-charter school every two years to measure district-wide mode split for school trips. The SFMTA compiles and analyzes collision data to determine the number of incidents within ¼ mile of school sites. Many factors outside of the program influence both mode choice and traffic incidents near schools, so the SFMTA also gathers metrics on the outcomes of events and activities and employs a Theory of Change for how these events and activities support behavior change. For individual program events and activities, metrics can include number of participants, mode counts, and measuring skill, knowledge, and perceptions of transportation mode choices after participation in the activity.

School Traffic Calming Program

The Safe Routes to School Non-Infrastructure Program and School Traffic Calming Program are distinct programs with separate budgets and funding. The SFMTA's School Traffic Calming Program combines the School Walk Audits and Proactive School Safety programs and will conduct school walk audits at up to ten school sites each year, and proactive daylighting at up to 50 intersections around schools each year. While separate programs, the Safe Routes to School Non-Infrastructure Program and School Traffic Calming Program are complementary in their goals in decreasing commuting in single-family vehicles to San Francisco's schools, improving safety of walking and bicycling, reducing city congestion and air pollution, and inspiring the next generations of walkers, bicyclists, and transit users. The SFMTA is requesting Prop L funds for the School Traffic Calming Program as a separate request on this meeting agenda.

Project Location

Citywide

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$466,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Safe Routes to School Non-Infrastructure
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)				
Advertise Construction				
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2022		
Operations (OP)				
Open for Use			Apr-May-Jun	2026
Project Completion (means last eligible expenditure)			Oct-Nov-Dec	2026

SCHEDULE DETAILS

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Safe Routes to School Non-Infrastructure
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-218: Safer and Complete Streets	\$0	\$466,000	\$0	\$466,000
OBAG3 (FY23 & FY24)	\$0	\$0	\$3,541,000	\$3,541,000
Phases In Current Request Total:	\$0	\$466,000	\$3,541,000	\$4,007,000

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP L	\$0	\$709,000	\$0	\$709,000
OBAG3 (FY22 & FY25)	\$0	\$0	\$3,541,000	\$3,541,000
OBAG3 (FY23 & FY24)	\$0	\$0	\$3,541,000	\$3,541,000
SFMTA Operating	\$0	\$0	\$229,400	\$229,400
Funding Plan for Entire Project Total:	\$0	\$709,000	\$7,311,400	\$8,020,400

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$0		
Construction	\$8,020,400	\$466,000	Rates based off of recent project
Operations	\$0		
Total:	\$8,020,400	\$466,000	

% Complete of Design:	N/A
As of Date:	N/A
Expected Useful Life:	N/A

**San Francisco County Transportation Authority
Prop L/Prop AA/Prop D TNC Allocation Request Form**

MAJOR LINE ITEM BUDGET - SAFE ROUTES TO SCHOOL NON-INFRASTRUCTURE

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)					
Budget Line Item	Totals	SFMTA	SFE	SFUSD	Contractor
SFMTA					
Program Management	\$ 1,075,500	\$ 1,075,500			
SFE					
Curriculum Development	\$ 87,500		\$ 87,500		
SFUSD					
Outreach and coordination	\$ 344,000			\$ 344,000	
Contractor/PSC	\$ -				
Task 1: Project Management	\$ 450,000				\$ 450,000
Task 2: Communication and Promotion	\$ 187,500				\$ 187,500
Task 3: School Assessment	\$ 425,000				\$ 425,000
Task 4: Activity Implementation	\$ 950,000				\$ 950,000
Task 5: Evaluation	\$ 187,500				\$ 187,500
Task 6: Other Direct Costs	\$ 125,000				\$ 125,000
Contract mark-up and profit	\$ 175,000				\$ 175,000
TOTAL CONSTRUCTION PHASE	\$ 4,007,000	\$ 1,075,500	\$ 87,500	\$ 344,000	\$ 2,500,000

* Professional Services Contract includes project management, communication and promotion, school assessment and engagement, activity implementation, program evaluation, other direct costs, and negotiated profit and mark-up. Contract task amounts are estimates with specific budgets set based on program need through task orders.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Safe Routes to School Non-Infrastructure
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$466,000	Total PROP L Recommended	\$466,000

SGA Project Number:		Name:	Safe Routes to School Non-Infrastructure Project
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	12/31/2027
Phase:	Construction	Fundshare:	5.99%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	Total
PROP L EP-218	\$348,000	\$118,000	\$466,000

Deliverables

1. Quarterly progress reports shall include % complete of the funded phase, work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, and any issues that may impact schedule, in addition to all other requirements described in the Standard Grant Agreement.

2. Annually, SFMTA staff will provide a report on how the SRTS Non-Infrastructure project is doing with respect to achieving the established goals of reducing single family vehicle trips by 37% and school-related collisions by 50% by 2030. The next annual report is expected in December 2024.

Special Conditions

1. Recommendation includes a waiver to Prop L policy to allow funds to be used for retroactive expenses incurred since July 1, 2023. We have combined the allocation for two fiscal years into this request, covering July 1, 2023 - June 30, 2025, for administrative efficiencies.

Notes

1. Reminder: All flyers, brochures, posters, websites and other similar materials prepared with Proposition L funding shall comply with the attribution requirements established in the Standard Grant Agreement.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	88.37%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	91.16%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Safe Routes to School Non-Infrastructure
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$466,000
--------------------------------	-----------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

ML

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Crysta Highfield	Joel C Goldberg
Title:	Transportation Planner II	Grants Procurement Manager
Phone:	(415) 646-2454	555-5555
Email:	crysta.highfield@sfmta.com	joel.goldberg@sfmta.com

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	School Traffic Calming Program
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN INFORMATION

PROP L Expenditure Plans	Safer and Complete Streets
Current PROP L Request:	\$2,000,000
Supervisorial District	Citywide

REQUEST

Brief Project Description

The San Francisco Municipal Transportation Agency (SFMTA) requests \$2,000,000 in Prop L funds for the School Traffic Calming Program, which combines the School Walk Audits and Proactive School Safety programs. This request will fund planning, design, and implementation of improvements identified through school walk audits at up to ten school sites each year, and proactive daylighting at up to 50 intersections around walk audit schools each year.

Detailed Scope, Project Benefits and Community Outreach

The San Francisco Municipal Transportation Agency (SFMTA) requests an allocation of \$2,000,000 in Prop L funds for the School Traffic Calming Program, which combines the School Walk Audits and Proactive School Safety programs. This allocation will fund planning, design, and implementation of improvements identified through school walk audits at up to ten school sites each year, and proactive daylighting at up to 50 intersections around schools each year.

Background

For the purposes of this program, the term “engineering” is used to describe planning, design, and implementation of traffic engineering improvements. The program encompasses all K-12 schools in San Francisco (public and private) and includes both proactive and responsive work. Proactive work will identify potential problem areas to address while engaging communities for added input and review, including students and families. The responsive work will follow a more traditional approach of responding to community concerns as they are raised.

School Walk Audits

With funding from this allocation, the SFMTA will conduct up to ten school walk audits each school year. Walk audits are collaborative assessments that involve the gathering of information about infrastructure issues, motorist behavior and pedestrian/bicycling behavior around schools. SFMTA staff will determine school sites for walk audits primarily based on collision data around schools, focusing on schools that have not had significant infrastructure improvements, and schools that have capacity to participate in a walk through, including support from staff, parents, and the principal.

To prepare for a walk audit, SFMTA staff will collect relevant data, including operational and infrastructure conditions around the school (i.e., sidewalk and street widths, bicycle infrastructure, Muni stops, presence of stop/signal control, lane configurations, etc.), collision history, and prepare a map for all users that summarizes the route. Walk audits will generally be limited to a 2-3 block radius around the school. Participants may include SFMTA staff, school administration staff, students, and families, crossing guards, SFUSD staff, and Department of Public Health staff.

Based on the actual or perceived safety and comfort issues identified as part of the walk audit, SFMTA staff will develop a series of recommendations to address the issues. These recommendations will largely be lower-cost and relatively easy to implement, and may include but not be limited to:

- Engineering Treatments
 - Traffic calming
 - Turn restrictions
 - Minor traffic signal modifications and timing changes
 - Paint and sign upgrades

Traffic calming measures encourage slower mid-block speeds along residential streets in San Francisco and include physical safety improvements put in place on our roads for the purpose of altering, slowing down, or reducing motor-vehicle traffic. For school areas, typical recommendations include speed humps and raised crosswalks. These measures have been shown to reduce speeding and increase safety.

Proactive Daylighting at Walk Audit Schools

As part of the School Traffic Calming Program, SFMTA will proactively install daylighting at up to 50 intersections around walk audit schools in accordance with AB 413. Daylighting is a highly effective safety improvement that is a key component of intersections across the city. By converting the parking spaces immediately before a crosswalk into red zones, typically around twenty feet long depending on the location, daylighting increases the visibility of pedestrians crossing the street. Children are particularly vulnerable because they are shorter and more likely to be invisible behind a parked car. And with the increase in size and height of many trucks and SUVs, even adults are vulnerable to collisions at low-visibility intersections.

Phases

Planning, Outreach, Design: During the planning and design phase, SFMTA will work with school staff and SFUSD more generally to inform them of the walk audit process. Once recommendations have been developed, SFMTA staff will also perform targeted outreach to other stakeholders, including the San Francisco Fire Department, Muni, and SFMTA Accessible Services as necessary as a part of the routine transportation engineering project review and approval process. Once the project list is established as part of the planning phase, SFMTA staff will complete detailed design for each of the proposed measures and carry each measure through the SFMTA public hearing legislative process for approval and environmental clearance. Outreach during the design phase consists of public notice of the legislation process and the public hearing.

Construction: SFMTA will have responsibility for implementing measures that have been recommended and designed as part of the walk audit process.

The total amount of funding requested each year will be allocated as follows:

- Planning, Outreach, Design: \$220,000 will fund planning and design efforts, including:
 - Organize Walk Audits with school representatives and other stakeholders
 - Perform walk audits and prepare reports
 - Develop preliminary list of recommended improvements
 - Finalize recommended improvements; review with Muni and SFFD
 - Review and approval process including environmental clearance, TASC, Public Hearing and City Traffic Engineer Directive
- Construction: \$1,780,000 will fund construction efforts, including:
 - Prepare and update striping drawings
 - Prepare and submit work orders
 - Completion of work orders by relevant SFMTA Operations crews (Paint Shop, Sign Shop, Meter Shop, and Signal Shop)
 - Coordinate construction of traffic calming devices by SFPW and/or an as-needed private contractor
 - Inspection and close out

San Francisco Safe Routes to School Program (SF-SRTS)

The SF-SRTS program is delivered through a partnership of four city agencies (SF Environment, SFMTA, San Francisco Department of Public Health (DPH), and SFUSD), and four local non-profit partners (San Francisco Bicycle Coalition, Walk San Francisco, Tenderloin Safe Passage, and the YMCA). Vision Zero is the City’s road safety policy to eliminate all traffic deaths in San Francisco. While school-related traffic deaths are very rare, students still experience safety challenges traveling to, from, and around schools. Therefore, the program has set a goal of reducing collisions and injuries around schools, and the school walk audit program will contribute towards these safety goals around city schools as part of the overall SF-SRTS.

Project Location

Citywide

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Planning/Conceptual Engineering (PLAN), Design Engineering (PS&E), Construction (CON)

Justification for Multi-phase Request

We recommend a multi-phase allocation given that the phases will be occurring concurrently.

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP L Amount	\$2,000,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	School Traffic Calming Program
Primary Sponsor:	San Francisco Municipal Transportation Agency

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)	Jul-Aug-Sep	2024	Apr-May-Jun	2026
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)			Apr-May-Jun	
Advertise Construction				
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2024		
Operations (OP)				
Open for Use			Apr-May-Jun	2027
Project Completion (means last eligible expenditure)			Jul-Aug-Sep	2027

SCHEDULE DETAILS

SFMTA plans to identify the ten schools that will receive walk audits by January 2025. Conducting walk audits is likely to begin in March 2025, weather permitting. Walk audit reports are scheduled to be finalized by December 2025. SFMTA plans to start implementing daylighting at walk audit schools in January 2025, weather permitting, and implement recommendations from walk audits on a rolling basis through June 2027. See attached Walk Audit Guidelines for details.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	School Traffic Calming Program
Primary Sponsor:	San Francisco Municipal Transportation Agency

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-218: Safer and Complete Streets	\$0	\$2,000,000	\$0	\$2,000,000
Phases In Current Request Total:	\$0	\$2,000,000	\$0	\$2,000,000

COST SUMMARY

Phase	Total Cost	PROP L - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$220,000	\$220,000	prior work
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$0		
Construction	\$1,780,000	\$1,780,000	prior work
Operations	\$0		
Total:	\$2,000,000	\$2,000,000	

% Complete of Design:	0.0%
As of Date:	05/07/2024
Expected Useful Life:	30 Years

San Francisco County Transportation Authority Prop L/Prop AA/Prop D TNC Allocation Request Form

SCHOOLS TRAFFIC CALMING PROGRAM - PLANNING & DESIGN

MAJOR LINE ITEM BUDGET

BUDGET SUMMARY

Agency	Planning & Design					Total
SFMTA	\$ 220,000.00	\$ -	\$ -	\$ -	\$ -	\$ 220,000
SFCTA	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Consultant	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Other Direct Costs *	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Total	\$ 220,000	\$ -	\$ -	\$ -	\$ -	\$ 220,000

* Direct Costs include mailing, reproduction costs room rental fees.

DETAILED LABOR COST ESTIMATE - BY AGENCY

SFMTA	Hours	Base Hourly Rate	Fully Burdened Labor Cost	Fully Burdened Hourly Cost	FTE	Total
Engineer Principal (5212)		\$ 134.8755	\$ 664,780	\$ 319.61	0.000	\$ -
Sr. Engineer (5211)	100	\$ 108.0423	\$ 538,435	\$ 258.86	0.048	\$ 25,886
Engineer (5241)	180	\$ 93.3639	\$ 469,321	\$ 225.64	0.087	\$ 40,614
Transit Planner IV (5290)	355	\$ 82.6279	\$ 418,770	\$ 201.33	0.170	\$ 71,372
Associate Engineer (5207)	180	\$ 82.1625	\$ 416,579	\$ 200.28	0.086	\$ 36,023
Assistant Engineer (5203)	180	\$ 69.2774	\$ 354,363	\$ 170.37	0.087	\$ 30,666
Engineering Associate (5366)	50	\$ 63.2144	\$ 325,668	\$ 156.57	0.024	\$ 7,829
Junior Engineer (5201)	50	\$ 61.3404	\$ 316,565	\$ 152.19	0.024	\$ 7,610
Engineering Assistant (5362)		\$ 49.2529	\$ 257,850	\$ 123.97	0.000	\$ -
Senior Clerk (1406)		\$ 44.6817	\$ 235,103	\$ 113.03	0.000	\$ -
Contingency		\$ -	\$ -	\$ -	0.000	\$ -
Total	1094				0.53	\$ 220,000

Planning & Design cost per school = \$22,000

**San Francisco County Transportation Authority
Prop L/Prop AA/Prop D TNC Allocation Request Form**

**SCHOOL TRAFFIC CALMING PROGRAM - CONSTRUCTION
MAJOR LINE ITEM BUDGET**

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)

Description	Unit Cost	Number of Improvements	SFPW Cost	SFMTA Cost	Number of Improvements per School	Cost of Improvements per School
1. Traffic Calming						
1a. Asphalt Raised Crosswalk	\$ 20,000	10	\$ 200,000		1	\$ 20,000
1b. Speed Table	\$ 20,000	10	\$ 200,000		1	\$ 20,000
1c. Speed Hump/Cushion	\$ 15,000	40	\$ 600,000		4	\$ 60,000
1d. Traffic Island	\$ 10,000	40	\$ 400,000		4	\$ 40,000
1e. Paint & Signs for Traffic Calming	\$ 2,000	60	\$ 120,000		6	\$ 12,000
2. Minor Improvements						
2a. Signal Timing Change	\$ 2,000	10		\$ 20,000	1	\$ 2,000
2b. Marked Crosswalk	\$ 1,000	20		\$ 20,000	2	\$ 2,000
2c. Traffic Sign	\$ 500	40		\$ 20,000	4	\$ 2,000
2d. Daylighting (1 approach)	\$ 500	200		\$ 100,000	20	\$ 10,000
3. Construction Management/Support	\$ 100,000			\$ 100,000		\$ 10,000
TOTALS		430	\$ 1,520,000	\$ 260,000	43	\$ 178,000

Construction Cost per school = \$178,000

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	School Traffic Calming Program
Primary Sponsor:	San Francisco Municipal Transportation Agency

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP L Requested:	\$2,000,000	Total PROP L Recommended	\$2,000,000

SGA Project Number:		Name:	School Traffic Calming Program
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	06/30/2026
Phase:	Planning/Conceptual Engineering	Fundshare:	100.0%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	FY2026/27	Total
PROP L EP-218	\$70,000	\$100,000	\$50,000	\$220,000

Deliverables

- By December 2024, SFMTA shall provide the list of the schools that will receive walk audits to be funded by this request.
- Quarterly progress reports will include the status of each walk audit, including the work done the prior quarter, the work planned in the upcoming quarter, and any issues that may impact schedule, in addition to all other requirements described in the Standard Grant Agreement.
- Upon completion of all walk audit reports, anticipated by December 2025, SFMTA will provide the final walk audit reports, including recommended traffic calming measures at each school to be constructed using Prop L funds for the construction phase. SFMTA shall post the final walk audit reports to an SFMTA webpage.

Special Conditions

- The Safer and Complete Streets 5YPP includes the following condition for the requested School Traffic Calming Program funds: Prior to allocation of Prop L funds, SFMTA shall present draft walk audit program guidelines to the Transportation Authority Board before finalizing. The guidelines shall include how the public can request a walk audit, how SFMTA prioritizes among schools to receive walk audits, and what to expect during and after the audit (e.g. types of recommendations, process for finalizing the recommendations, and implementation timeline).

The SFMTA is presenting the walk audit guidelines as part of the subject item, which satisfies this condition at time of programming.

- Approval of this request is conditioned on concurrent amendment of the Safer & Complete Streets 5YPP to update the phase from Design to Planning and to update the cashflow between phases.

Notes

- Walk audits will be completed in accordance with the walk audit guidelines attached to this request.

SGA Project Number:		Name:	School Traffic Calming Program
Sponsor:	San Francisco Municipal Transportation Agency	Expiration Date:	12/31/2027
Phase:	Construction	Fundshare:	100.0%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	FY2026/27	Total
PROP L EP-218	\$30,000	\$670,000	\$1,080,000	\$1,780,000

Deliverables

1. Quarterly progress reports will include the status of implementation of all recommended improvements at each walk audit school, listed by measure and location, including traffic calming and proactive daylighting. Progress reports shall include the work done in the prior quarter, the work planned in the upcoming quarter, and any issues that may impact schedule, in addition to all other requirements described in the Standard Grant Agreement.

Special Conditions

1. Approval of this request is conditioned on concurrent amendment of the Safer & Complete Streets 5YPP to update the phase from Design to Planning and to update the cashflow between phases.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	No PROP AA	No TNC TAX	0.0%
Actual Leveraging - This Project	No PROP AA	No TNC TAX	0.0%

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	School Traffic Calming Program
Primary Sponsor:	San Francisco Municipal Transportation Agency

EXPENDITURE PLAN SUMMARY

Current PROP L Request:	\$2,000,000
--------------------------------	-------------

1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:
DC

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Damon Curtis	Joel C Goldberg
Title:	Project Manager	Grants Procurement Manager
Phone:	555-5555	555-5555
Email:	damon.curtis@sfmta.com	joel.goldberg@sfmta.com

School Traffic Calming Program School Walk Audit Guidelines (May 2024)



Background

SFMTA's School Traffic Calming Program is a combination of school walk audits and proactive daylighting. The current Prop L allocation is intended to fund planning, design, and implementation of improvements identified through school walk audits at up to ten school sites each year, and proactive daylighting at up to fifty (50) intersections around schools each year.

Walk Audits

Walk audits are collaborative assessments that help the SFMTA identify infrastructure needs, motorist behaviors, and pedestrian/bicyclist behaviors on streets within a 2-3 block radius of public and private K-12 schools in San Francisco. With funding from this allocation, and in collaboration with local school communities, the SFMTA will conduct up to ten (10) school walk audits each school year.

School Prioritization & Selection

Each school year, SFMTA's School Traffic Calming Program selects up to ten (10) schools for walk audits. The process of selecting schools begins with a ranking of all public and private K-12 schools based primarily on the following criteria:

1. Five-year pedestrian-involved collision history within ¼-mile of the school – TransBASE
2. School enrollment data – California Department of Education
3. Department of Public Health data on student residency within a walkable radius of each school. This anonymous data (names and addresses NOT included) is used to determine the potential for walking and bicycling to school – SRTS Non-Infrastructure Program

Based on the above criteria, SFMTA staff develops a preliminary list of ten (10) schools for participation in the walk audit program, then the following factors are used to help refine and finalize school selections:

1. Existing Infrastructure – A review of planned and recently completed pedestrian safety improvements implemented in school areas during the previous 5 years (schools having already received, or with plans to receive, significant improvements may drop in ranking).
2. Equity – Where applicable, consideration may be given to schools within equity priority communities or California Communities of Concern. Also, and to the extent possible, efforts will be made to balance the number of schools across all eleven supervisorial districts. Since only ten schools are selected each year, this program will seek to ensure at least at least one school within each supervisorial district receives a walk-audit over a given two-year period.

Options available for schools not selected for a walk audit

For schools not selected to participate in the Walk Audit Program in a given school year, SFMTA continually responds to individual and school requests for evaluation of traffic safety concerns, particularly as they pertain to pedestrian and bicyclist safety in the vicinity of schools. SFMTA also provides a variety of project paths and programs offering solutions to traffic safety concerns. What follows is a partial list of ongoing projects and programs addressing traffic safety citywide:

1. Application-Based Residential Traffic Calming Program
2. Slow Streets Program
3. Quick-Build Projects on the High Injury Network
4. Vision Zero Program
5. Transportation Engineering Operations – Resident requests through 311

School Walk Audit Process

Once schools are selected, SFMTA staff will outreach to school administrators, parent-teacher groups, Unified School District transportation Staff, district supervisor Staff, and local advocacy groups, to announce the school's selection and plan for an inclusive walk audit process. The date, time and meeting location will be established by SFMTA staff in collaboration with the school community. The school principal or administrator will coordinate a walk team, typically a group of 6-12 people, including school administration, staff, students, families, advocates, and local SFMTA crossing guards.

To prepare for a walk audit, SFMTA staff will survey operational and infrastructure conditions around the school, including collision history, sidewalk and street widths, bicycle infrastructure, transit stops, nearby stop/signal controls, warning signage, pavement striping and markings, and lane configurations.

Prior to the Walk Audit, SFMTA will distribute a Walk Packet that details and explains the treatments that can be recommended (and implemented) through the walk audit program. The packet will include an outline of the walk route with space for participants to note traffic safety concerns and improvement requests. The packet also will include information about school access conditions and policies, including current access routes, student pick up and drop off activities, Muni or school district bus service, color curb zones, and school crossing guards.

Walk Audit Route

The walking route typically includes only streets within a 2-3 block radius of the school. If a school requests the walk include other streets frequently used by students, if circumstances and funding allow, SFMTA staff may expand the walking route to include those streets. However, recommended improvements are generally prioritized for streets adjacent to the school.

Day of the Walk Audit

On the day of the walk, participants meet at the agreed upon time and place. Each walker is given a Walk Packet to record notes and a pen. SFMTA staff lead the walk, encouraging participants to share perceived obstacles to safe and comfortable walking in the area around the school. SFMTA staff takes notes during the walk. Walk leaders will initiate conversations at certain locations along the walk as necessary to help generate discussion amongst group participants.

After the Walk Audit

Following the Walk Audit, SFMTA staff prepare a draft Walk Audit Report with recommendations based on feedback gathered during the walk or in subsequent communications.

Final Walk Audit Report

The draft Walk Audit Report is distributed to participants for review and comment. This comment period, generally two weeks, is the final stage of public participation in the report. Following the comment period, the report is finalized by SFMTA staff and shared with the school, Walk Audit participants, the SFCTA, and the district supervisor's office.

Implementation of Recommended Improvements

Recommendations are divided into near-term and long-term improvements. Long-term and more costly improvements are documented and made available for future coordination opportunities and/or proposed for inclusion in future capital projects. Recommendations that do not fall under SFMTA purview (e.g., street trees, landscaping, street lights, street cleaning, pot holes and other pavement defects), are documented and referred to the appropriate city department for follow up.

Near-term improvements that do not require legislation (e.g., red zones, painted safety zones, loading zone, signal timing changes, minor striping changes, pavement markings, warning signs) are designed and work ordered to the appropriate SFMTA shop(s) for implementation.

Near-term improvements that do require legislation (e.g., traffic calming, parking changes, road diets, follow the standard process of design, fire department and transit review, internal engineering review, multi-agency review, and a public hearing followed by final approval by the City Traffic Engineer. Recommendations are implemented by SFMTA and SFPW crews, or in some instances a private contractor.

School Traffic Calming Program – Projected Timeline (24-25 School Year)

Year 1 Summary (July 2024 - June 2025):

- Identify and conduct walk audits at ten schools; walk audits likely to begin in March when weather improves
- Proactive daylighting will begin once schools are identified, as early as January weather permitting

Year 2 Summary (July 2025 - June 2026):

- Finalize walk audit reports and recommended improvements
- Begin implementing recommended improvements, primarily those that don't require legislation or coordination (e.g. painting crosswalks and installing warning signs)
- Complete proactive daylighting at walk audit schools (up to 50 intersections)

Year 3 Summary (July 2026 - June 2027):

- Continue implementing recommended improvements, primarily those that require legislation and coordination (e.g. speed humps and traffic islands)

Learn More About School Walk Audits

San Franciscans can learn more about school walk audits and sign up for updates by visiting the program website: www.sfmta.com/SchoolWalkAudits.

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Safer and Complete Streets (EP 18)
 Programming and Allocations to Date
 Pending June 2024 Board

Agency	Project Name	Phase	Status	Fiscal Year					Total
				2023/24	2024/25	2025/26	2026/27	2027/28	
Subprogram: Capital Projects									
SFMTA	5th Street Corridor Improvements	CON	Programmed		\$1,000,000				\$1,000,000
SFMTA	7th Ave Bikeway	PS&E	Programmed		\$50,000				\$50,000
SFMTA	7th Ave Bikeway	CON	Programmed			\$100,000			\$100,000
SFMTA	Active Communities Plan Implementation	TBD	Programmed		\$4,350,000				\$4,350,000
SFMTA	Active Communities Plan Implementation	TBD	Programmed			\$3,750,000			\$3,750,000
SFMTA	Active Communities Plan Implementation	TBD	Programmed				\$3,750,000		\$3,750,000
SFMTA	Active Communities Plan Implementation	TBD	Programmed					\$3,750,000	\$3,750,000
SFMTA	Central Embarcadero Enhancement (OBAG Match)	PS&E	Pending	\$200,000					\$200,000
SFMTA	District 4 Street Improvements	CON	Programmed	\$700,000					\$700,000
SFMTA	Golden Gate Greenway (Tenderloin) ¹	PS&E	Pending	\$140,000					\$140,000
SFMTA	Golden Gate Greenway (Tenderloin) ¹	CON	Programmed		\$960,000				\$960,000
SFMTA	Howard Streetscape	CON	Programmed		\$2,000,000				\$2,000,000
SFPW	Market Octavia Living Alleys Phase 1B	CON	Programmed			\$700,000			\$700,000
SFMTA	Page Slow Street	PS&E	Programmed		\$407,000				\$407,000
SFMTA	Page Slow Street	CON	Programmed			\$593,000			\$593,000
SFMTA	Safe Streets Evaluation Program	PLAN	Programmed		\$450,000				\$450,000
SFMTA	Safe Streets Evaluation Program	PLAN	Programmed				\$400,000		\$400,000
SFMTA	School Traffic Calming Program ²	PS&E	Programmed	\$0					\$0
SFMTA	School Traffic Calming Program ²	PLAN	Pending	\$220,000					\$220,000
SFMTA	School Traffic Calming Program ²	CON	Pending	\$1,780,000					\$1,780,000
SFMTA	School Traffic Calming Program	PS&E	Programmed		\$220,000				\$220,000
SFMTA	School Traffic Calming Program	CON	Programmed		\$1,780,000				\$1,780,000
SFMTA	School Traffic Calming Program	PS&E	Programmed			\$220,000			\$220,000
SFMTA	School Traffic Calming Program	CON	Programmed			\$1,780,000			\$1,780,000
SFMTA	School Traffic Calming Program	PS&E	Programmed				\$220,000		\$220,000
SFMTA	School Traffic Calming Program	CON	Programmed				\$1,780,000		\$1,780,000
SFMTA	School Traffic Calming Program	PS&E	Programmed					\$220,000	\$220,000
SFMTA	School Traffic Calming Program	CON	Programmed					\$1,780,000	\$1,780,000
SFPW	Sickles Avenue Streetscape	CON	Programmed		\$1,300,000				\$1,300,000
SFMTA	Slow Streets Implementation ¹	CON	Programmed		\$200,000				\$200,000
SFMTA	Slow Streets Implementation	CON	Programmed		\$200,000				\$200,000

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)

Safer and Complete Streets (EP 18)

Programming and Allocations to Date

Pending June 2024 Board

Agency	Project Name	Phase	Status	Fiscal Year					Total
				2023/24	2024/25	2025/26	2026/27	2027/28	
SFMTA	Slow Streets Implementation	CON	Programmed			\$200,000			\$200,000
SFMTA	Slow Streets Implementation	CON	Programmed				\$200,000		\$200,000
SFMTA	Slow Streets Implementation	CON	Programmed					\$200,000	\$200,000
SFMTA	SoMa Arterial Traffic Calming	CON	Programmed		\$1,000,000				\$1,000,000
SFMTA	Tenderloin Protected Intersections	CON	Programmed			\$250,000			\$250,000
SFMTA	Valencia Street Bikeway Improvements	CON	Programmed				\$1,000,000		\$1,000,000
SFMTA	Vision Zero Left Turn Reduction Program	CON	Allocated	\$100,000					\$100,000
SFMTA	Vision Zero Left Turn Reduction Program	CON	Programmed		\$100,000				\$100,000
SFMTA	Vision Zero Speed Limit Reduction	CON	Allocated	\$100,000					\$100,000
SFMTA	Vision Zero Speed Limit Reduction	CON	Programmed			\$100,000			\$100,000
SFMTA	Vision Zero Speed Limit Reduction	CON	Programmed					\$100,000	\$100,000
SFCTA	Yerba Buena Island Multi-Use Path	CON	Programmed			\$1,000,000			\$1,000,000
Subprogram: Outreach and Education Projects									
SFMTA	Bicycle Education and Outreach	CON	Allocated	\$200,000					\$200,000
SFMTA	Bicycle Education and Outreach	CON	Programmed		\$200,000				\$200,000
SFMTA	Bicycle Education and Outreach	CON	Programmed			\$200,000			\$200,000
SFMTA	Bicycle Education and Outreach	CON	Programmed				\$200,000		\$200,000
SFMTA	Bicycle Education and Outreach	CON	Programmed					\$200,000	\$200,000
SFMTA	Safe Routes to School Non-Infrastructure	CON	Pending	\$230,000					\$230,000
SFMTA	Safe Routes to School Non-Infrastructure	CON	Pending		\$236,000				\$236,000
SFMTA	Safe Routes to School Non-Infrastructure	CON	Programmed			\$243,000			\$243,000
SFMTA	Safe Routes to School Non-Infrastructure	CON	Programmed				\$251,000		\$251,000
SFMTA	Safe Routes to School Non-Infrastructure	CON	Programmed					\$258,000	\$258,000
SFMTA	Vision Zero Education and Communications: Speed Safety Cameras FY24	CON	Allocated	\$150,000					\$150,000
SFMTA	Vision Zero Education and Communications FY25-28	CON	Programmed		\$200,000				\$200,000
SFMTA	Vision Zero Education and Communications FY25-28	CON	Programmed				\$200,000		\$200,000
Subprogram: New Traffic Signals									
SFMTA	Contract 66 New Traffic Signals	CON	Programmed	\$3,300,000					\$3,300,000
SFMTA	Contract 67 New Traffic Signals	PS&E	Programmed		\$1,100,000				\$1,100,000
SFMTA	Skyline and Sloat Intersection Improvements	CON	Allocated	\$800,000					\$800,000

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Safer and Complete Streets (EP 18)
 Programming and Allocations to Date
 Pending June 2024 Board

Agency	Project Name	Phase	Status	Fiscal Year					Total
				2023/24	2024/25	2025/26	2026/27	2027/28	
Total Programmed in 2023 5YPP				\$7,920,000	\$15,753,000	\$9,136,000	\$8,001,000	\$6,508,000	\$47,318,000
Total Allocated and Pending				\$3,920,000	\$236,000	\$0	\$0	\$0	\$4,156,000
Total Unallocated				\$4,000,000	\$15,517,000	\$9,136,000	\$8,001,000	\$6,508,000	\$43,162,000
Total Programmed in 2023 Strategic Plan				\$8,080,000	\$15,593,000	\$9,136,000	\$8,001,000	\$6,508,000	\$47,318,000
Deobligated Funds				\$0	\$0	\$0	\$0	\$0	\$0
Cumulative Remaining Programming Capacity				\$160,000	\$0	\$0	\$0	\$0	\$0
Pending Allocation/Appropriation									
Board Approved Allocation/Appropriation									

FOOTNOTES:

- ¹ 5YPP amendment to fund Golden Gate Greenway (Tenderloin) with \$140,000 in FY23/24 for design (Resolution 2024-xx, 5/21/2024):
 Slow Streets Implementation: Reduced from \$200,000 to \$0 in Fiscal Year 2023/24 for design and increased from \$0 to \$200,000 in FY24/25 for design.
 Golden Gate Greenway (Tenderloin): Reduced from \$1,000,000 to \$960,000 in FY2024/25 for construction.
 Golden Gate Greenway (Tenderloin): Increased from \$100,000 to \$140,000 in FY2023/24 for design.
- ² 5YPP amendment to fund School Traffic Calming Program with \$220,000 in FY23/24 for planning and update cash flow in School Traffic Calming Program construction in FY23/24 (Resolution 2024-xx, 6/xx/2024):
 School Traffic Calming, FY23/24 Design: Reduced from \$220,000 to \$0 in FY23/24.
 School Traffic Calming, FY23/24 Planning: Added project with \$220,000 in FY23/24. Delayed \$30,000 cash flow from FY24/25 to FY25/26.
 School Traffic Calming, FY23/24 Construction: Advanced \$30,000 in FY24/25 cash flow and reduced FY25/26 cash flow from \$700,000 to \$670,000.

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Safer and Complete Streets (EP 18)
 Cash Flow (Maximum Annual Reimbursement)
 Pending June 2024 Board

Project Name	Phase	Fiscal Year					Total
		2023/24	2024/25	2025/26	2026/27	2027/28	
5th Street Corridor Improvements	CON				\$500,000	\$500,000	\$1,000,000
7th Ave Bikeway	PS&E		\$25,000	\$25,000			\$50,000
7th Ave Bikeway	CON			\$50,000	\$50,000		\$100,000
Active Communities Plan Implementation	TBD			\$500,000	\$550,000	\$1,300,000	\$4,350,000
Active Communities Plan Implementation	TBD					\$750,000	\$3,750,000
Active Communities Plan Implementation	TBD						\$3,750,000
Active Communities Plan Implementation	TBD						\$3,750,000
Central Embarcadero Enhancement (OBAG Match)	PS&E	\$50,000	\$150,000				\$200,000
District 4 Street Improvements	CON		\$350,000	\$350,000			\$700,000
Golden Gate Greenway (Tenderloin) ¹	PS&E		\$140,000				\$140,000
Golden Gate Greenway (Tenderloin) ¹	CON			\$210,000	\$500,000	\$250,000	\$960,000
Howard Streetscape	CON			\$500,000	\$500,000	\$1,000,000	\$2,000,000
Market Octavia Living Alleys Phase 1B	CON				\$350,000	\$350,000	\$700,000
Page Slow Street	PS&E			\$200,000	\$207,000		\$407,000
Page Slow Street	CON					\$500,000	\$593,000
Safe Streets Evaluation Program	PLAN		\$250,000	\$200,000			\$450,000
Safe Streets Evaluation Program	PLAN				\$200,000	\$200,000	\$400,000
School Traffic Calming Program ²	PS&E		\$0	\$0			\$0
School Traffic Calming Program ²	PLAN		\$70,000	\$100,000	\$50,000		\$220,000
School Traffic Calming Program ²	CON		\$30,000	\$670,000	\$1,080,000		\$1,780,000
School Traffic Calming Program	PS&E			\$100,000	\$120,000		\$220,000
School Traffic Calming Program	CON				\$700,000	\$1,080,000	\$1,780,000
School Traffic Calming Program	PS&E				\$100,000	\$120,000	\$220,000
School Traffic Calming Program	CON					\$700,000	\$1,780,000
School Traffic Calming Program	PS&E					\$100,000	\$220,000
School Traffic Calming Program	CON						\$1,780,000
School Traffic Calming Program	PS&E						\$220,000
School Traffic Calming Program	CON						\$1,780,000
Sickles Avenue Streetscape	CON		\$300,000	\$1,000,000			\$1,300,000
Slow Streets Implementation ¹	CON		\$60,000	\$140,000			\$200,000
Slow Streets Implementation	CON			\$100,000	\$100,000		\$200,000

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Safer and Complete Streets (EP 18)
 Cash Flow (Maximum Annual Reimbursement)
 Pending June 2024 Board

Project Name	Phase	Fiscal Year					Total
		2023/24	2024/25	2025/26	2026/27	2027/28	
Slow Streets Implementation	CON				\$100,000	\$100,000	\$200,000
Slow Streets Implementation	CON					\$100,000	\$200,000
Slow Streets Implementation	CON						\$200,000
SoMa Arterial Traffic Calming	CON			\$120,000	\$520,000	\$360,000	\$1,000,000
Tenderloin Protected Intersections	CON				\$125,000	\$125,000	\$250,000
Valencia Street Bikeway Improvements	CON					\$500,000	\$1,000,000
Vision Zero Left Turn Reduction Program	CON		\$50,000	\$50,000			\$100,000
Vision Zero Left Turn Reduction Program	CON				\$50,000	\$50,000	\$100,000
Vision Zero Speed Limit Reduction	CON		\$100,000				\$100,000
Vision Zero Speed Limit Reduction	CON				\$100,000		\$100,000
Vision Zero Speed Limit Reduction	CON						\$100,000
Yerba Buena Island Multi-Use Path	CON				\$500,000	\$500,000	\$1,000,000
Bicycle Education and Outreach	CON		\$200,000				\$200,000
Bicycle Education and Outreach	CON			\$200,000			\$200,000
Bicycle Education and Outreach	CON				\$200,000		\$200,000
Bicycle Education and Outreach	CON					\$200,000	\$200,000
Bicycle Education and Outreach	CON						\$200,000
Safe Routes to School Non-Infrastructure	CON	\$100,000	\$130,000				\$230,000
Safe Routes to School Non-Infrastructure	CON		\$118,000	\$118,000			\$236,000
Safe Routes to School Non-Infrastructure	CON			\$122,000	\$121,000		\$243,000
Safe Routes to School Non-Infrastructure	CON				\$126,000	\$125,000	\$251,000
Safe Routes to School Non-Infrastructure	CON					\$129,000	\$258,000
Vision Zero Education and Communications: Speed Safety Cameras FY24	CON		\$50,000	\$100,000			\$150,000
Vision Zero Education and Communications FY25-28	CON			\$50,000	\$150,000		\$200,000
Vision Zero Education and Communications FY25-28	CON				\$50,000	\$150,000	\$200,000
Contract 66 New Traffic Signals	CON		\$1,100,000	\$1,100,000	\$1,100,000		\$3,300,000
Contract 67 New Traffic Signals	PS&E		\$550,000	\$550,000			\$1,100,000
Skyline and Sloat Intersection Improvements	CON		\$600,000	\$200,000			\$800,000

2023 Prop L 5-Year Project List (FY 2023/24 - FY 2027/28)
 Safer and Complete Streets (EP 18)
 Cash Flow (Maximum Annual Reimbursement)
 Pending June 2024 Board

Project Name	Phase	Fiscal Year					Total
		2023/24	2024/25	2025/26	2026/27	2027/28	
Cash Flow Programmed in 2023 5YPP		\$150,000	\$4,273,000	\$6,755,000	\$8,149,000	\$9,189,000	\$47,318,000
Total Cash Flow Allocated and Pending		\$150,000	\$1,638,000	\$1,238,000	\$1,130,000	\$0	\$4,156,000
Total Cash Flow Unallocated		\$0	\$2,635,000	\$5,517,000	\$7,019,000	\$9,189,000	\$43,162,000
Total Cash Flow in 2023 Strategic Plan		\$150,000	\$4,273,000	\$6,805,000	\$8,099,000	\$9,189,000	\$47,318,000
Deobligated Funds		\$0	\$0	\$0	\$0	\$0	\$0
Cumulative Remaining Cash Flow Capacity		\$0	\$0	\$50,000	\$0	\$0	\$0
Pending Allocation/Appropriation							
Board Approved Allocation/Appropriation							

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN INFORMATION

PROP AA Expenditure Plans	Prop AA Streets Projects
Current PROP AA Request:	\$2,360,572
Supervisorial Districts	District 03, District 05, District 06

REQUEST

Brief Project Description

The Prop AA funds requested will fund the paving scope of work which includes demolition and pavement renovation of 29 blocks, construction and retrofit of approximately 31 curb ramps, new sidewalk construction, traffic control, and all related and incidental work within project limits.

Detailed Scope, Project Benefits and Community Outreach

Public Works (SFPW) requests Prop AA funds for the construction phase of the 8th St, Clay St and Leavenworth St Pavement Renovation project. The requested Prop AA grant will fund the paving scope of work which includes demolition and pavement renovation of 29 blocks, construction and retrofit of approximately 31 curb ramps, new sidewalk construction, traffic control, and all related and incidental work within project limits.

The project schedule will be coordinated with other projects and agencies as work programs are determined to minimize construction impacts to the City.

SFPW inspects each of the City's blocks and assigns a Pavement Condition Index (PCI) score every two years. The PCI score ranges from a low of 0 to a high of 100. These scores assist SFPW with implementing the pavement management strategy of aiming to preserve streets by applying the right treatment to the right roadway at the right time. Streets are selected based on PCI scores as well as the presence of transit and bicycle routes, street clearance (i.e., coordination with utilities) and geographic equity. The average PCI score within the project limits is mid 50's. Streets with a PCI between 50 and 69 are considered "at-risk" and are quickly deteriorating and would require larger scale repair work if they are not treated soon. Residential streets make up two-thirds of San Francisco's street network.

The following are the proposed locations of the project:

7th St from Charles J Brenham Pl to Mission St - 2 Blocks

8th St from Mission St to Folsom St - 6 Blocks

Clay St from Jones St to Polk St - 5 Blocks

142

Clementina St from Kaplan Ln to 3rd St - 1 Block
Golden Gate Ave from 6th St to Jones St - 1 Block
Harrison St from 8th St to 9th St - 2 Blocks
Larkin St from Sacramento St to Jackson St - 3 Blocks
Leavenworth St from McAllister St to Bush St - 9 Blocks

All candidates shown are subject to substitution and schedule changes pending, visual confirmation, utility clearances and coordination with other agencies. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the candidates to be postponed.

Project Location

Various blocks on 8th St, Clay St and Leavenworth St

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Construction (CON)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP AA Amount	\$2,360,572.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Primary Sponsor:	Department of Public Works

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)				
Environmental Studies (PA&ED)				
Right of Way				
Design Engineering (PS&E)	Jan-Feb-Mar	2022	Apr-May-Jun	2024
Advertise Construction	Apr-May-Jun	2024		
Start Construction (e.g. Award Contract)	Jul-Aug-Sep	2024		
Operations (OP)				
Open for Use			Jul-Aug-Sep	2026
Project Completion (means last eligible expenditure)			Jul-Aug-Sep	2027

SCHEDULE DETAILS

Through the project's coordination process, there are no other known projects and/or scopes of work other than Public Utilities Commission joining the project with sewer rehabilitation scope of work.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Primary Sponsor:	Department of Public Works

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-701: Prop AA Streets Projects	\$0	\$2,360,572	\$0	\$2,360,572
Road Maintenance and Rehabilitation (RMRA)	\$0	\$1,777,268	\$0	\$1,777,268
Phases In Current Request Total:	\$0	\$4,137,840	\$0	\$4,137,840

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP AA	\$0	\$2,360,572	\$0	\$2,360,572
Highway Use Tax (HUTA)	\$0	\$0	\$350,000	\$350,000
Road Maintenance and Rehabilitation (RMRA)	\$0	\$1,777,268	\$0	\$1,777,268
Funding Plan for Entire Project Total:	\$0	\$4,137,840	\$350,000	\$4,487,840

COST SUMMARY

Phase	Total Cost	PROP AA - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$0		
Environmental Studies	\$0		
Right of Way	\$0		
Design Engineering	\$350,000		Based on work performed so far
Construction	\$4,137,840	\$2,360,572	Engineer's estimate at 95% design
Operations	\$0		
Total:	\$4,487,840	\$2,360,572	

% Complete of Design:	95.0%
As of Date:	03/31/2024
Expected Useful Life:	20 Years

**San Francisco County Transportation Authority
Prop L/Prop AA/TNC Tax Allocation Request Form**

MAJOR LINE ITEM BUDGET - 8TH ST, CLAY ST, AND LEAVENWORTH ST PAVEMENT RENOVATION

SUMMARY BY MAJOR LINE ITEM (BY AGENCY LABOR BY TASK)				
Budget Line Item	Totals	% of contract	SFPW	Contractor
1. Contract				
Traffic Control/ Pavement Markings	\$ 274,000			\$ 274,000
Planing	\$ 323,933			\$ 323,933
Asphalt Concrete	\$ 993,510			\$ 993,510
Concrete Base/Pavement	\$ 1,031,239			\$ 1,031,239
Concrete Sidewalk	\$ 87,600			\$ 87,600
Concrete Curb	\$ 166,235			\$ 166,235
Pull Box/Adjust Manhole	\$ 39,000			\$ 39,000
Hydrant and Watermain Valve Box	\$ 3,750			\$ 3,750
Mobilization/Demobilization	\$ 145,800			\$ 145,800
Subtotal	\$ 3,065,067			\$ 3,065,067
2. Construction Management/Support	\$ 766,267	25%	\$ 766,267	
3. Contingency	\$ 306,507	10%		
TOTAL CONSTRUCTION PHASE	\$ 4,137,840		\$ 766,267	\$ 3,065,067

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Primary Sponsor:	Department of Public Works

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP AA Requested:	\$2,360,572	Total PROP AA Recommended	\$2,360,572

SGA Project Number:	725-108061	Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Sponsor:	Department of Public Works	Expiration Date:	09/30/2027
Phase:	Construction	Fundshare:	57.05%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	FY2025/26	FY2026/27	Total
PROP AA EP-701	\$1,416,343	\$708,172	\$236,057	\$2,360,572

Deliverables

1. Quarterly progress reports (QPRs) shall include % complete to date, photos of work being performed, upcoming project milestones (e.g. ground-breaking, ribbon-cutting), and delivery updates including work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, and any issues that may impact delivery, in addition to all other requirements described in the Standard Grant Agreement.

2. With the first QPR (July 2024) Sponsor shall provide 2-3 photos of typical before conditions; with the first quarterly report following initiation of fieldwork Sponsor shall provide a photo documenting compliance with the Prop AA attribution requirements as described in the SGA; and on completion of the project Sponsor shall provide 2-3 photos of completed work.

Special Conditions

1. The Transportation Authority will not reimburse SFPW for the construction phase until Transportation Authority staff releases the funds (\$2,360,343) pending receipt of evidence of completion of design (e.g. copy of certifications page).

Notes

1. Reminder: All construction signage, project fact sheets, websites and other similar materials shall comply with the attribution requirements established in the Standard Grant Agreement.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	42.95%	No TNC TAX	No PROP L
Actual Leveraging - This Project	47.4%	No TNC TAX	No PROP L

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	8th St, Clay St and Leavenworth St Pavement Renovation
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN SUMMARY

Current PROP AA Request:	\$2,360,572
---------------------------------	-------------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.



Initials of sponsor staff member verifying the above statement:

JLY

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Edmund Lee	Victoria Chan
Title:	Project Manager	Budget Manager
Phone:	555-5555	(415) 205-6316
Email:	edmund.lee@sfdpw.org	victoria.w.chan@sfdpw.org

148 Attachment 1 Street Resurfacing Program: 8th St, Clay St and Leavenworth St Pavement Renovation

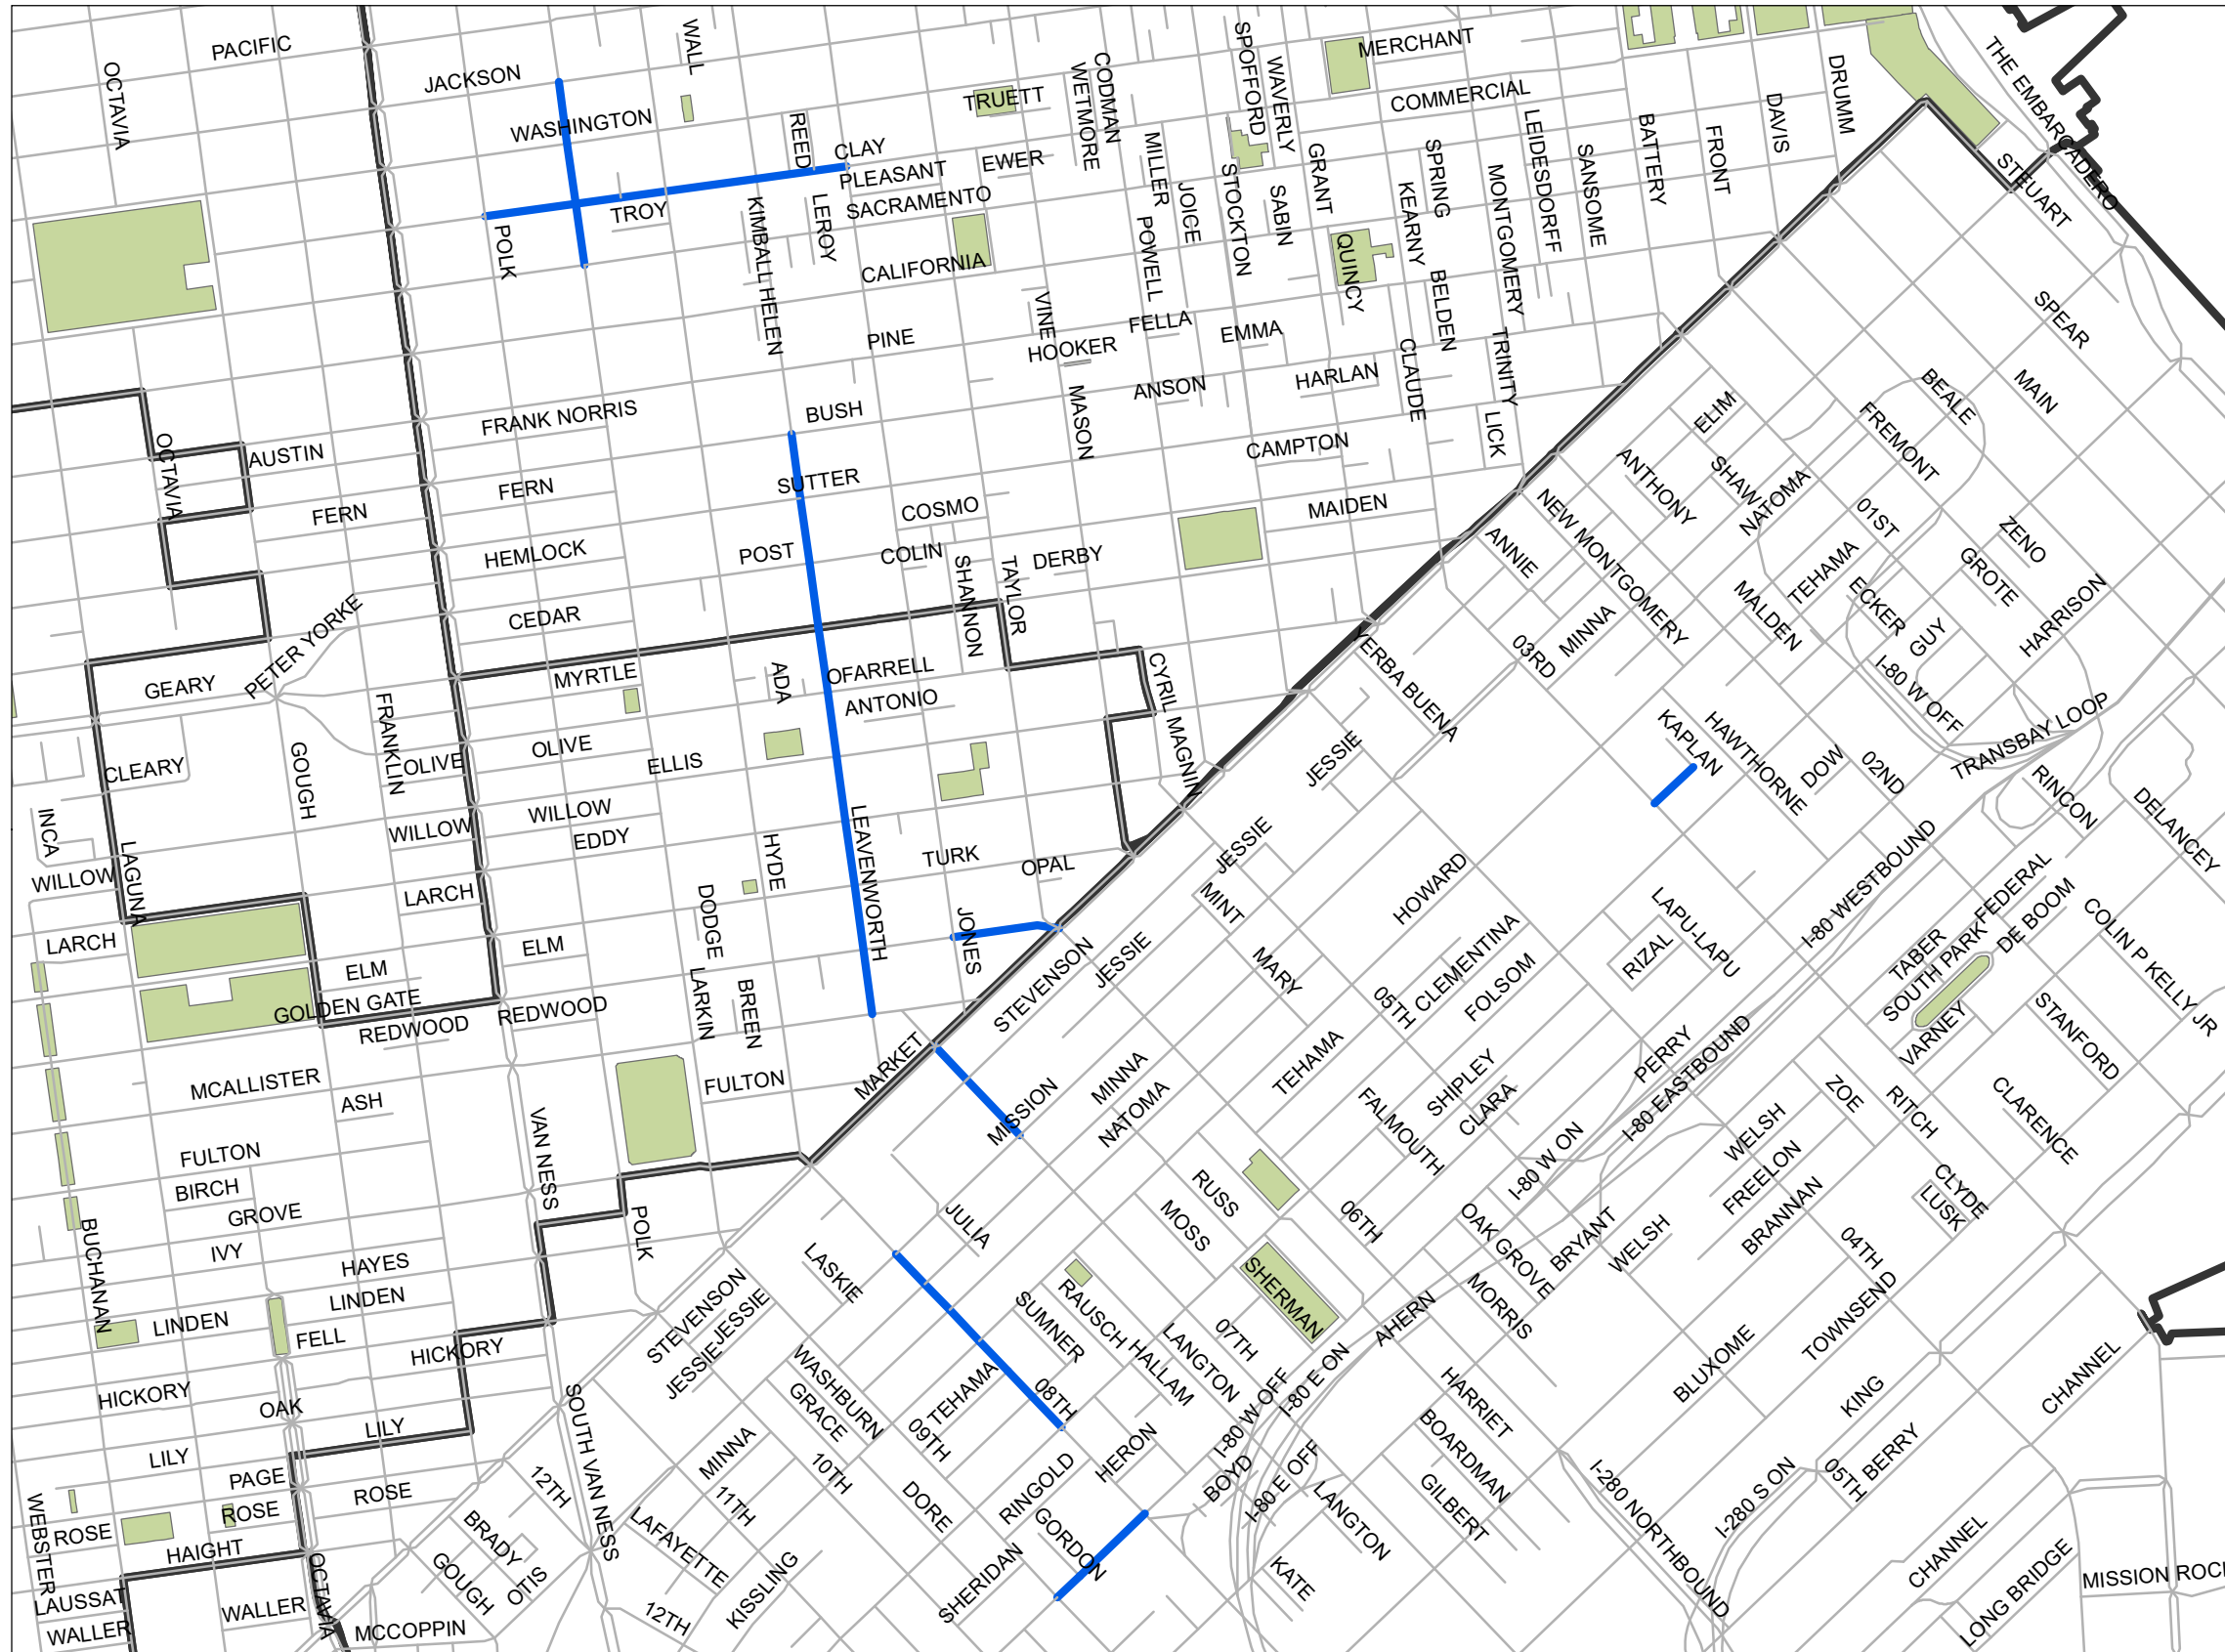

Legend

 8th St, Clay St and Leavenworth St Pavement Renovation

NOTES:
Information as of April 2024

All Public Works Street Resurfacing Program candidates are subject to substitution and schedule changes pending available funding, visual confirmation, utility clearances, and coordination with other agencies and are NOT guaranteed to be moved forward to construction. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the Public Works Street Resurfacing Program candidates to be postponed or dropped from consideration.



8th St, Clay St and Leavenworth St Pavement Renovation Project Location Candidates

Note: All Public Works Street Resurfacing Program candidates are subject to substitution and schedule changes pending available funding, visual confirmation, utility clearances and coordination with other agencies and are NOT guaranteed to be moved forward to construction. Unforeseen challenges such as increased work scope, changing priorities, cost increases or declining revenue may arise causing the Public Works Street Resurfacing Program candidates to be postponed or dropped from consideration.

On Street	From Street	To Street	BOS
07TH ST	CHARLES J BRENHAM PL \ MARKET ST	ODD FELLOWS WAY \ STEVENSON ST	6
07TH ST	ODD FELLOWS WAY \ STEVENSON ST	MISSION ST	6
08TH ST	MISSION ST	MINNA ST	6
08TH ST	MINNA ST	NATOMA ST	6
08TH ST	NATOMA ST	HOWARD ST	6
08TH ST	HOWARD ST	TEHAMA ST	6
08TH ST	TEHAMA ST	CLEMENTINA ST	6
08TH ST	CLEMENTINA ST	FOLSOM ST	6
CLAY ST	JONES ST	LEAVENWORTH ST	3
CLAY ST	LEAVENWORTH ST	HYDE ST	3
CLAY ST	HYDE ST	TORRENS CT	3
CLAY ST	TORRENS CT	LARKIN ST	3
CLAY ST	LARKIN ST	POLK ST	3
CLEMENTINA ST	KAPLAN LN	03RD ST	6
GOLDEN GATE AVE	06TH ST \ MARKET ST \ TAYLOR ST	JONES ST	5
HARRISON ST	08TH ST	GORDON ST	6
HARRISON ST	GORDON ST	09TH ST	6
LARKIN ST	SACRAMENTO ST	CLAY ST	3
LARKIN ST	CLAY ST	WASHINGTON ST	3
LARKIN ST	WASHINGTON ST	JACKSON ST	3
LEAVENWORTH ST	MCALLISTER ST	GOLDEN GATE AVE	5
LEAVENWORTH ST	GOLDEN GATE AVE	TURK ST	5
LEAVENWORTH ST	TURK ST	EDDY ST	5
LEAVENWORTH ST	EDDY ST	ELLIS ST	5
LEAVENWORTH ST	ELLIS ST	OFARRELL ST	5
LEAVENWORTH ST	OFARRELL ST	GEARY ST	5
LEAVENWORTH ST	GEARY ST	POST ST	3
LEAVENWORTH ST	POST ST	SUTTER ST	3
LEAVENWORTH ST	SUTTER ST	BUSH ST	3

[this page intentionally left blank]

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Japantown Buchanan Mall Improvements
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN INFORMATION

PROP AA Expenditure Plans	Prop AA Pedestrian Projects
Current PROP AA Request:	\$100,000
Supervisorial District	District 05

REQUEST

Brief Project Description

In the cultural heart of Japantown, this project will implement improvements to the Japantown Buchanan Mall, a culturally significant public plaza. This Prop AA request will fund the design phase for improvements that include repaving the uneven walkways, planting more trees, landscaping with culturally relevant plants, enhancing the existing historic public art, installing new pedestrian lighting, and other ADA compliant improvements to curb ramps and seating.

Detailed Scope, Project Benefits and Community Outreach

The Japantown Buchanan Mall is a publicly-owned plaza located at the geographic and cultural heart of Japantown, lined with shops, and maintained by the Nihonmachi Parking Corporation. Despite its importance, the community perceives the space to be difficult to walk on, and that it could be further activated – this project seeks to revitalize the space through pedestrian safety as well as artistic and landscaping improvements including:

- Repaving the side walkways, planting more trees, landscaping with culturally relevant plants, and enhancing the existing historic public art (historic fountains, cobblestone river, and Torii gate) with new, complementary public art
- Encouraging businesses to provide outdoor seating and displays along the storefronts
- Utilizing new energy- and water-efficient technologies to light the plaza and maintain the fountains

Prop AA funds would leverage the California Natural Resources Agency grant funding programmed for this project. Coordination will take place with the adjacent Japantown Peace Plaza project with work just south of the proposed project limits.

152

Project Location

Buchanan St, Post St to Sutter St

Is this project in an Equity Priority Community?	Yes
Does this project benefit disadvantaged populations?	Yes

Project Phase(s)

Design Engineering (PS&E)

5YPP/STRATEGIC PLAN INFORMATION

Type of Project in the Prop L 5YPP/Prop AA Strategic Plan?	Named Project
Is requested amount greater than the amount programmed in the relevant 5YPP or Strategic Plan?	Less than or Equal to Programmed Amount
PROP AA Amount	\$100,000.00

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Japantown Buchanan Mall Improvements
Primary Sponsor:	Department of Public Works

ENVIRONMENTAL CLEARANCE

Environmental Type:	Categorically Exempt
----------------------------	----------------------

PROJECT DELIVERY MILESTONES

Phase	Start		End	
	Quarter	Calendar Year	Quarter	Calendar Year
Planning/Conceptual Engineering (PLAN)	Apr-May-Jun	2023	Jan-Feb-Mar	2024
Environmental Studies (PA&ED)	Apr-May-Jun	2024	Apr-May-Jun	2024
Right of Way				
Design Engineering (PS&E)	Jan-Feb-Mar	2024	Jan-Feb-Mar	2025
Advertise Construction	Jan-Feb-Mar	2025		
Start Construction (e.g. Award Contract)	Oct-Nov-Dec	2025		
Operations (OP)				
Open for Use			Oct-Nov-Dec	2026
Project Completion (means last eligible expenditure)			Oct-Nov-Dec	2027

SCHEDULE DETAILS

SF Rec & Park Department broke ground for construction on April 27th, 2024 for the Japantown Peace Plaza Renovation Project and anticipates it to be completed in early 2026. The SF Public Works Japantown Buchanan Mall Project is separate but neighboring to the Japantown Peace Plaza project.

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Japantown Buchanan Mall Improvements
Primary Sponsor:	Department of Public Works

FUNDING PLAN - FOR CURRENT REQUEST

Fund Source	Planned	Programmed	Allocated	Project Total
EP-702: Prop AA Pedestrian Projects	\$0	\$100,000	\$0	\$100,000
Certificates of Participation (COP)	\$0	\$0	\$200,000	\$200,000
CNRA Grant (State)	\$0	\$0	\$1,200,000	\$1,200,000
Phases In Current Request Total:	\$0	\$100,000	\$1,400,000	\$1,500,000

FUNDING PLAN - ENTIRE PROJECT (ALL PHASES)

Fund Source	Planned	Programmed	Allocated	Project Total
PROP AA	\$0	\$500,000	\$0	\$500,000
Certificates of Participation (COP)	\$0	\$0	\$2,000,000	\$2,000,000
CNRA Grant (State)	\$0	\$0	\$5,000,000	\$5,000,000
Funding Plan for Entire Project Total:	\$0	\$500,000	\$7,000,000	\$7,500,000

COST SUMMARY

Phase	Total Cost	PROP AA - Current Request	Source of Cost Estimate
Planning/Conceptual Engineering	\$640,000		Actuals plus estimated cost to complete
Environmental Studies	\$10,000		Preliminary engineer's estimate
Right of Way	\$0		
Design Engineering	\$1,500,000	\$100,000	Preliminary engineer's estimate
Construction	\$5,350,000		Preliminary engineer's estimate
Operations	\$0		
Total:	\$7,500,000	\$100,000	

% Complete of Design:	15.0%
As of Date:	03/31/2024
Expected Useful Life:	20 Years

San Francisco County Transportation Authority

Prop L/Prop AA/Prop D TNC Allocation Request Form

MAJOR LINE ITEM BUDGET - JAPANTOWN BUCHANAN MALL IMPROVEMENTS

SUMMARY BY MAJOR LINE ITEM - DESIGN		
Budget Line Item	Totals	% of phase
1. Total Labor	\$ 1,295,000	
2. Consultant	\$ 60,000	
3. Other Direct Costs *	\$ 15,000	
4. Contingency	\$ 130,000	9%
TOTAL PHASE	\$ 1,500,000	

TOTAL LABOR COST BY AGENCY	
SFMTA	\$ 30,000
SFPW	\$ 1,265,000
TOTAL	\$ 1,295,000

* e.g. Permits and Planning Dept fees, mailing, reproduction

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Japantown Buchanan Mall Improvements
Primary Sponsor:	Department of Public Works

SFCTA RECOMMENDATION

Resolution Number:		Resolution Date:	
Total PROP AA Requested:	\$100,000	Total PROP AA Recommended	\$100,000

SGA Project Number:	725-208062	Name:	Japantown Buchanan Mall Improvements
Sponsor:	Department of Public Works	Expiration Date:	09/30/2025
Phase:	Design Engineering	Fundshare:	6.67%

Cash Flow Distribution Schedule by Fiscal Year

Fund Source	FY2024/25	Total
PROP AA EP-702	\$100,000	\$100,000

Deliverables
1. Quarterly progress reports shall include % complete of the funded phase, work performed in the prior quarter, work anticipated to be performed in the upcoming quarter, and any issues that may impact schedule, in addition to all other requirements described in the Standard Grant Agreement.
2. With the first quarterly progress report, Sponsor shall provide 2-3 photos of existing conditions.
3. Upon completion, Sponsor shall provide evidence of completion of 100% design (e.g., copy of certifications page, copy of workorder, internal design completion documentation, or similar).
4. Upon completion, Sponsor shall provide an updated scope, schedule, budget, and funding plan for construction. This deliverable may be met with an allocation request for construction.

Metric	PROP AA	TNC TAX	PROP L
Actual Leveraging - Current Request	93.33%	No TNC TAX	No PROP L
Actual Leveraging - This Project	93.33%	No TNC TAX	No PROP L

San Francisco County Transportation Authority Allocation Request Form

FY of Allocation Action:	FY2024/25
Project Name:	Japantown Buchanan Mall Improvements
Primary Sponsor:	Department of Public Works

EXPENDITURE PLAN SUMMARY

Current PROP AA Request:	\$100,000
---------------------------------	-----------

- 1) The requested sales tax and/or vehicle registration fee revenues will be used to supplement and under no circumstance replace existing local revenues used for transportation purposes.

Initials of sponsor staff member verifying the above statement:

JLY

CONTACT INFORMATION

	Project Manager	Grants Manager
Name:	Trent Tieger	Victoria Chan
Title:	Project Manager	Budget Manager
Phone:	(415) 558-4045	(415) 205-6316
Email:	trent.tieger@sfdpw.org	victoria.w.chan@sfdpw.org


PREFERRED DESIGN DIRECTION



8 pedestrian scale pole lighting (16ft)



9 garden gate lighting



10 lanterns (see options)




11 string lights (see options)



12 reinstall lamp posts



13 movable furnishings + storage structure




1 precast seat walls




2 restored fountains w/ new plumbing and lighting



3 cobble w/ compliant walking surface



4 stone paving w/ metal inlay accents



5 refurbished Ruth Asawa benches



6 ginkgo trees



7 cherry trees



HOW TO GET INVOLVED
SIGN UP FOR OUR MAILING LIST!
[SFPlanning.org/JapantownOsakaWay](https://sfplanning.org/JapantownOsakaWay)



San Francisco Planning

PUBLIC WORKS

SAN FRANCISCO

OFFICE OF THE CITY ATTORNEY

sfac

San Francisco

CBD

Japantown Community Benefit District

Nihonmachi Parking Corporation

Merchants Focus Group
SEPTEMBER 12, 2023

JAPANTOWN
OSAKA WAY (BUCHANAN MALL)
UPGRADES PROJECT

ジャパントウン
大阪道 (ブキャナンモール)
アップグレードプロジェクト
